

National Highways Authority of India
(Ministry of Road Transport & Highways)

Four Laning of Sethiyahopu-Cholapuram from Km. 65.960 to Km. 116.440
Section of NH-45C under NHDP-IV on Hybrid Annuity Mode Basis.

PATEL SETHIYAHOPU-CHOLOPURAM HIGHWAY PRIVATE LIMITED



MONTHLY PROGRESS REPORT
AUGUST 2023

Table of Content

| | |
|---|----|
| Table of Content | 02 |
| List of Tables | 03 |
| List of Figures | 04 |
| Executive Summary | 05 |
| Project Synopsis | 05 |
| 1. Background and Project Details | 12 |
| 1.1. Project Overview..... | 12 |
| 1.2. Salient Project Features | 13 |
| 1.3. Contractual Project Milestones | 14 |
| 1.4. Payment Milestones During Construction Period..... | 16 |
| 1.5. Permits & Approvals..... | 17 |
| 2. Right of Way Status | 19 |
| 2.1. Land Acquisition | 19 |
| 2.2. Removal of Religious Structures..... | 20 |
| 2.3. Shifting of Utilities and Electrical HT/LT Lines | 20 |
| 2.4. Tree felling..... | 22 |
| 3. Progress Briefing – Contractor Activities | 23 |
| 3.1. Pre-Construction Activities | 23 |
| 4. Physical Progress of Work | 24 |
| 4.1 Physical Progress of Work | 24 |
| 5. Financial & Physical Progress of Work | 61 |
| 5.1 Escrow Details/Financial Expenses Details | 64 |
| 6. Quality Control and Quality Assurance | 65 |
| 6.1 List of Lab Equipment's | 65 |
| 6.2 Quality Control Test Summary | 69 |
| 7. Weather Report..... | 85 |
| 8. Safety..... | 87 |
| 9. Support required from NHAI..... | 88 |
| 10. Important Events..... | 89 |
| 11. Organization Chart..... | 90 |
| 12. Manpower details | 93 |
| 13. List of Plants, Machinery and Equipments..... | 94 |

| | | |
|----|----------------------------------|-----|
| 14 | Change of Scope Proposals | 96 |
| 15 | Details of Correspondences | 97 |
| 16 | Progress Photographs..... | 102 |

List of Tables

| | |
|---|----|
| Table 1.1: Details of Project Alignment | 08 |
| Table 2.1-1: Details of proposed ROW as per Schedule-A | 19 |
| Table 2.1-2: Compensation disbursement for land | 20 |
| Table 2.1-3: Compensation disbursement for Structures | 20 |
| Table 2.2-1: Status of Removal of Religious structures | 20 |
| Table 2.3-1: Status of sanction of Estimates-Relocation of RWS Pipe Line | 20 |
| Table 2.3-2: Status of sanction of Estimates- Electrical Lines Relocation | 21 |
| Table 2.3-3: Status of Utility Relocation | 21 |
| Table 2.4-1: Status of Tree Cutting | 22 |
| Table 3.1-1: Status of Highway Design and Drawings as per Concession Agreement | 23 |
| Table 3.1-2: Status of Structure Design and Drawings as per Concession Agreement | 23 |
| Table 3.1-3: Status of Structure Design and Drawings additionally included under Positive change of Scope due to demand of local public | 23 |
| Table 4.1 : Strip Chart for Highway Works | 29 |
| Table 4.2 - 1 : Strip Chart for status of Box Culverts on Existing Road | 49 |
| Table 4.2 - 2 : Strip Chart for status of Box Culverts on Bypass | 51 |
| Table 4.2 - 3 : Strip Chart for status of MNB - Box | 53 |
| Table 4.2 - 4 : Strip Chart for status of LVUP | 55 |
| Table 4.2 - 5 : Strip Chart for status of MNB (> 15m Span) | 56 |
| Table 4.2 - 6 : Strip Chart for status of MJB | 57 |
| Table 4.2 - 7 : Strip Chart for status of FLYOVER | 59 |
| Table 4.2 - 8 : Strip Chart for status of VUP | 60 |
| Table 5.1- 1 : Pen Picture Escrow | 64 |
| Table 5.1- 2 : Escrow Details | 64 |
| Table 6.1 - 1 QA/QC Lab Equipment at Annaikarai Lab | 65 |
| Table 6.1 - 2 QA/QC Lab Equipment at Meensurity Lab | 66 |
| Table 6.2-1: Summary of Quality Control Tests | 70 |
| Table 10.1 : Details of Important Events | 89 |
| Table 12.1 – Manpower Details | 93 |
| Table 13.1 - List of Plants, Machinery and Equipment's | 94 |
| Table 14.1 - Status of Change of Scope Proposals | 96 |

| | |
|--|-----|
| Table 15.1 - Concessionaire to NHAI | 98 |
| Table 15.2. - NHAI to Concessionaire | 99 |
| Table 15.3. - Concessionaire to Independent Engineer | 100 |
| Table 15.4. - Independent Engineer to Concessionaire | 101 |

List of Figures

| | |
|--|----|
| Figure 1 : Project Location Map | 06 |
| Figure 2 : Project Alignment Map | 07 |
| Figure 3a : Financial Progress - Planned vs Achieved | 62 |
| Figure 3b : Physical Progress - Planned vs Achieved | 63 |
| Figure 4 : Organization Chart - EPC Team | 91 |
| Figure 5 : Organization Chart - SPV Team | 92 |

Executive Summary

The old National Highway (NH -45C) runs through the state of Tamil Nadu. The project road is part of the 168 km long Vikravandi to Thanjavur section of the existing National Highway 45C (NH-45C). Recently MORTH has amended the number and Length of the National Highways. The old NH 12 in the state of Tamil Nadu has become the part of the New National Highway 36. It links Chennai with Thanjavur and is 418 km long.

The Sethiyahopu to Cholopuram section of NH-45C is an important link to connect Metropolitan city of Chennai to religious and tourist places of Cholopuram, Thanjavur, kumbakonam, Puducherry. The project is also expected to provide improved connectivity to other religious places & other major cities like Rameswaram, Madurai, Tiruchirappalli, etc. The Project stretches passing through the 03 nos. of districts of Cuddalore, Ariyalur and Thanjavur.

Project Synopsis

The Government of India had entrusted to the National Highway Authority of India (NHAI) the development, maintenance and management of National Highway No. 45C including the section from km 65.960 to Km 116.440 (approx. 50.480 Km). The Authority had resolved to augment for four Laning of Sethiyahopu - Cholopuram from Km 65.960 to Km 116.440 section of NH - 45C in the State of Tamil Nadu under NHDP Phase-IV on design, build, operate and transfer (the "DBOT Annuity" or "Hybrid Annuity") basis.

The scope of work will broadly include rehabilitation, upgradation and widening of the existing carriageway to four - lane standards with construction of new pavement, rehabilitation of existing pavement, construction and/or rehabilitation of major and minor bridges, culverts, road intersections, interchanges, drains etc. Including those prescribed in the Concession Agreement and its Schedule and the operation and maintenance itself. The map of project road is given in Figures below. The details of habitations are given in table - 01.

Figure 1: Project Location Map

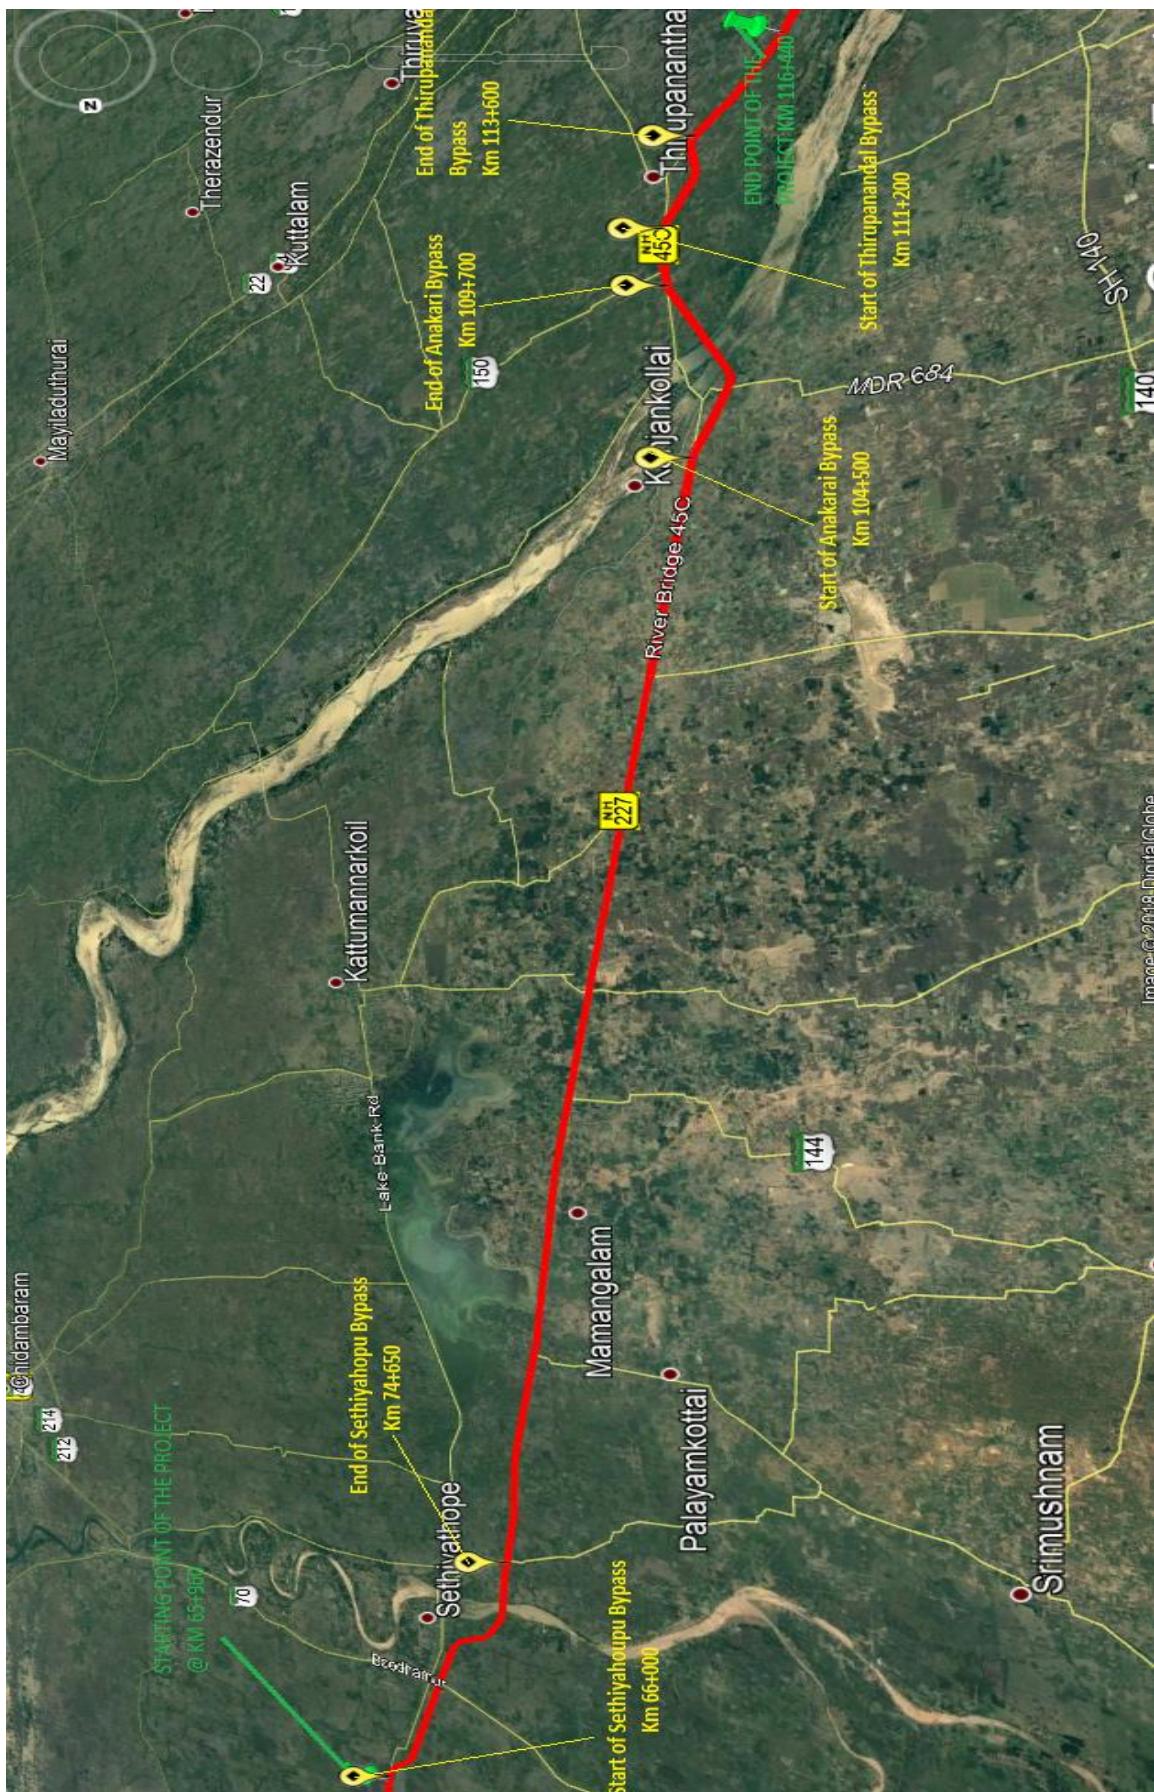


Figure 2: Project Alignment Map

SETHI YAHOPU TO CHOLOPURAM HIGHWAY PROJECT OF NH45 C

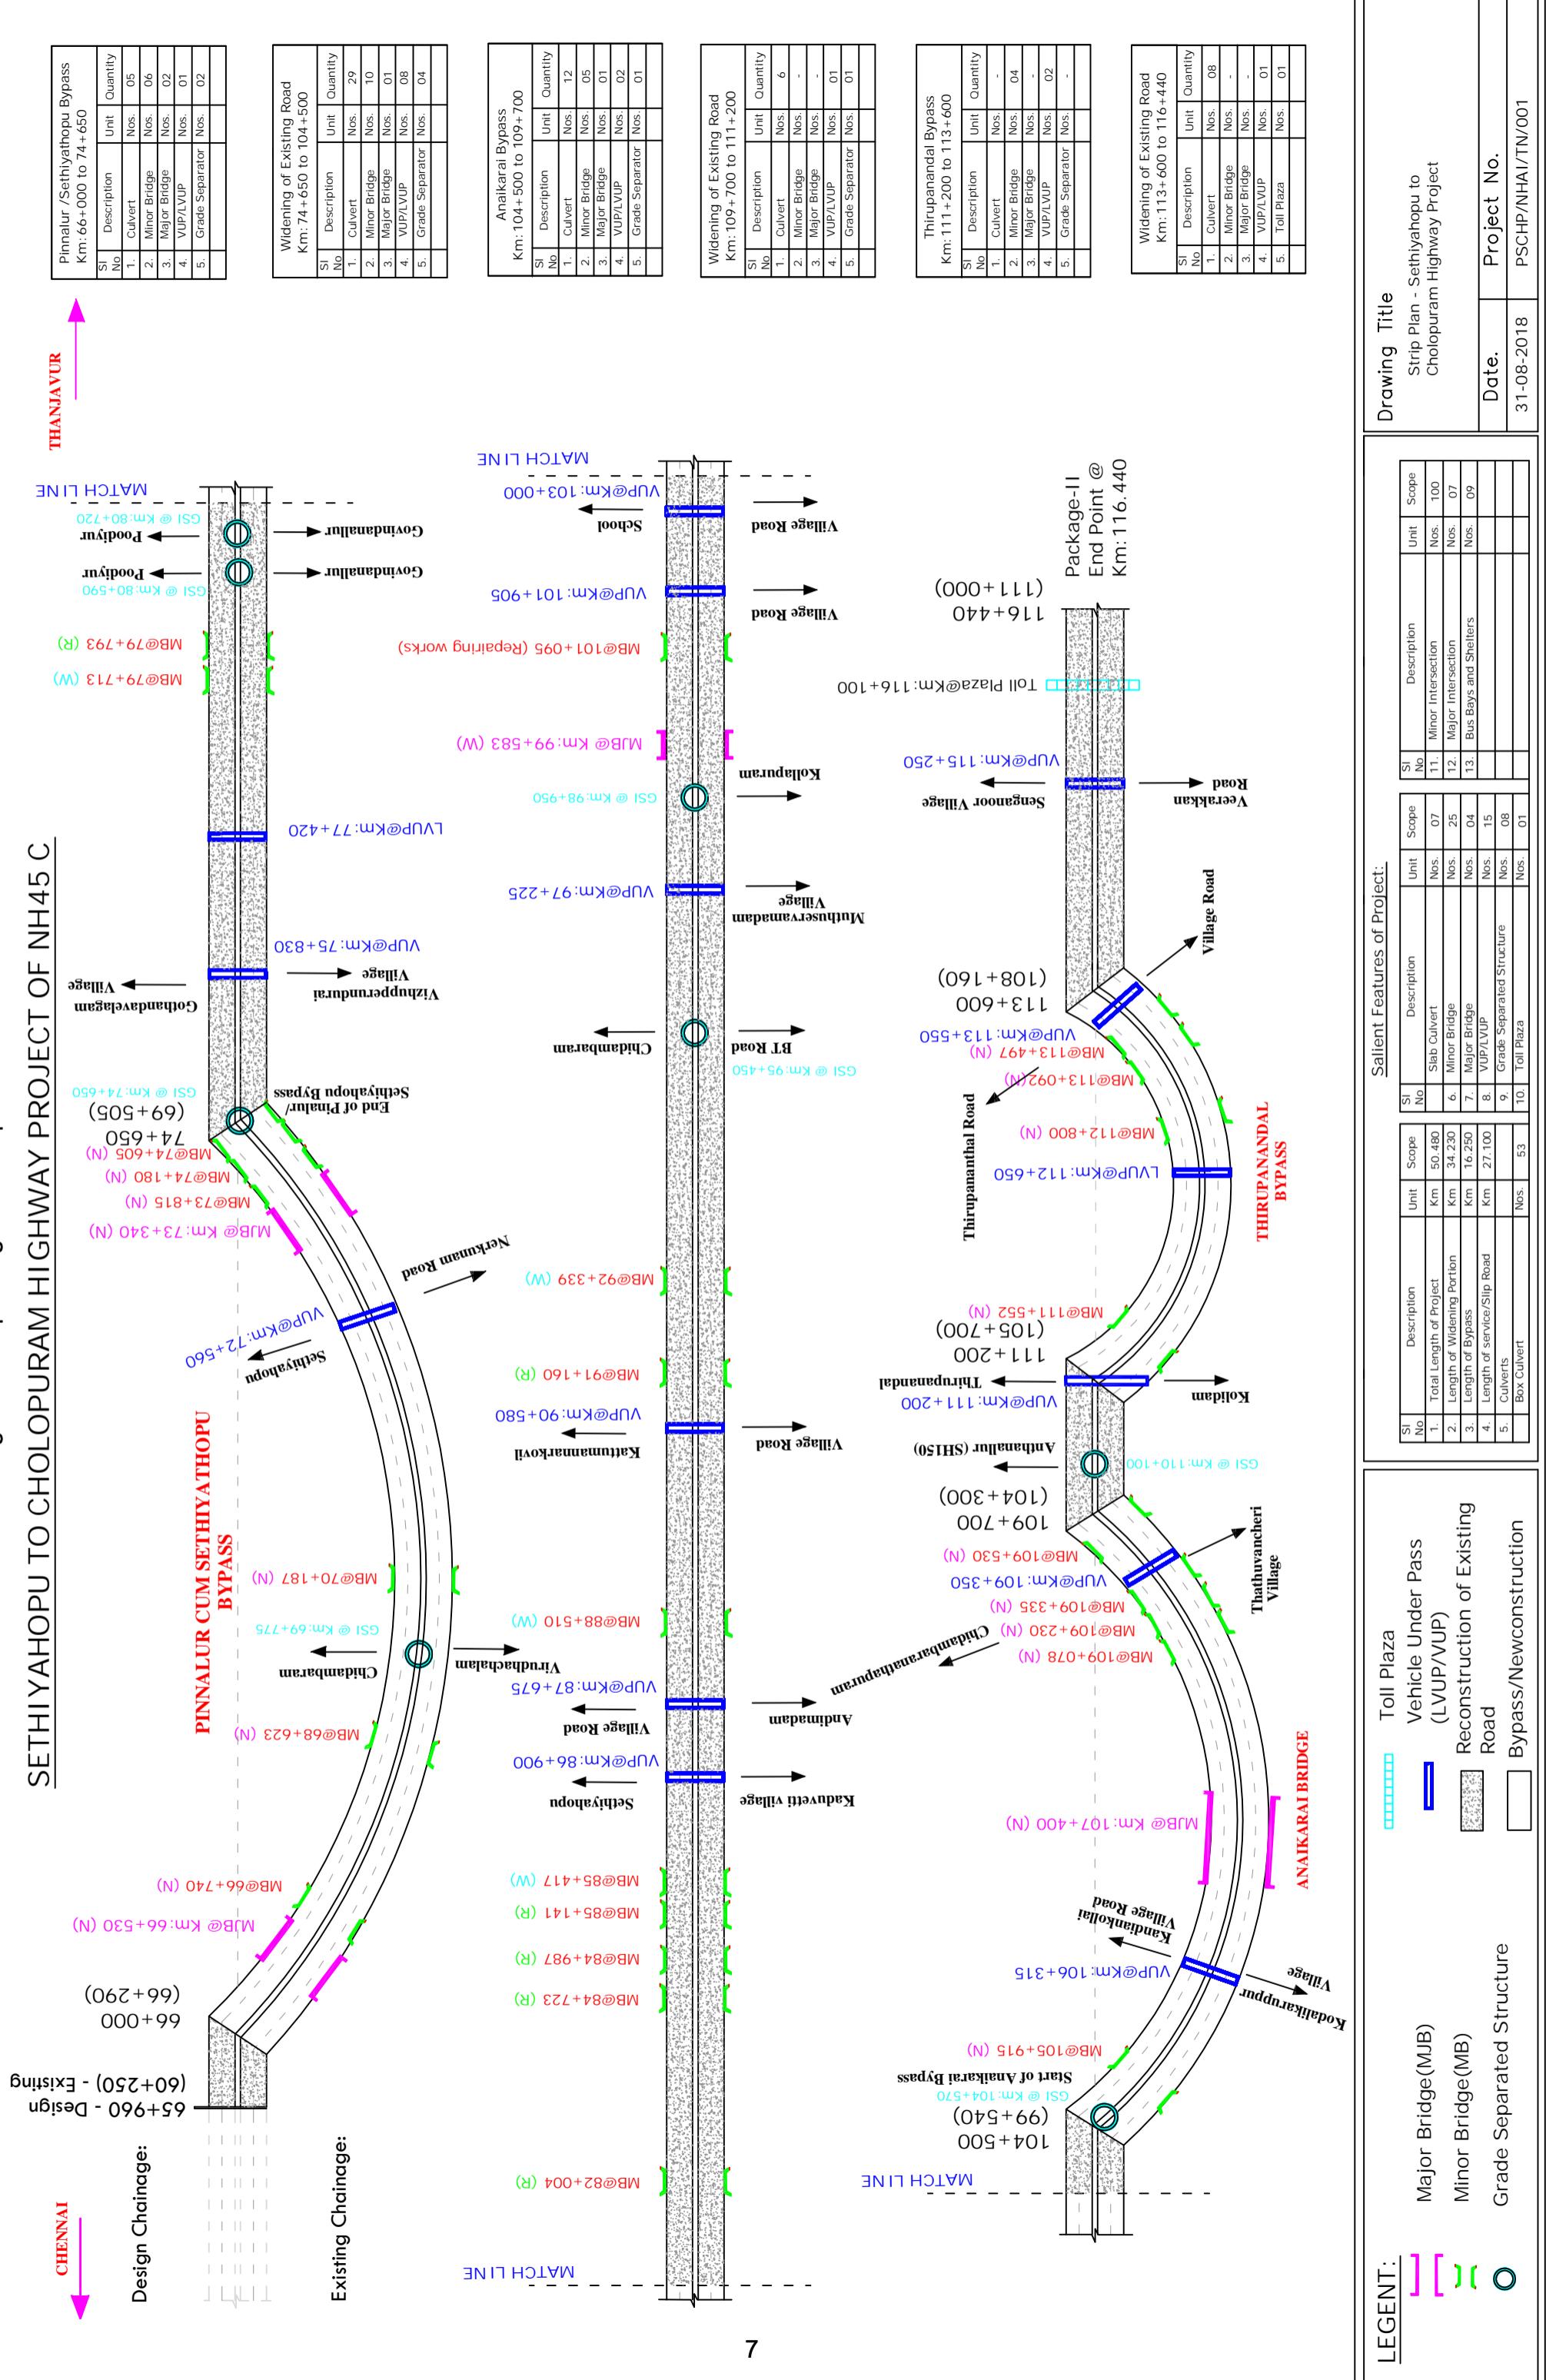


Table - 1.1: Details of Project Alignments

| Existing and Proposed Alignments | | | | | | | |
|----------------------------------|------------------------|--------|----------------------|--------|-------------|--|---------------------|
| Sl. no. | Existing Chainage (Km) | | Design Chainage (Km) | | LENGTH (Km) | TCS Type | Remarks |
| | From | To | From | To | | | |
| 1 | 60.250 | Bypass | 65.960 | 69.460 | 3.500 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 2 | Bypass | Bypass | 69.460 | 70.090 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 3 | Bypass | Bypass | 70.090 | 72.350 | 2.260 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 4 | Bypass | Bypass | 72.350 | 72.775 | 0.425 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 5 | Bypass | Bypass | 72.775 | 74.335 | 1.560 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 6 | Bypass | 69.820 | 74.335 | 74.960 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 7 | 69.820 | 70.375 | 74.960 | 75.520 | 0.560 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 8 | 70.375 | 71.010 | 75.520 | 76.150 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 9 | 71.010 | 71.855 | 76.150 | 76.900 | 0.750 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 10 | 71.855 | 72.170 | 76.900 | 77.220 | 0.320 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 11 | 72.170 | 72.570 | 77.220 | 77.620 | 0.400 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 12 | 72.570 | 72.800 | 77.620 | 77.850 | 0.230 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 13 | 72.800 | 73.230 | 77.850 | 78.300 | 0.450 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 14 | 73.230 | 75.105 | 78.300 | 80.150 | 1.850 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 15 | 75.105 | 76.080 | 80.150 | 81.120 | 0.970 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 16 | 76.080 | 76.460 | 81.120 | 81.500 | 0.380 | TCS-1 | Concentric Widening |
| 17 | 76.460 | 77.000 | 81.500 | 82.240 | 0.740 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |

| | | | | | | | |
|----|--------|--------|--------|--------|-------|--|---------------------|
| 18 | 77.000 | 78.115 | 82.240 | 83.150 | 0.910 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 19 | 78.115 | 79.110 | 83.150 | 84.150 | 1.000 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 20 | 79.110 | 79.510 | 84.150 | 84.550 | 0.400 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 21 | 79.510 | 80.610 | 84.550 | 85.650 | 1.100 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 22 | 80.610 | 81.555 | 85.650 | 86.580 | 0.930 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 23 | 81.555 | 82.170 | 86.580 | 87.210 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 24 | 82.170 | 82.320 | 87.210 | 87.360 | 0.150 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 25 | 82.320 | 82.910 | 87.360 | 87.990 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 26 | 82.910 | 83.180 | 87.990 | 88.265 | 0.275 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 27 | 83.180 | 83.660 | 88.265 | 88.745 | 0.480 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 28 | 83.660 | 85.220 | 88.745 | 90.265 | 1.520 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 29 | 85.220 | 85.850 | 90.265 | 90.895 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 30 | 85.850 | 86.555 | 90.895 | 91.600 | 0.705 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 31 | 86.555 | 87.015 | 91.600 | 92.050 | 0.450 | TCS-1 | Concentric Widening |
| 32 | 87.015 | 87.525 | 92.050 | 92.560 | 0.510 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 33 | 87.525 | 90.000 | 92.560 | 95.035 | 2.475 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 34 | 90.000 | 90.830 | 95.035 | 95.865 | 0.830 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 35 | 90.830 | 91.350 | 95.865 | 96.400 | 0.535 | Type-B (Fig 2.6 of the manual) with both side service road | Concentric Widening |
| 36 | 91.350 | 91.970 | 96.400 | 96.910 | 0.510 | TCS-1 | Concentric Widening |

| | | | | | | | |
|-----|---------|---------|---------|---------|-------|--|---------------------|
| 37 | 91.970 | 92.460 | 96.910 | 97.535 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 38 | 92.460 | 93.550 | 97.535 | 98.535 | 1.000 | TCS-1 | Concentric Widening |
| 39 | 93.550 | 94.370 | 98.535 | 99.335 | 0.800 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 39A | 94.370 | 94.875 | 99.335 | 99.840 | 0.505 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 40 | 94.875 | 95.350 | 99.840 | 100.300 | 0.460 | Type-B (Fig 2.6 of the manual) with both side service road | |
| 41 | 95.350 | 96.630 | 100.300 | 101.590 | 1.290 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 42 | 96.630 | 97.260 | 101.590 | 102.225 | 0.635 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 43 | 97.260 | 97.720 | 102.225 | 102.685 | 0.460 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 44 | 97.720 | 98.360 | 102.685 | 103.315 | 0.630 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 45 | 98.360 | 99.190 | 103.315 | 104.160 | 0.845 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 46 | 99.190 | Bypass | 104.160 | 104.990 | 0.830 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 47 | Bypass | Bypass | 104.990 | 106.000 | 1.010 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 48 | Bypass | Bypass | 106.000 | 106.625 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 49 | Bypass | Bypass | 106.625 | 109.035 | 2.410 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 50 | Bypass | 104.260 | 109.035 | 109.660 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 51 | 104.260 | 105.015 | 109.660 | 110.515 | 0.855 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 52 | 105.015 | 105.390 | 110.515 | 110.890 | 0.375 | Type-B (Fig 2.6 of the manual) with both side service road | Eccentric Widening |
| 53 | 105.390 | Bypass | 110.890 | 111.515 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |

| | | | | | | | |
|----|---------|---------|---------|---------|-------|--|--------------------|
| 54 | Bypass | Bypass | 111.515 | 112.430 | 0.915 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 55 | Bypass | Bypass | 112.430 | 112.840 | 0.410 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 56 | Bypass | Bypass | 112.840 | 113.225 | 0.385 | Type-A-3 (Fig 2.4 of the manual) | Bypass |
| 57 | Bypass | 108.410 | 113.225 | 113.850 | 0.625 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 58 | 108.410 | 109.395 | 113.850 | 114.835 | 0.985 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |
| 59 | 109.395 | 110.220 | 114.835 | 115.660 | 0.825 | Figure 7.8- Grade separator and its approaches with RE wall and both side 5.5 m wide Slip road | |
| 60 | 110.220 | 111.000 | 115.660 | 116.440 | 0.780 | Type-A-3 (Fig 2.4 of the manual) | Eccentric Widening |

1. Background and Project Details

1.1. Project Overview

| | |
|--|---|
| Name of Work | Four Laning of Sethiyahopu-Cholopuram from Km. 65.960 to Km. 116.440 Section of NH-45C under NHDP-IV on Hybrid Annuity Mode Basis. |
| Name of Employer | National Highways Authority of India (NHAI) G-5 & 6, Sector-10, Dwarka, New Delhi -110075 |
| Name of Concessionaire | Patel Sethiyahopu – Cholopuram Highway Pvt Ltd, Patel House, Beside Prakruti Resorts, Channi Road, Vadodara. Gujarat– 391740 Tel: +91-265 277 6678 Fax: +91-265 277 7878 |
| Independent Engineer | M/s. Theme Engineering Services Pvt. Ltd, Plot No. 2, Annai Anjugam Nagar, Ullur, Chettimandapam, Kumbakonam – 612001. |
| EPC Contractor | M/s. Patel Infrastructure Limited, Patel House, Beside Prakruti Resort, Channi Road, Vadodara Gujarat– 391740, Tel: +91-265 277 6678 Fax: +91-265 277 7878 |
| Design Consultant | CTL Global Services Pvt. Ltd. 101 , 1st Floor, Krishna Chambers, HAL, Airport Road, Bangalore-560017 |
| Senior Lender | Punjab National Bank, Large Corporate Branch, Neelkamal Building, Opp. Sales India, Ashram Road, Ahmedabad - 380009 |
| Lenders Independent Engineers | Sharul Techno-Financial Consultancy Services Pvt. Ltd., 403, Aspire Tower 5, Amanora Park Town, Hadapsar, Pune - 411028. |
| Length of Road (Design Length) | 50.480 Kms |
| Total Bid Project Cost | Rs. 1461.00 Cr. (as per concession agreement) |
| Date of Concession Agreement | November 9, 2017 |
| Concession Period | 17 Years (Construction Period 2 Years from Appointed date, Operation period 15 years from COD) |
| Appointed Date | 16.08.2018 |
| Construction Period | 2 years from Appointed date |
| Completion Date as per CA | 15.08.2020 |
| Date of Settlement Agreement No. 01 | 04.03.2021 |
| Date of Settlement Agreement No. 02 | 20.03.2023 |
| Revised Completion Date as per SA | 30.06.2024 |
| Maintenance Period | 15 years from COD |

1.2. Salient Project Features

Besides the construction of new carriageways and widening & strengthening of existing carriageways, the following table summaries the major elements of the project construction:-

| | |
|-------------------------------|--|
| 4 - Lane Divided Carriage Way | 50.48 Km. |
| Service Road/ Slip Road | 26.595 Km (Slip Road = 14.510 Kms & Service Road = 12.085 Kms) |
| Major Bridge | 04 Nos. |
| Minor Bridge | 25 Nos. |
| Grade Separate Intersection | 08 Nos. |
| Vehicular Underpass | 13 Nos. |
| Light Vehicular Underpass | 2 Nos. |
| Culverts | 60 Nos. |
| Major Intersections | 07 Nos. |
| Minor Intersections | 100 Nos. |
| Bus Bays | 09 Nos. |
| Toll Plaza | 01 Nos. |

1.3. Contractual Project Milestones

Following is a listing of the Key Project Milestones:-

| Mile Stone | Description | Target Dates as per CA | Dates as per Settlement Agreement signed on dated 04.03.2021 | Revised target dates as per Settlement Agreement signed on dated 20.03.2023 |
|----------------------|---|------------------------------|--|---|
| Mile Stone -I | Concessionaire shall expended not less than 20 % of the Total capital cost and shall have commenced construction of the project and achieved 20% of physical progress on 214 th day from the Appointed Date. | 18 th March 2019 | ➤ 31 st May'2021- Total 28.345 Km. four lane to be completed for PCOD-I. | ➤ 10 th December'2021- Total 28.345 Km. four lane to be completed for PCC-I . |
| Mile Stone -II | Concessionaire shall expended not less than 35% of the Total capital cost and shall have commenced construction of the project and achieved 35% of physical progress on 334 th day from the Appointed Date. | 16 th July 2019 | ➤ 30 th Nov'2021- Total 35.940 Km. four lane to be completed for PCOD-II. | ➤ 28 th February'2023- Total 35.240 Km. four lane to be completed for PCC-II . |
| Mile Stone -III | Concessionaire shall expended not less than 75 % of the Total capital cost and shall have commenced construction of the project and achieved 75% of physical progress on 584 th day from the Appointed Date. | 22 nd March 2020 | ➤ 31 st July'2022- Total 50.480 Km. four lane to be completed for final completion. | ➤ 10 th August'2023- Total 40.140 Km. four lane to be completed for PCC-III. |
| Scheduled Completion | Concessionaire shall have completed Project on 730 th day from the Appointed Date. | 15 th August 2020 | | ➤ 30 th June'2024- Total 50.480 Km four lane to be completed for final completion. |

Note: The Settlement Agreement was signed between Concessionaire and Authority on dated 04.03.2021 with the target of completion of 28.345 Kms length by 31.05.2021, and further completion of additional 7.595 Kms length by 30.11.2021 i.e. up to Payment Date of 1st Annuity. The non-workable length/non-handed over length is 14.54 Km as per joint site verification by Concessionaire, IE and NHAI. This 14.54 Km length shall be handed over to the Concessionaire by 31.05.2021 and shall be completed by 31.07.2022.

However, out of 14.540 Kms, only 4.180 Kms was handed over to the Concessionaire by 31.05.2021. Out of the balance length equal to 10.360 Kms (i.e. 14.540 kms - 4.180 kms), Concessionaire considered 4.230 Kms length as workable length and remaining length equal to 6.130 Kms (i.e. 10.360 kms - 4.230 kms) was under approval of descope proposal at NHAI, HQ from the scope of work of Concessionaire.

The Competent Authority has communicated extension of time approval for 105 days due to occurrence of Force Majeure event on account of 2nd wave of COVID-19.

The Concessionaire had also requested to Authority/IE for the extension of time for PCOD-2 up to 28.02.2023 and PCOD-3 upto 10.08.2023 due to constraints of issue in obtaining permission for extracting soils from borrow area and also due to interruption in the availability of pond ash.

The Concessionaire had also submitted the proposal for additional descope to Authority / IE in 3.51 Km length in addition to the already proposed descoping of 6.13 Km length due to interruption in the availability of pond ash required for the construction of RE Wall stretches and also due to local villagers were not allowing the concessionaire to continue the construction activities in some stretches. Hence, the concessionaire was not able to execute any construction activity in 3.51 Km length up to 31.05.2021 and submitted the proposal of additional de scope to Authority/IE.

In line of the submission done by the concessionaire, Independent Engineer has examined both the proposals submitted by the concessionaire and Independent Engineer vide IE letter no. 4906 & 4897 Dt. 04.11.2022 has recommended both the proposals to PIU, NHAI (i.e. total comprehensive descope proposal in 9.640 Km length (6.13Km+3.51Km) and extension of time proposal for PCOD-02 (completion of 35.940 Km) up to 28.02.2023 and extension of time proposal for PCOD-03 (completion of 40.840 Km duly considering the descope proposal of 9.640 Km length) up to 10.08.2023 for the approval of competent authority.

In line of the recommendation done by IE, PIU NHAI vide letter no. 3153 Dt. 04.11.2022 has also recommended both the proposals to RO, NHAI (i.e. total comprehensive descope proposal in 9.640 Km length (6.13Km+3.51Km) and extension of time proposal for PCOD-02 (completion of 35.940 Km) up to 28.02.2023 and extension of time proposal for PCOD-03 (completion of 40.840 Km duly considering the descope proposal of 9.640 Km length) up to 10.08.2023) for getting the approval from the competent authority.

In line of the recommendation given by PIU, NHAI regarding total comprehensive descope proposal in 9.640 Km length & additional EOT for 270 days, Settlement Agreement has been signed between NHAI (Authority) & PSCHPL (Concessionaire) on dated 20.03.2023 and the following has been finalized between NHAI (Authority) & PSCHPL (Concessionaire):-

1. The cumulative length for the completion of PCC-2 has been revised from 35.940 Km to 35.240 Km due to local public not allowing the concessionaire to execute the construction activities & demanding for the construction of additional scope of work and hence the same need to be considered under the proposal of change of scope.
2. The cumulative length for the completion of PCC-3 has been revised from 40.840 Km (duly considering the descope proposal of 9.640 Km length) to 40.140 Km due to local public not allowing the concessionaire to execute the construction activities & demanding for the construction of additional scope of work and hence the same need to be considered under the proposal of change of scope.
3. It was acknowledged by both the parties i.e. NHAI (Authority) & PSCHPL (Concessionaire) that 100% encumbrance free land is now available for the completion of entire project. Hence, from the project completion point of view, the descope length (i.e. 9.64 Km) & the length affected due to additional change of scope (i.e. 0.70 Km) has been considered for PCC-4 and the target date finalized for the completion of PCC-4 (i.e. 9.64 Km + 0.70 Km = 10.34 Km) is 30.06.2024.

Status of Progress of Work as per Settlement Agreement signed on Dated 20.03.2023:-

| Sr. No. | Description | Target length & Date | Tentative BPC | Achieved as on date | Remarks |
|---------|-------------|--|---------------|---------------------|--|
| 1 | PCC-01 | Completion of 28.345 Kms by 10.12.2021 | 803.60 Cr. | 76.96% | Presently, Work is in Progress in the PCC-03 & PCC-04 Stretches by the concessionaire. |
| 2 | PCC-02 | Completion of 35.240 Kms by 28.02.2023 | 1045.91 Cr. | | |
| 3 | PCC-03 | Completion of 40.140 Kms by 10.08.2023 | 1189.40 Cr.* | | |
| 4 | PCC-04 | Completion of 50.480 Kms by 30.06.2024 | 1461.00 Cr.* | | |

*NOTE:- Approximate amount mentioned for PCC-03 & PCC-04. The revised BPC would be derived for PCC-03 & PCC-04 by IE and accordingly the subsequent payment would be paid to the concessionaire.

1. IE vide letter no. 1144 dated 02.06.2022 has issued the Provisional Completion Certificate-1 (PCC-01) after the completion of 28.345 Kms w.e.f. 10.12.2021.

2. IE vide letter no. 1434 dated 16.06.2023 has issued the Provisional Completion Certificate-2 (PCC-02) after the completion of 35.240 Kms w.e.f. 18.02.2023.

1.4. Payment milestone during Construction Period

| Payment Mile Stone | Eligibility Criteria | Payment Amount (Rs.) | Claimed Amount (Rs.) | Date of release of payment |
|--|--|----------------------|----------------------|----------------------------|
| Mile Stone-I | On Achievement of 10% of Physical Progress | 116.88 Crs. | 110.94 Crs. | 04.10.2019 |
| Mile Stone-II | On Achievement of 30% of Physical Progress | 116.88 Crs. | 110.94 Crs. | 25.09.2020 |
| IPC No. 01 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 31.856% of Physical Progress | 10.85 Crs. | 10.29 Crs. | 29.09.2020 |
| IPC No. 02 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 32.758% of Physical Progress | 5.27 Crs. | 5.00 Crs. | 10.11.2020 |
| IPC No. 03 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 34.484% of Physical Progress | 10.09 Crs. | 9.57 Crs. | 10.11.2020 |
| IPC No. 04 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 35.144% of Physical Progress | 3.86 Crs. | 3.66 Crs. | 10.12.2020 |
| IPC No. 05 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 36.052% of Physical Progress | 5.31 Crs. | 5.04 Crs. | 12.02.2021 |
| IPC No. 06 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 37.886% of Physical Progress | 10.72 Crs. | 10.17 Crs. | 18.03.2021 |
| IPC No. 07 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 39.452% of Physical Progress | 9.15 Crs. | 8.69 Crs. | 31.03.2021 |
| IPC No. 08 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 40.979% of Physical Progress | 8.92 Crs. | 8.47 Crs. | 10.05.2021 |
| IPC No. 09 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 41.432% of Physical Progress | 2.65 Crs. | 2.51 Crs. | 09.06.2021 |
| IPC No. 10 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 43.429% of Physical Progress | 11.67 Crs. | 11.08 Crs. | 16.07.2021 |
| IPC No. 11 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 46.976% of Physical Progress | 20.73 Crs. | 19.67 Crs. | 27.08.2021 |
| IPC No. 12 of Mile Stone-III (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 49.966% of Physical Progress | 17.47 Crs. | 16.59 Crs. | 20.09.2021 |
| Payment Mile Stone-III & IPC No. 01 of Mile Stone-IV (as per NHAI) | On achievement of 63.787% of physical progress | 22.32 Crs. | 21.20 Crs. | 30.06.2022 |

| | | | | |
|---|--|------------|------------|------------|
| Policy Guidelines/Atmnirbhar Bharat) | | | | |
| IPC No. 02 of Mile Stone-IV (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 66.181% of physical progress | 13.99 Crs. | 13.28 Crs. | 22.08.2022 |
| IPC No. 03 of Mile Stone-IV (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 67.868% of physical progress | 9.86 Crs. | 9.36 Crs. | 29.12.2022 |
| IPC No. 04 of Mile Stone-IV (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 69.633% of physical progress | 10.31 Crs. | 9.79 Crs. | 02.03.2023 |
| IPC No. 05 of Mile Stone-IV (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 70.071% of physical progress | 2.56 Crs. | 2.43 Crs. | 29.03.2023 |
| IPC No. 06 of Mile Stone-IV (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 71.347% of physical progress | 7.46 Crs. | 7.08 Crs. | 28.04.2023 |
| Payment Mile Stone-IV & IPC No. 01 of Mile Stone-V (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 73.410% of physical progress | 12.06 Crs. | 11.44 Crs. | 22.07.2023 |
| IPC No. 02 of Mile Stone-V (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 75.066% of physical progress | 9.68 Crs. | 9.19 Crs. | 05.08.2023 |
| IPC No. 03 of Mile Stone-V (as per NHAI Policy Guidelines/Atmnirbhar Bharat) | On Achievement of 75.954% of physical progress | 5.19 Crs. | 4.93 Crs. | 30.08.2023 |

NOTE:- The Payment amount & claimed amount against the achievement of Physical Progress as mentioned above in the table does not include the escalation amount received to the concessionaire from the Authority.

1.5. Permits & Approvals

| Sr. No. | Details | Authority | Current Status | Remarks |
|---------|--------------------------------------|---|----------------|---------------------|
| 1 | Extraction of Boulders from Quarries | Dist. Mining Officer | Obtained | |
| 2 | Installation of Crusher | Village Panchayat Head | Obtained | |
| 3 | -----D O----- | Pollution Control Board | Obtained | |
| 4 | Use of Explosives | District Collector | Obtained | |
| 5 | Labour License | Labour Commissioner | Obtained | |
| 6 | Environmental Clearance | | NA | |
| 7 | Trees Cutting Permission | Forest department through NHAI | Obtained | |
| 8 | Electric Poles Shifting | Tamil Nadu Electricity Board | Obtained | Work is in Progress |
| 9 | Water Pipes Shifting | Tamilnadu Water Supply and Drainage Board | Obtained | Work is in Progress |

| | | | | |
|----|--|--|----|--|
| 10 | Drawing Water from river/ reservoir | | NA | |
|----|--|--|----|--|

2. Right of Way Status

2.1. Land Acquisition

As per the Schedule – A of Concession Agreement, the Proposed Right of Way (ROW) is of 45, 52.50 & 60 meters as mentioned in the table below:-

| Table 2.1-1: Details of proposed ROW as per Schedule-A | | | | |
|---|----------------------|--------------------|-----------|--------------------------------------|
| | Design Chainage (Km) | Design Length (Km) | Width (m) | Remarks |
| Full Right of Way (full width) | | | | |
| Stretch | 65.960 to 75.150 | 9.190 | 60.00 | Within 15 days of date of Agreement. |
| Stretch | 75.150 to 82.380 | 7.230 | 45.00 | |
| Stretch | 82.380 to 83.080 | 0.700 | 60.00 | |
| Stretch | 83.080 to 84.050 | 0.970 | 45.00 | |
| Stretch | 84.050 to 86.440 | 2.390 | 60.00 | |
| Stretch | 86.440 to 87.660 | 1.220 | 52.50 | |
| Stretch | 87.660 to 91.730 | 4.070 | 45.00 | |
| Stretch | 91.730 to 93.730 | 2.000 | 52.50 | |
| Stretch | 93.730 to 95.900 | 2.170 | 45.00 | |
| Stretch | 95.900 to 99.700 | 3.800 | 60.00 | |
| Stretch | 99.700 to 104.500 | 4.800 | 30.00 | |
| Stretch | 104.500 to 109.700 | 5.200 | 60.00 | |
| Stretch | 109.700 to 110.980 | 1.280 | 30.00 | |
| Stretch | 110.980 to 113.700 | 2.720 | 60.00 | |
| Stretch | 113.700 to 116.440 | 2.740 | 30.00 | |
| Total Length | | 50.480 | | |

| Balance Right of way (width) | | | | |
|-------------------------------------|----------------------|--------------------|-----------|--|
| | Design Chainage (Km) | Design Length (Km) | Width (m) | |
| Stretch | 099.700 to 104.500 | 4.800 | 15.00 | Within 90(Ninety) days of the Appointed date |
| Stretch | 109.700 to 110.980 | 1.280 | 15.00 | |
| Stretch | 113.700 to 116.400 | 2.740 | 15.00 | |

Besides this, the Authority has to acquire additional land at Bus bays/Bus Shelter locations, turning radius at Minor & Major junctions. The location of Bus bays/Bus Shelter as per Schedule C of Concession Agreement is given below in the tabular form:-

| Sr. No. | Design Chainage | Side | Work Status |
|---------|-----------------|----------------|----------------|
| 1 | 76.700 | Both Hand Side | |
| 2 | 79.350 | Both Hand Side | |
| 3 | 80.400 | Both Hand Side | |
| 4 | 81.450 | Both Hand Side | |
| 5 | 84.350 | Both Hand Side | Work Completed |
| 6 | 92.250 | Both Hand Side | Work Completed |
| 7 | 93.150 | Both Hand Side | |
| 8 | 94.250 | Both Hand Side | |
| 9 | 97.850 | Both Hand Side | Work Completed |

The status of compensation disbursement for land and structures are given below in the tabular form:-

| Table 2.1-2: Compensation disbursement for land | | | | | |
|---|----------------------|-------------------------|-----------------------|------------------------------|---------|
| SL. No. | Name of the District | Total No. of Land cases | Amount paid (in Nos.) | Balance to be Paid (in Nos.) | Remarks |
| 1 | Cuddalore | 710 | 710 | 0 | |
| 2 | Ariyalur | 355 | 355 | 0 | |
| 3 | Thanjavur | 102 | 102 | 0 | |
| Total in Nos. | | 1167 | 1167 | 0 | |
| Total in % | | 100% | 0% | | |

| Table 2.1-3 - Compensation disbursement for Structures | | | | | |
|--|----------------------|-------------------------|-----------------------|------------------------------|---------|
| Sl. No. | Name of the District | Total No. of structures | Amount paid (in Nos.) | Balance to be Paid (in Nos.) | Remarks |
| 1 | Cuddalore | 383 | 383 | 0 | |
| 2 | Ariyalur | 461 | 461 | 0 | |
| 3 | Thanjavur | 148 | 148 | 0 | |
| Total in Nos. | | 992 | 992 | 0 | |
| Total in % | | 100% | 0% | | |

2.2. Removal of Religious Structures

The following structures coming within the ROW are to be demolished:-

| Table 2.2-1: Status of Removal of Religious structures | | | | |
|--|----------------------|-------------------------|------------------------------|-------------------|
| Sl No. | Name of the District | Total No. of structures | Removed as on Date (in Nos.) | Balance (in Nos.) |
| 1 | Cuddalore | 10 | 10 | 0 |
| 2 | Ariyalur | 10 | 10 | 0 |
| 3 | Thanjavur | 2 | 2 | 0 |
| Total in Nos. | | 22 | 22 | 0 |

2.3. Shifting of Utilities and Electrical HT/LT Lines

To proceed with the project construction, several utilities are required to be shifted under the supervision of the respective authorities. These includes water supply pipe line, hand pumps, overhead water tanks, Electrical lines as shown in the table below:-

| Sr. No. | Name of the District | Chainages | | | Total Number of Estimates | Remarks |
|---------|----------------------|-----------|----|--------------|---------------------------|---------|
| | | From | To | Length in Km | | |
| Sr. No. | Name of the District | Chainages | | | Total Number of Estimates | Remarks |
| | | From | To | Length in Km | | |

| | | | | | | |
|---|-----------|---------|---------|-------|----|---------------------|
| 1 | Cuddalore | 65+960 | 86+440 | 20.48 | 25 | Work is in Progress |
| 2 | Ariyalur | 86+440 | 106+860 | 20.42 | 46 | |
| 3 | Thanjavur | 106+860 | 116+440 | 9.58 | 4 | |

Table 2.3-2: Status of sanction of Estimates - Electrical Lines Relocation

| Sr. No | Name of the District | Chainages | | | Number of Estimates | Present Status | Remarks |
|--------|-----------------------|-------------------------------------|---------|--------------|---------------------|-------------------|--|
| | | From | To | Length in Km | | | |
| 1 | Cuddalore | 65+960 | 86+440 | 20.48 | 10 | Estimate Approved | Supervision charges are paid and work is in progress |
| 2 | Ariyalur | 86+440 | 106+860 | 20.42 | 5 | Estimate Approved | |
| 3 | Thanjavur | 106+860 | 116+440 | 9.58 | 5 | Estimate Approved | |
| 4 | Cuddalore & Thanjavur | Km:70+020, Km:73+470 and Km:113+720 | | | 3 | Estimate Approved | Supervision Charges paid |

Table 2.3-3: Status of Utility Relocation

| Sl. No. | Authority | Description | Unit | Total Length/ Nos. | Work done | Balance work to be done | Remarks |
|---------|----------------------|------------------------------------|------|--------------------|------------------|-------------------------|---------------------|
| 1 | BDO & EE, TWAD | Water Supply Pipe Line | Kms. | 72.695 | 32.635 | 40.060 | Work is in progress |
| 2 | BDO of Concern Union | Hand Pump/Pump Room with Bore well | Nos. | 24 | 16 | 8 | |
| 3 | BDO of Concern Union | Over Head Tank | Nos. | 15 | 13 Nos Completed | 2 | |
| 4 | TNEB | Electrical Lines | Kms. | 6.83 | 6.13 | 0.70 | |
| 5 | TNEB | Erection of HT Tower at Ch. 73+470 | Nos. | 2 | 2 | 0 | |
| 6 | CMWSSB | Veeranam Pipeline | Nos. | 1 | 0 | 1 | Work is in progress |
| 7 | PWD | Weir located at Ch. 103+990 | Nos. | 1 | 1 | 0 | |

2.4. Tree felling

Table 2.4-1: Status of Tree felling

| Sl. No. | Name of the District | Chainages | | | Effectuated Length in Kms. | Completed as on Date | Balance as on Date | Balance no. of Trees | Remarks |
|------------|-------------------------|-----------|---------|-----------------|----------------------------------|-------------------------|-----------------------|----------------------------|---------|
| | | From | To | Length in Km | | | | | |
| 1 | Cuddalore | 65+960 | 86+440 | 20.48 | 6.535 | 6.535 | 0 | 0 | |
| 2 | Ariyalur | 86+440 | 106+860 | 20.42 | 8.385 | 8.385 | 0 | 0 | |
| 3 | Thanjavur | 106+860 | 116+440 | 9.58 | 2.515 | 2.515 | 0 | 0 | |
| Total | | | | 50.480 | 17.435 | 17.435 | 0 | 0 | |

3. Progress Briefing – Contractor Activities

3.1. Pre-construction Activities

Detailed Design & Drawings

The Plan and Profile, as well as the Pavement Design for the entire 50.480 km project length has been completed, reviewed and accepted by the Independent Engineer (IE). Construction Methodology, QA & QC procedures submitted to the IE has been reviewed and accepted.

Table 3.1-1: Status of Highway Design and Drawings as per Concession Agreement

| Sr. No. | Description | Unit | Total Scope As per Sch. B | Design & Drawing Submitted | Design & Drawing Approved |
|---------|------------------------------|------|---------------------------|----------------------------|---------------------------|
| 1 | Pavement Design | Km | 50.48 | 50.48 | 50.48 |
| 2 | Plan & Profile | Km | 50.48 | 50.48 | 50.48 |
| 3 | Typical Cross Sections | Type | 7 | 7 | 7 |
| 4 | Major Intersections | No | 07 | - | - |
| 5 | Minor Intersections | No | 100 | - | - |
| 6 | Toll Plaza (Typical Details) | No | 01 | 01 | - |
| 7 | Slip/Service Roads | Km | 26.595 | 26.595 | 26.595 |

Table 3.1-2 : Status of Structure Design and Drawings as per Concession Agreement

| Sr. No. | Description | Unit | Total Scope As per Sch. B | Design & Drawing Submitted | Design & Drawing Approved |
|---------|------------------------------|------|---------------------------|----------------------------|---------------------------|
| 1 | Major Bridges | No | 04 | 04 | 04 |
| 2 | Minor Bridges | No | 25 | 25 | 25 |
| 3 | Grade Separated Intersection | No | 08 | 08 | 08 |
| 4 | VUP/LVUP | No | 15 | 15 | 15 |
| 5 | Box /Slab Culvert | No | 60 | 60 | 60 |

Table 3.1-3 : Status of Structure Design and Drawings additionally included under Positive Change of Scope due to demand of local public

| Sr. No. | Structure Location | Type of Structure | Unit | Design & Drawing Submitted | Design & Drawing Approved |
|---------|--------------------|-------------------|------|----------------------------|---------------------------|
| 1 | 66+185 | LVUP | Nos. | - | - |
| 2 | 71+900 | Box Culvert | Nos. | - | - |
| 3 | 72+250 | Minor Bridge | Nos. | 01 | - |
| 4 | 72+780 | Minor Bridge | Nos. | 01 | 01 |
| 5 | 72+820 | Minor Bridge | Nos. | 01 | 01 |
| 6 | 72+860 | Minor Bridge | Nos. | 01 | 01 |
| 7 | 73+040 | Minor Bridge | Nos. | 01 | 01 |
| 8 | 80+300 | PUP | Nos. | - | - |
| 9 | 81+900 | Box Culvert | Nos. | - | - |
| 10 | 95+200 | PUP | Nos. | 01 | 01 |
| 11 | 95+700 | PUP | Nos. | 01 | 01 |
| 12 | 105+220 | PUP | Nos. | 01 | 01 |
| 13 | 106+890 | PUP | Nos. | 01 | - |
| 14 | 106+905 | Box Culvert | Nos. | 01 | - |

4. Physical Progress of Work

4.1. Physical Progress of Work:

The Progress of the Major works carried out at the Site till the month of August 2023 is as follows:-

CUMMULATIVE STATEMENT

For Main Carriageway

| Sr. No . | Description | Total Length of Project (in. Km.) | Progress up to Previous Month (in Km.) | Progress during this Month (in Km.) | Cumulative Progress Achieved up to this Month (in Km.) | Work in Progress (In Km.) | Balance Length to be Completed | Cumulative % of Progress Achieved |
|----------|-------------------------------------|-----------------------------------|--|-------------------------------------|--|---------------------------|--------------------------------|-----------------------------------|
| 1 | Clearing and Grubbing | | | | | | | |
| | LHS | 50.480 | 49.625 | 0.250 | 49.875 | 0.000 | 0.605 | 98.80% |
| | RHS | 50.480 | 49.625 | 0.250 | 49.875 | 0.000 | 0.605 | 98.80% |
| 2 | Embankment Top | | | | | | | |
| | LHS | 50.480 | 40.490 | 0.000 | 40.490 | 4.650 | 9.990 | 80.21% |
| | RHS | 50.480 | 40.240 | 0.000 | 40.240 | 4.800 | 10.240 | 79.71% |
| 3 | Subgrade Top | | | | | | | |
| | LHS | 50.480 | 39.986 | 0.259 | 40.245 | 0.245 | 10.235 | 79.72% |
| | RHS | 50.480 | 39.745 | 0.450 | 40.195 | 0.045 | 10.285 | 79.63% |
| 4 | GSB/ Cement Treated Sub Base | | | | | | | |
| | LHS | 50.480 | 39.600 | 0.090 | 39.690 | 0.000 | 10.790 | 78.63% |
| | RHS | 50.480 | 39.620 | 0.100 | 39.720 | 0.000 | 10.760 | 78.68% |
| 5 | Wet Mix Macadam | | | | | | | |
| | LHS | 50.480 | 39.600 | 0.090 | 39.690 | 0.000 | 10.790 | 78.63% |
| | RHS | 50.480 | 39.340 | 0.360 | 39.700 | 0.000 | 10.780 | 78.65% |
| 6 | Dense Bituminous Macadam | | | | | | | |
| | LHS | 50.480 | 39.340 | 0.350 | 39.690 | 0.000 | 10.790 | 78.63% |
| | RHS | 50.480 | 39.340 | 0.360 | 39.700 | 0.000 | 10.780 | 78.65% |
| 7 | Bituminous Concrete | | | | | | | |
| | LHS | 50.480 | 39.340 | 0.350 | 39.690 | 0.000 | 10.790 | 78.63% |
| | RHS | 50.480 | 39.330 | 0.360 | 39.690 | 0.000 | 10.790 | 78.63% |

For Service road

| Sr. No . | Description | Total Length of Service Road (in Km.) | Progress up to Previous Month (in Km.) | Progress during this Month (in Km.) | Cumulative Progress Achieved up to this Month (in Km.) | Work in Progress (in Km.) | Balance Length to be Completed | Cumulative % of Progress Achieved |
|----------|--------------------------|---------------------------------------|--|-------------------------------------|--|---------------------------|--------------------------------|-----------------------------------|
| 1 | Embankment | 53.190 | 42.270 | 0.315 | 42.585 | 0.000 | 10.605 | 80.06% |
| 2 | Sub grade | 53.190 | 42.270 | 0.315 | 42.585 | 0.000 | 10.605 | 80.06% |
| 3 | GSB/ Cement Treated Base | 53.190 | 42.120 | 0.315 | 42.435 | 0.000 | 10.755 | 79.78% |
| 4 | Wet Mix Macadam | 53.190 | 41.520 | 0.440 | 41.960 | 0.000 | 11.230 | 78.89% |
| 5 | Dense Bituminous Macadam | 53.190 | 40.760 | 0.360 | 41.120 | 0.000 | 12.070 | 77.31% |
| 6 | Bituminous Concrete | 53.190 | 29.105 | 0.000 | 29.105 | 0.000 | 24.085 | 54.72% |

Structure Work

| Sr. No. | Type of Structure | Total No. of Structures | Nos. of Structures | | | | Remarks |
|---------|---------------------------|-------------------------|--------------------|------------------|------------------------|--|---------|
| | | | Completed | Work in Progress | Balance to be taken up | | |
| 1 | Culvert | 60 | 52.25 | 0.75 | 7.00 | | |
| 2 | Light Vehicular Underpass | 2 | 1 | 1 | 0 | | |
| 3 | Vehicular Underpass | 13 | 11.50 | 1.00 | 0.50 | Balance 0.5 No. has been included under Negative Change of Scope. | |
| 4 | Minor Bridges | 25 | 25.00 | 0 | 0 | | |
| 5 | Major Bridge | 4 | 3.50 | 0.50 | 0 | | |
| 6 | Flyover | 8 | 6.00 | 1.00 | 1.00 | Balance 1.00 No. has been included under Negative Change of Scope. | |

The Physical Progress of the Project up to the month of August 2023 as per the weightages finalized in the Approved Schedule G is as follows:-

| Item | Stage for Payment | Unit | Qty. | Weightage in percentage to Contract Price | Completed up to August'20 23 | Physical Progress (%) | Remarks |
|---|---|-------|-------|---|------------------------------|-----------------------|---------|
| Road works including culverts, minor bridges, underpasses, overpasses, approaches to ROB/RUB/ Major Bridges/ Structures (but excluding service roads) | A- Widening and strengthening of existing road | | | | | | |
| | (1) Earthwork up to top of the sub-grade | Km | 66.96 | 9.517% | 52.400 | 7.447% | |
| | (2) Granular work (sub-base, base, shoulders) | | | | | | |
| | (a) GSB/ Cement Treated Base | Km | 65.52 | 3.373% | 52.220 | 2.688% | |
| | (b) WMM/ Cement Treated Base | Km | 65.52 | 4.046% | 52.200 | 3.223% | |
| | (3) Shoulders | Km | 17.65 | 0.112% | 17.190 | 0.109% | |
| | (4) Bituminous work | Km | | | | | |
| | (a) DBM | Km | 65.52 | 3.344% | 52.200 | 2.664% | |
| | (b) BC | Km | 65.52 | 3.023% | 52.190 | 2.408% | |
| | (5) Rigid Pavement | | | | | | |
| | (6) Widening and repair of culverts | Nos . | 16 | 0.440% | 15.150 | 0.417% | |
| | (7) Widening and repair of minor bridges | Nos . | 4 | 0.959% | 4.000 | 0.959% | |
| | B- New realignment/bypass | | | | | | |
| | (1) Earthwork up to top of the sub-grade | Km | 28.68 | 6.437% | 21.540 | 4.835% | |
| | (2) Granular work (sub-base, base, shoulders) | | | | | | |
| | (a) GSB/ Cement Treated Base | Km | 28.68 | 1.615% | 20.790 | 1.171% | |
| | (b) WMM/ Cement Treated Base | Km | 28.68 | 1.436% | 20.790 | 1.041% | |
| | (3) Shoulders | Km | 24.63 | 0.112% | 15.470 | 0.071% | |
| | (4) Bituminous work | | | | | | |
| | (a) DBM | Km | 28.68 | 1.279% | 20.790 | 0.927% | |
| | (b) BC | Km | 28.68 | 1.158% | 20.790 | 0.840% | |
| | (5) Rigid Pavement | | | | | | |
| | C- New culverts, minor bridges, underpasses, overpasses on existing road, realignments, bypasses: | | | | | | |
| | (1) Culverts | Nos . | 44 | 2.070% | 37.10 | 1.745% | |
| | (2) Minor bridges | | | | | | |
| | (a) Foundation | Nos . | 58 | 3.953% | 58.00 | 3.953% | |


| | | | | | | | |
|---------------------------------------|--|-------|-----|--------|--------|--------|--|
| Major Bridge works and ROB/RUB | (b) Substructure | Nos . | 134 | 2.623% | 134.00 | 2.623% | |
| | (c) Superstructure (including crash barrier etc. complete) | Nos . | 50 | 1.559% | 47.60 | 1.485% | |
| | (5) Grade separated structures | | | | | | |
| | (a) Underpass (13 VUP, 2 LVUP) | | | | | | |
| | (i) Foundation | Nos . | 56 | 2.574% | 51.00 | 2.344% | |
| | (ii) Substructure | Nos . | 60 | 0.751% | 51.00 | 0.639% | |
| | (iii) Superstructure (including crash barrier etc. complete) | Nos . | 30 | 1.289% | 25.00 | 1.074% | |
| | (c) Flyover | | | | | | |
| | (i) Foundation | Nos . | 36 | 2.426% | 32.00 | 2.156% | |
| | (ii) Substructure | Nos . | 36 | 0.470% | 31.00 | 0.405% | |
| | (iii) Superstructure (including crash barrier etc. complete) | Nos . | 20 | 1.244% | 16.00 | 0.996% | |
| | (d) Foot over Bridge | | | | | | |
| | C- New Major Bridges | | | | | | |
| | (1) Foundation | | | 0.000% | | | |
| | (a) Open Foundation | | | 0.000% | | | |
| | (b) Pile Foundation/ Well Foundation | | | | | | |
| | (i) Pile Foundation | Nos . | 84 | 9.699% | 84.00 | 9.699% | |
| | (2) Sub-structure | Nos . | 84 | 4.576% | 84.00 | 4.576% | |
| | (3) Super-structure (including crash barriers etc. complete) | | | | | | |
| | (i) For MJB at Km. 107+400 | | | | | | |
| | (a) Casting of Superstructure (Box Segment) | Nos . | 666 | 1.450% | 666.00 | 1.450% | |
| | (b) Erection of Superstructure (Box Segment) | Nos . | 666 | 1.050% | 435.00 | 0.686% | |
| | (i) For other Major Bridges | | | | | | |
| | (a) Super-structure (including crash barriers etc. complete) | Nos . | 37 | 2.500% | 35.650 | 2.409% | |
| | D- New rail-road bridges | | | | | | |
| | (a) ROB | | | | | | |
| | (1) Foundation | Nos . | | 0.000% | | | |
| | (2) Sub-structure | Nos . | | 0.000% | | | |
| | (3) Super-structure (including crash barriers etc. complete) | Nos . | | 0.000% | | | |
| | (b) RUB | | | | | | |
| | (1) Foundation | Nos . | | 0.000% | | | |
| | (2) Sub-structure | Nos . | | 0.000% | | | |
| | (3) Super-structure (including crash barriers etc. complete) | Nos . | | 0.000% | | | |

| | | | | | | |
|--|--|-------|--------|-----------------|----------|---------------|
| Structures (elevated sections, reinforced earth) | A- Elevated Structures | | | | | |
| | (1) Foundation | Nos . | | 0.000% | | |
| | (2) Sub-structure | Nos . | | 0.000% | | |
| | (3) Super-structure (including crash barriers etc. complete) | Nos . | | 0.000% | | |
| Other Works | B- Reinforced earth Wall (includes Approaches of ROB, Underpasses, Overpasses, Flyover etc) | Sqm | 196027 | 7.604% | 1,00,420 | 3.895% |
| | (i) Service roads/ Slip Roads | Km | 53.19 | 4.690% | 29.105 | 2.566% |
| | (ii) Toll Plaza | Nos . | 1 | 1.821% | | |
| | (iii) Road side drains | Km | 28.85 | 5.429% | 13.930 | 2.622% |
| | (iv) Road signs, markings, km stones, safety devices, | | | | | |
| | (a) Road signs, markings, km stones, ... | Km | 100.96 | 2.558% | 71.880 | 1.821% |
| | (b) Concrete Crash Barrier/ W- Beam Crash Barrier in Road work | | | | | |
| | (i) Concrete Crash Barrier | Km | 26.5 | 1.179% | 10.170 | 0.452% |
| | (ii) W-Beam Crash Barrier | Km | 10.03 | 0.788% | 4.182 | 0.329% |
| | (v) Project facilities | | | | | |
| | (a) Bus Bays | No. | 18 | 0.009% | 6.000 | 0.003% |
| | (b) Truck Lay-byes | No. | | 0.000% | | |
| | (c) Rest areas | No. | | 0.000% | | |
| | (vi) Repairs to bridges/structures | Nos . | | | | |
| | (vii) Road side plantation | Km | 23.66 | 0.451% | 1.607 | 0.031% |
| | (viii) Protection works | | | | | |
| | (a) Boulder pitching on slopes | Km | 10.03 | 0.218% | 4.182 | 0.091% |
| | (b) Toe/Retaining wall | Km | 10.03 | 0.000% | | |
| | (x) Miscellaneous | Ls. | 100% | 0.164% | 70% | 0.115% |
| Total | | | | 100.000% | | 76.96% |

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

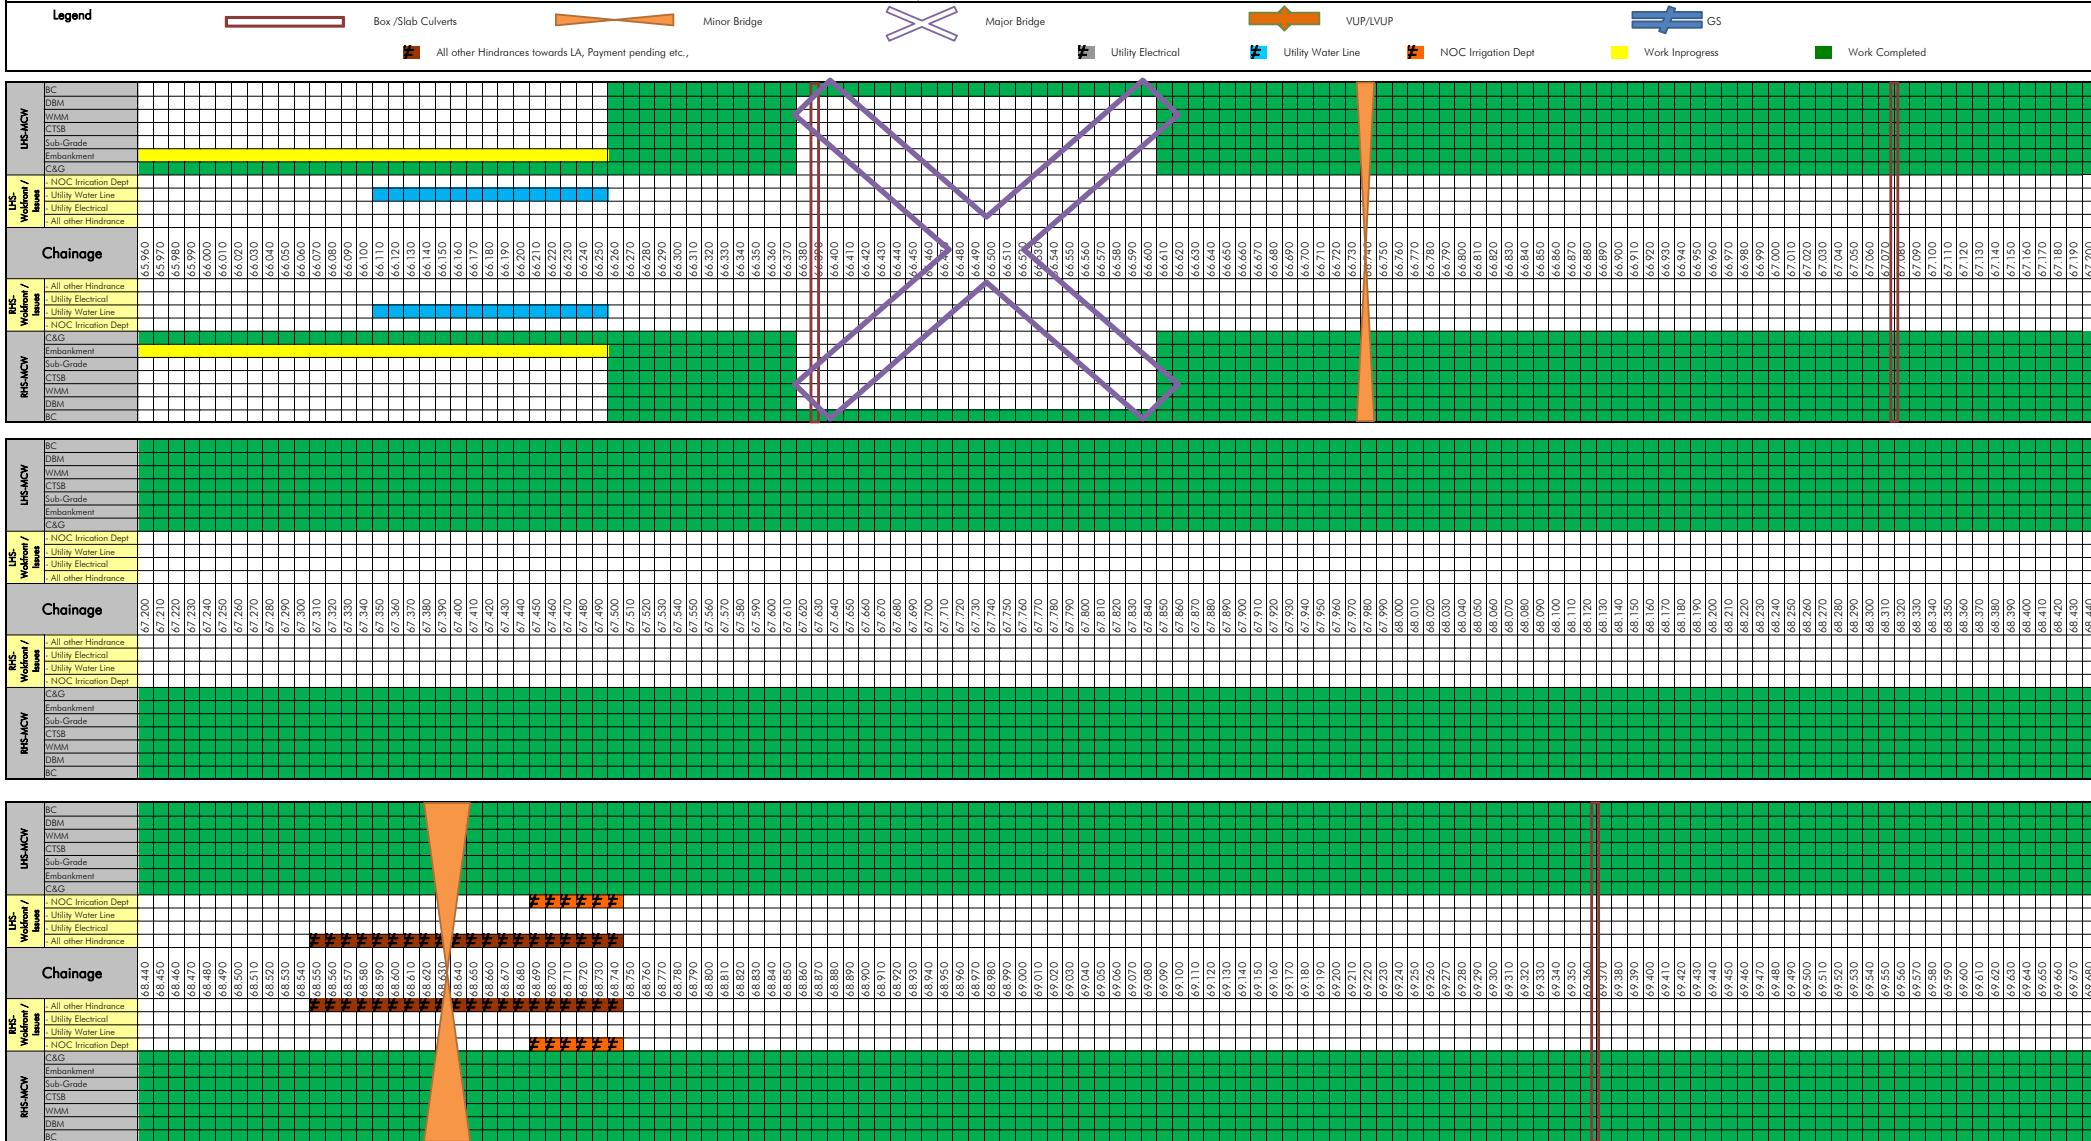


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023


Legend

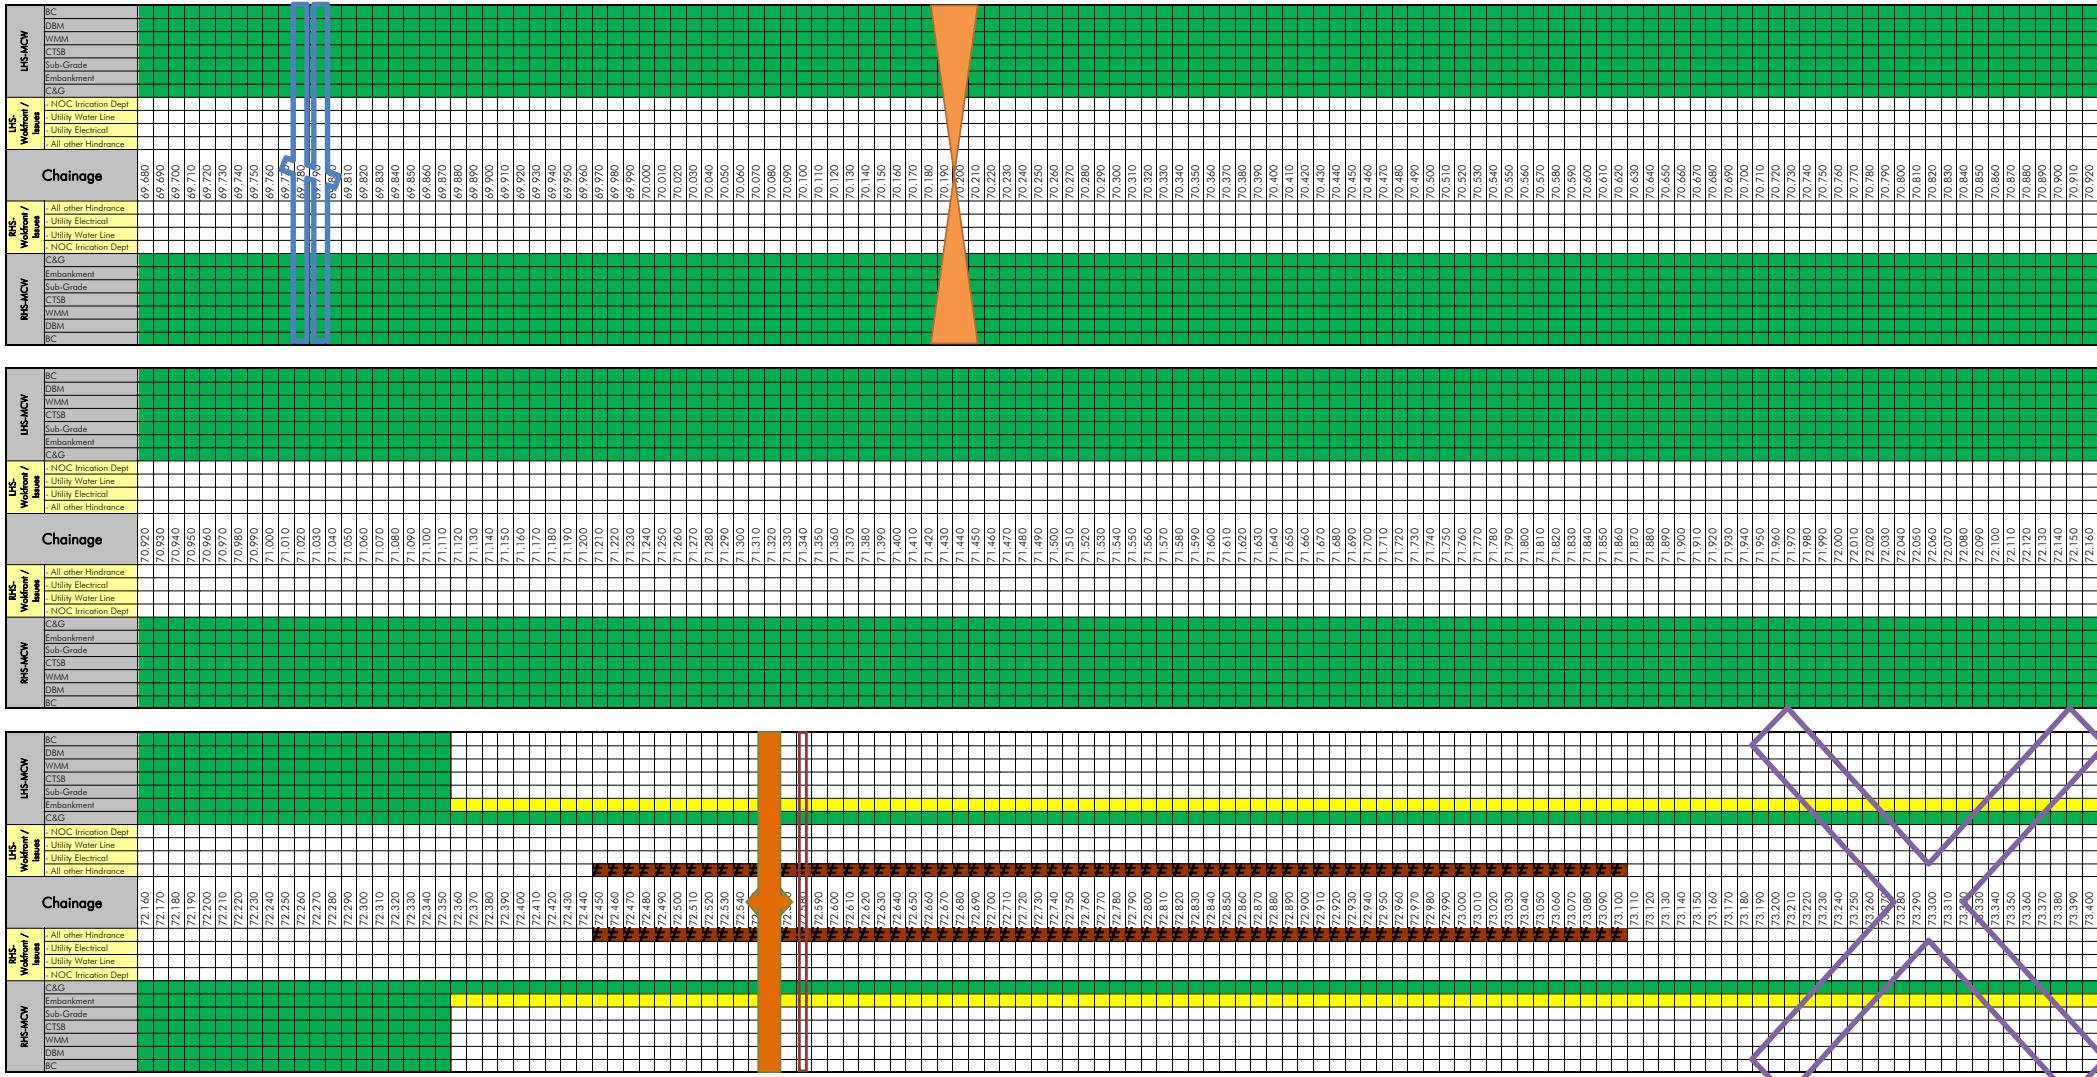

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

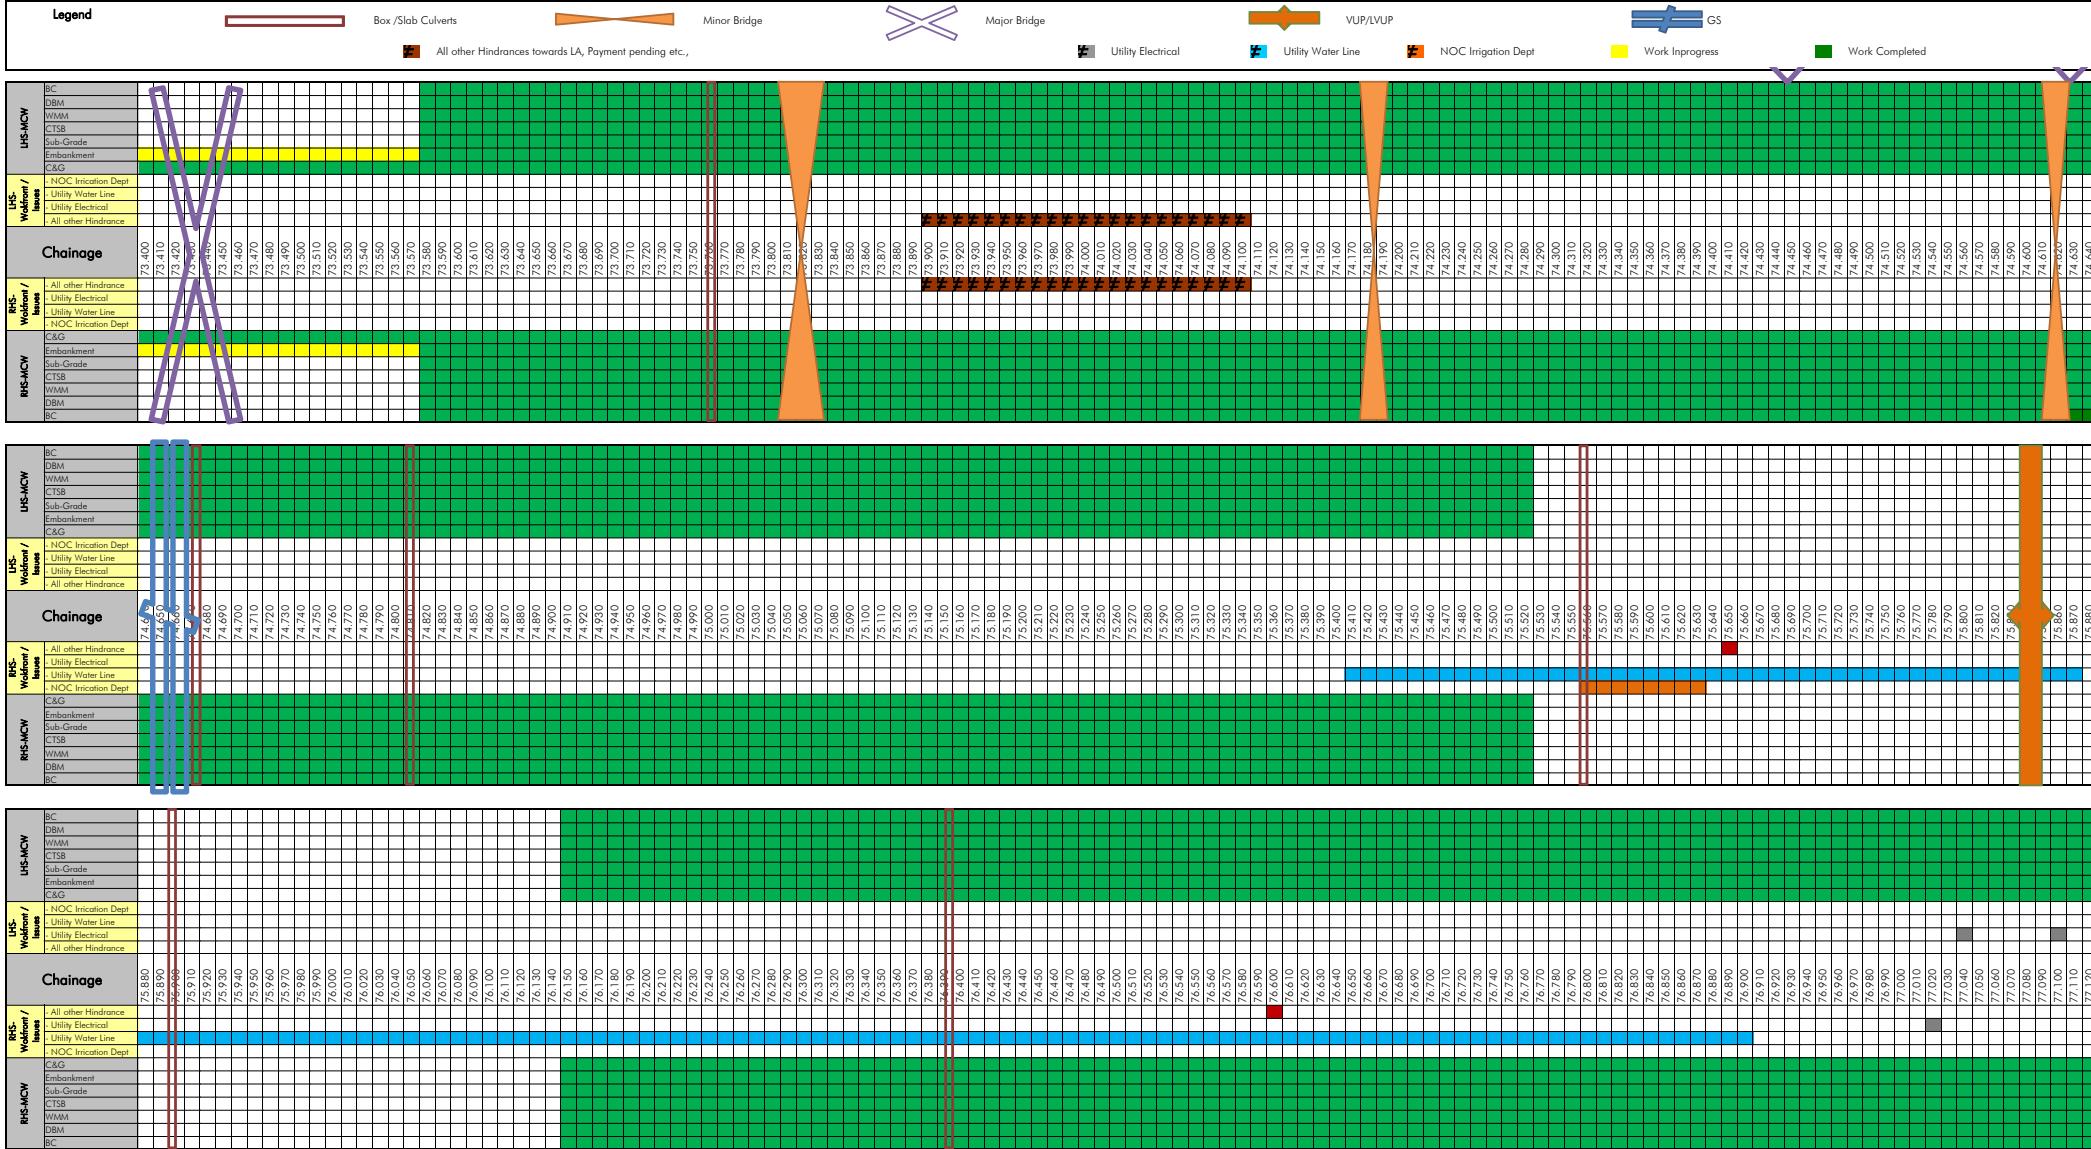

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend



3x / 3DDB CUVENS



Minor Bridge



Major Bridge






VUF/EVC



1



 All other Hindrances towards LA, Payment pending etc.

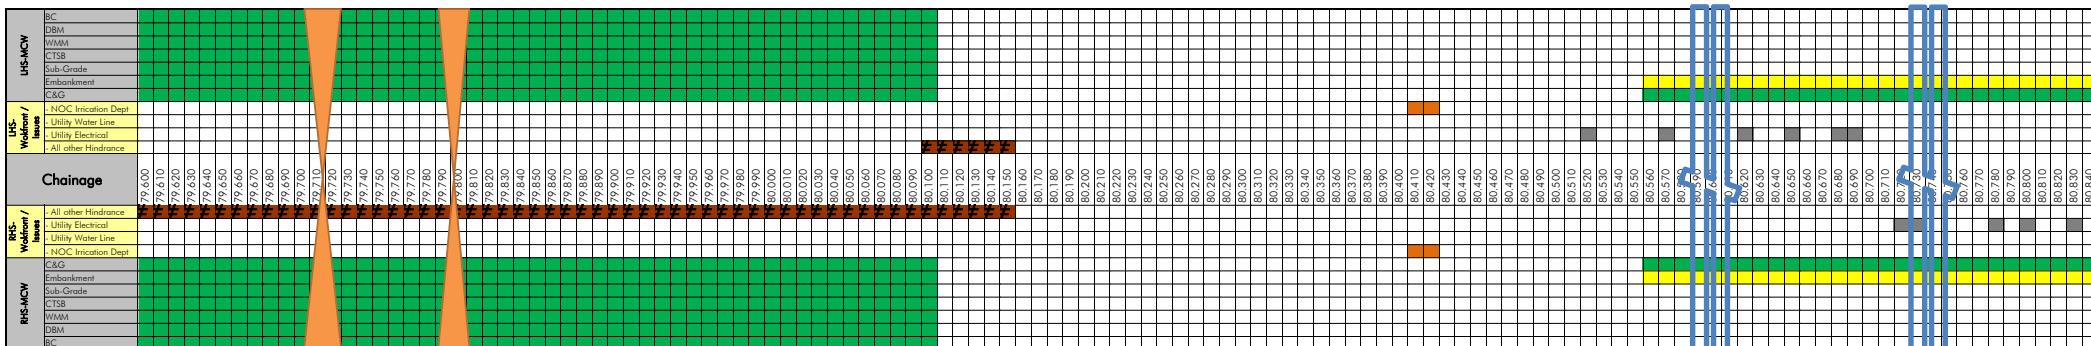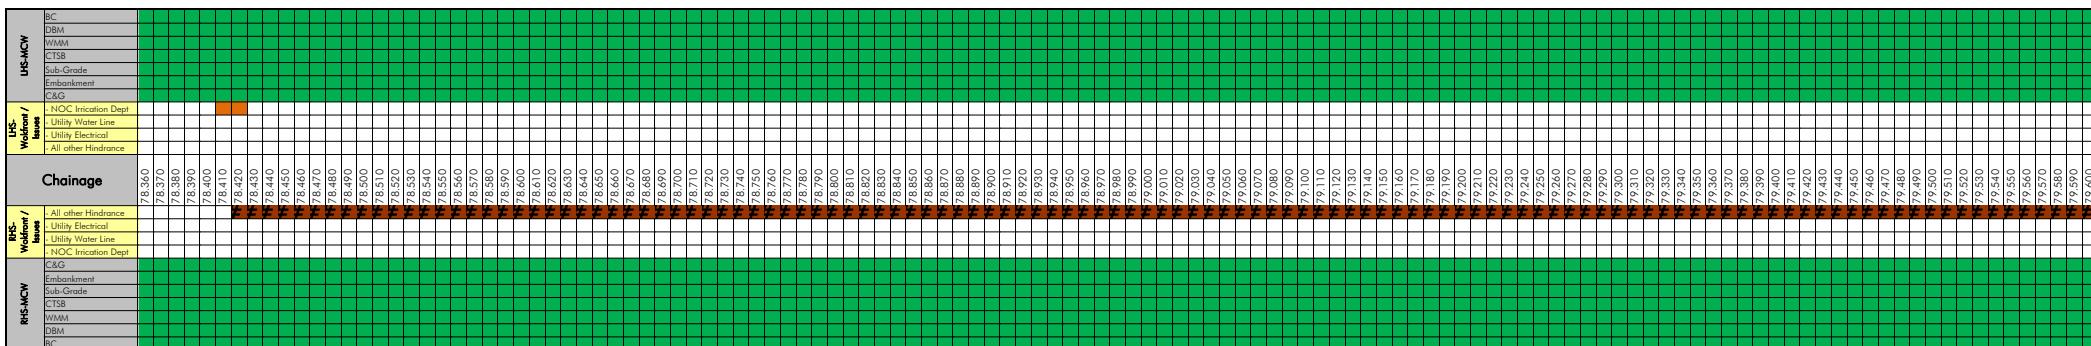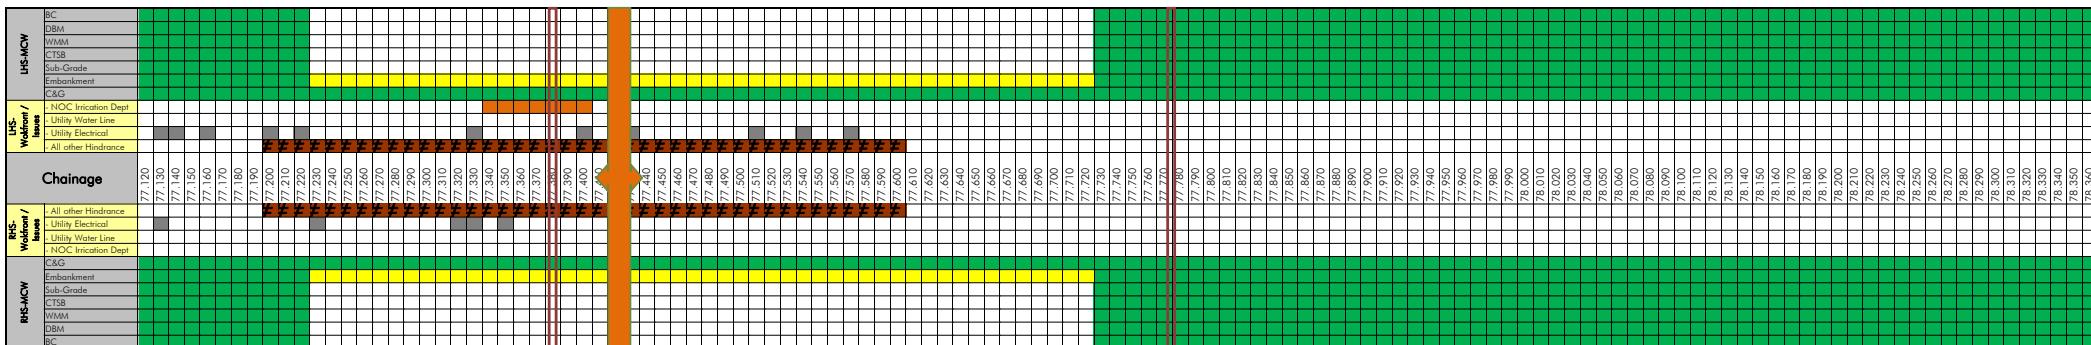


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend

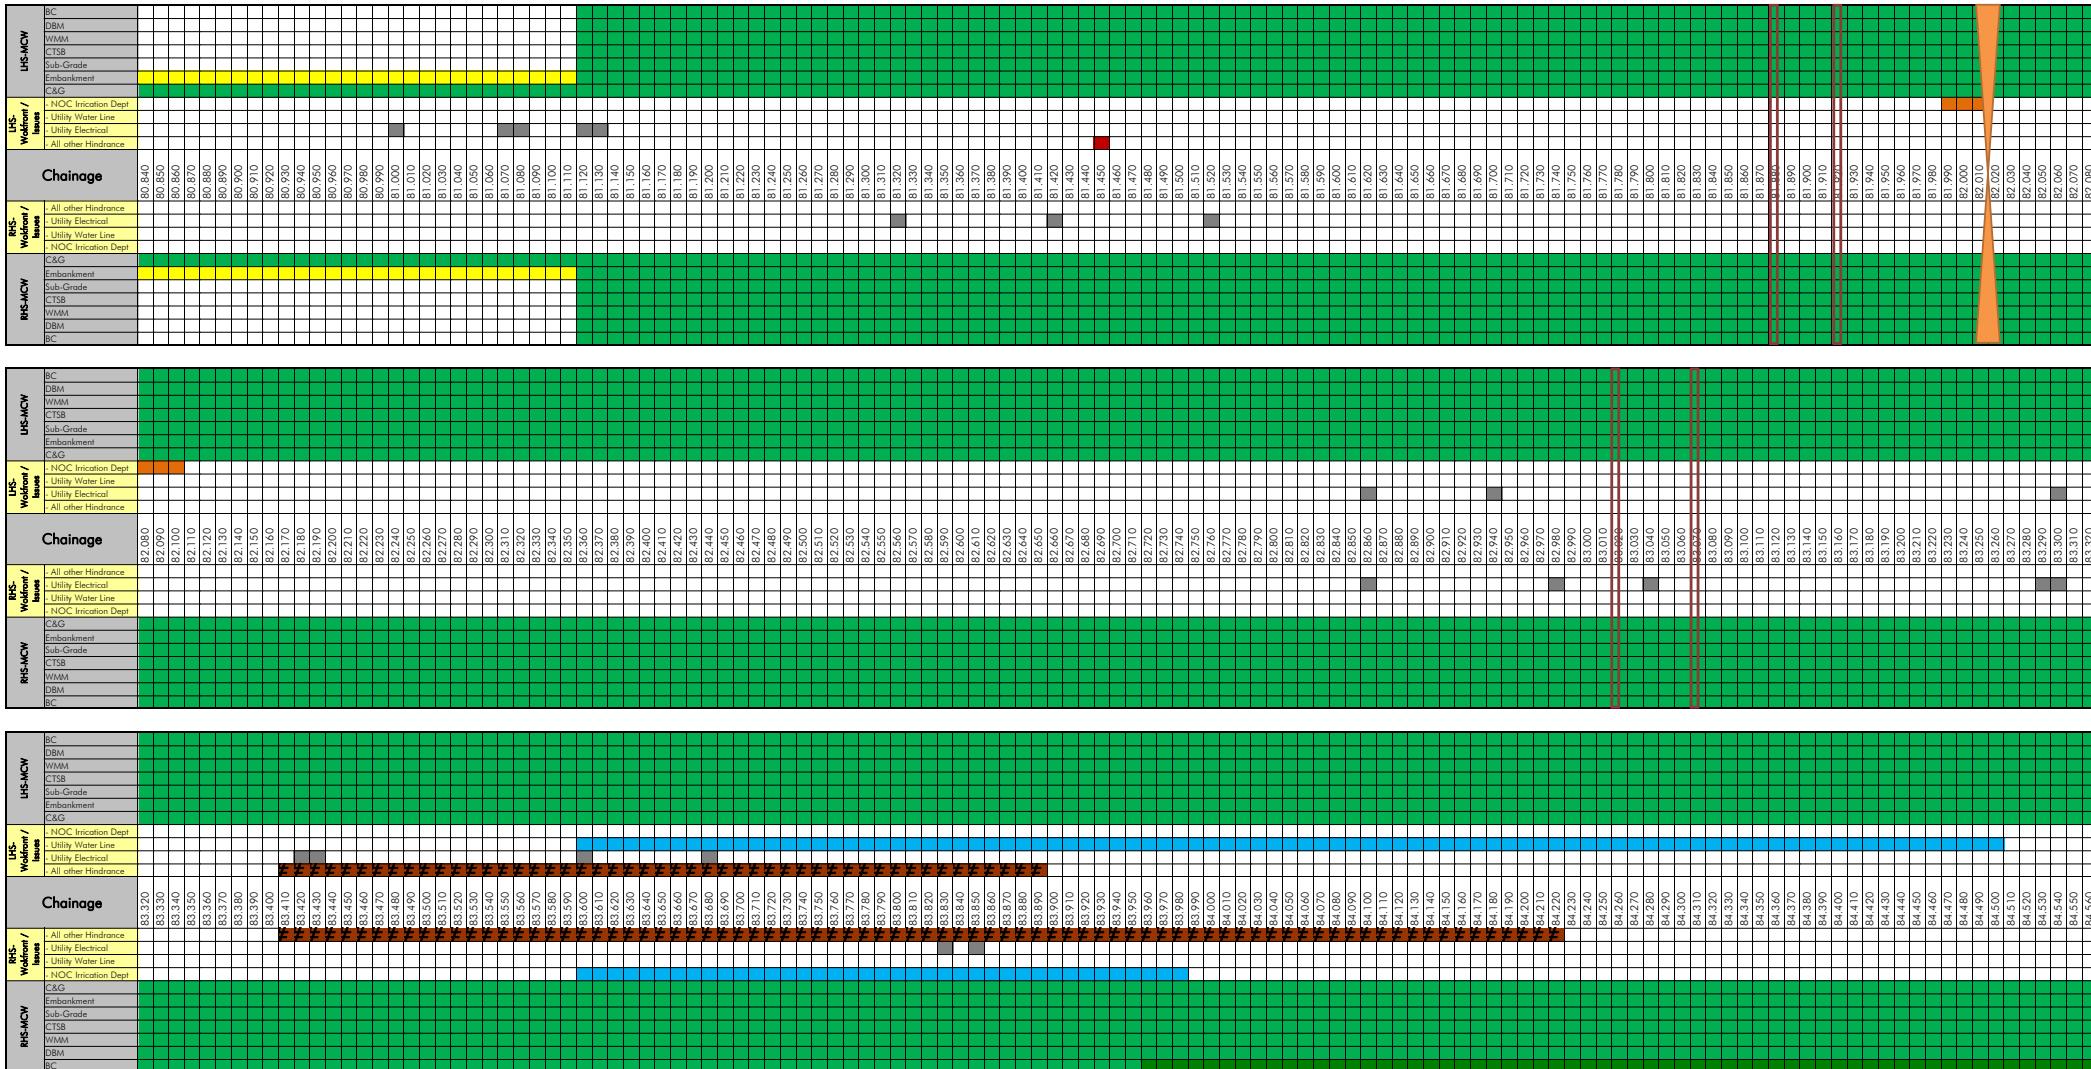


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend

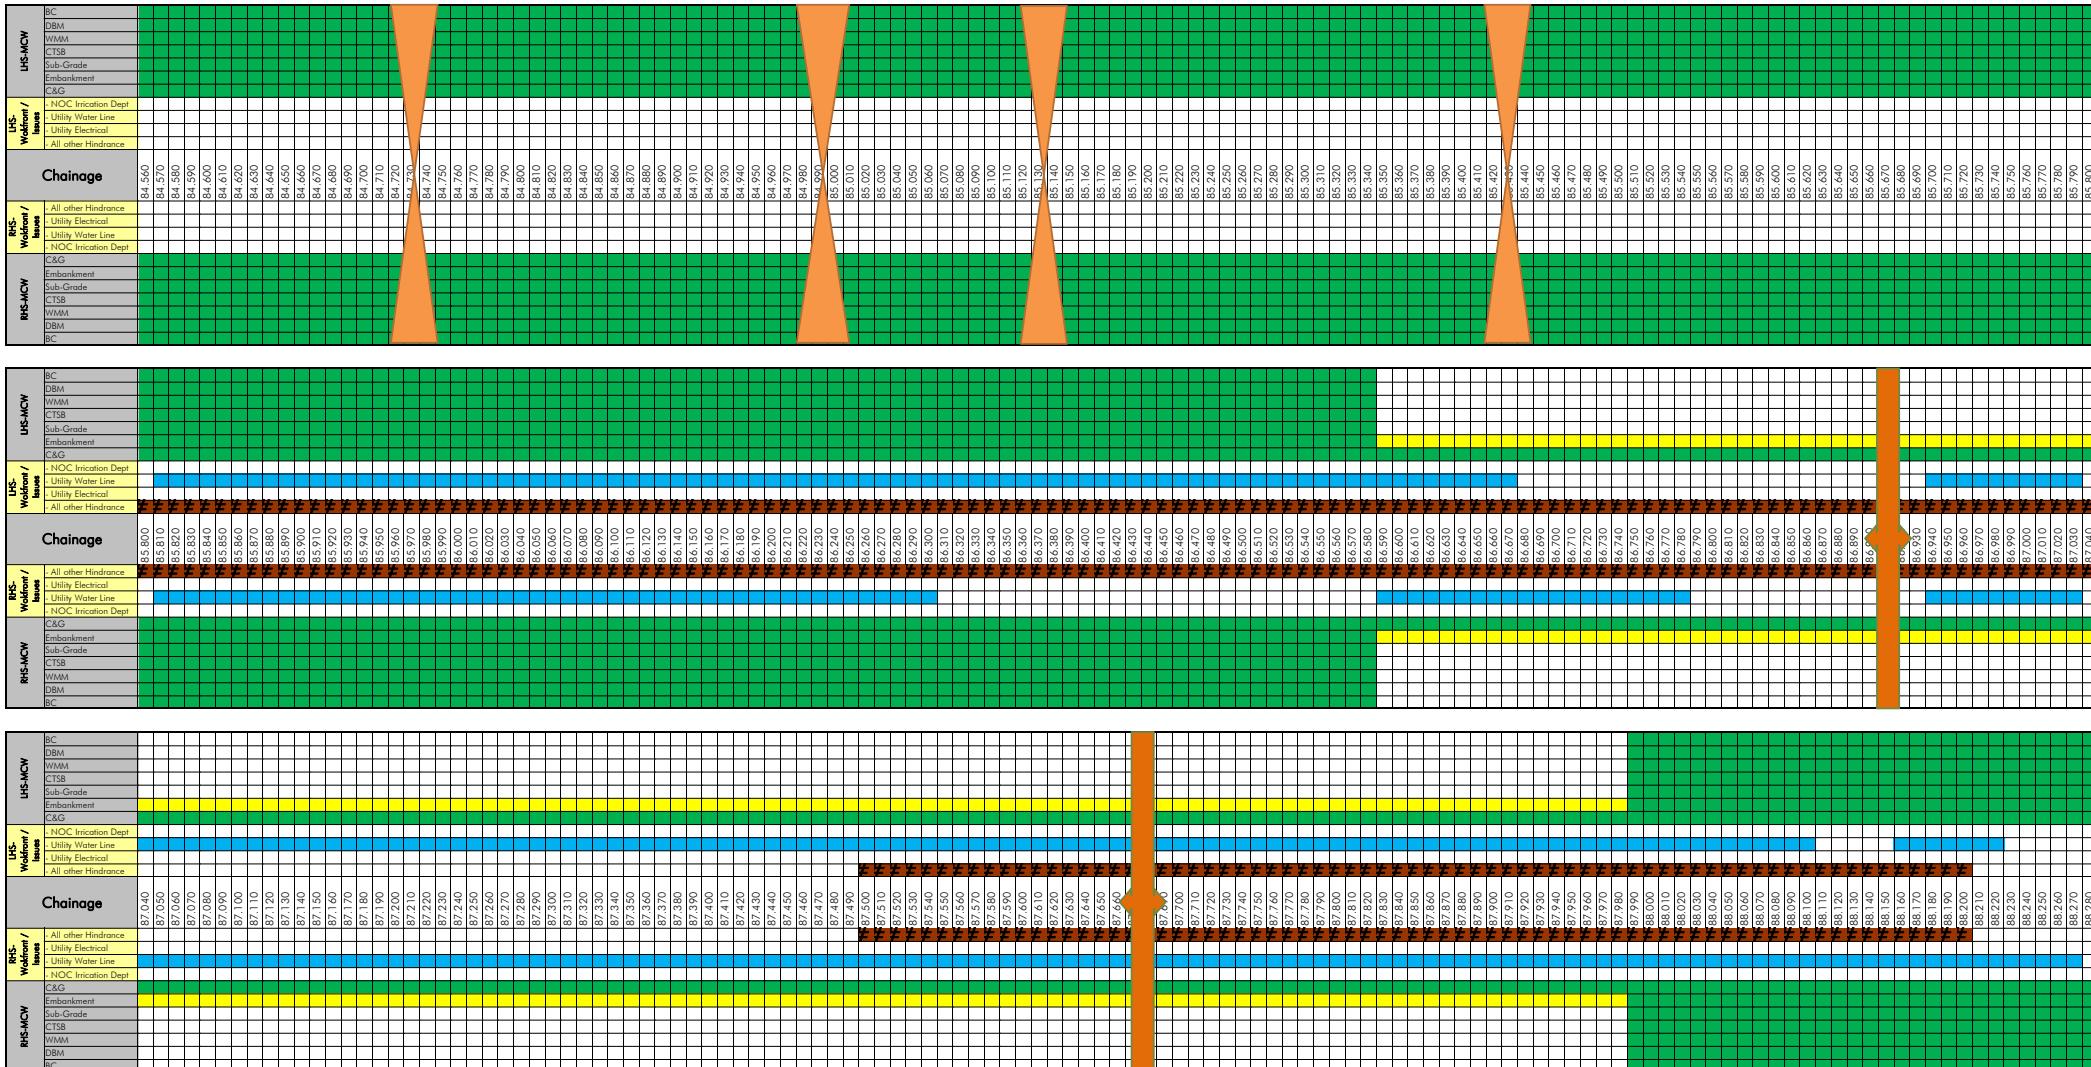


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend

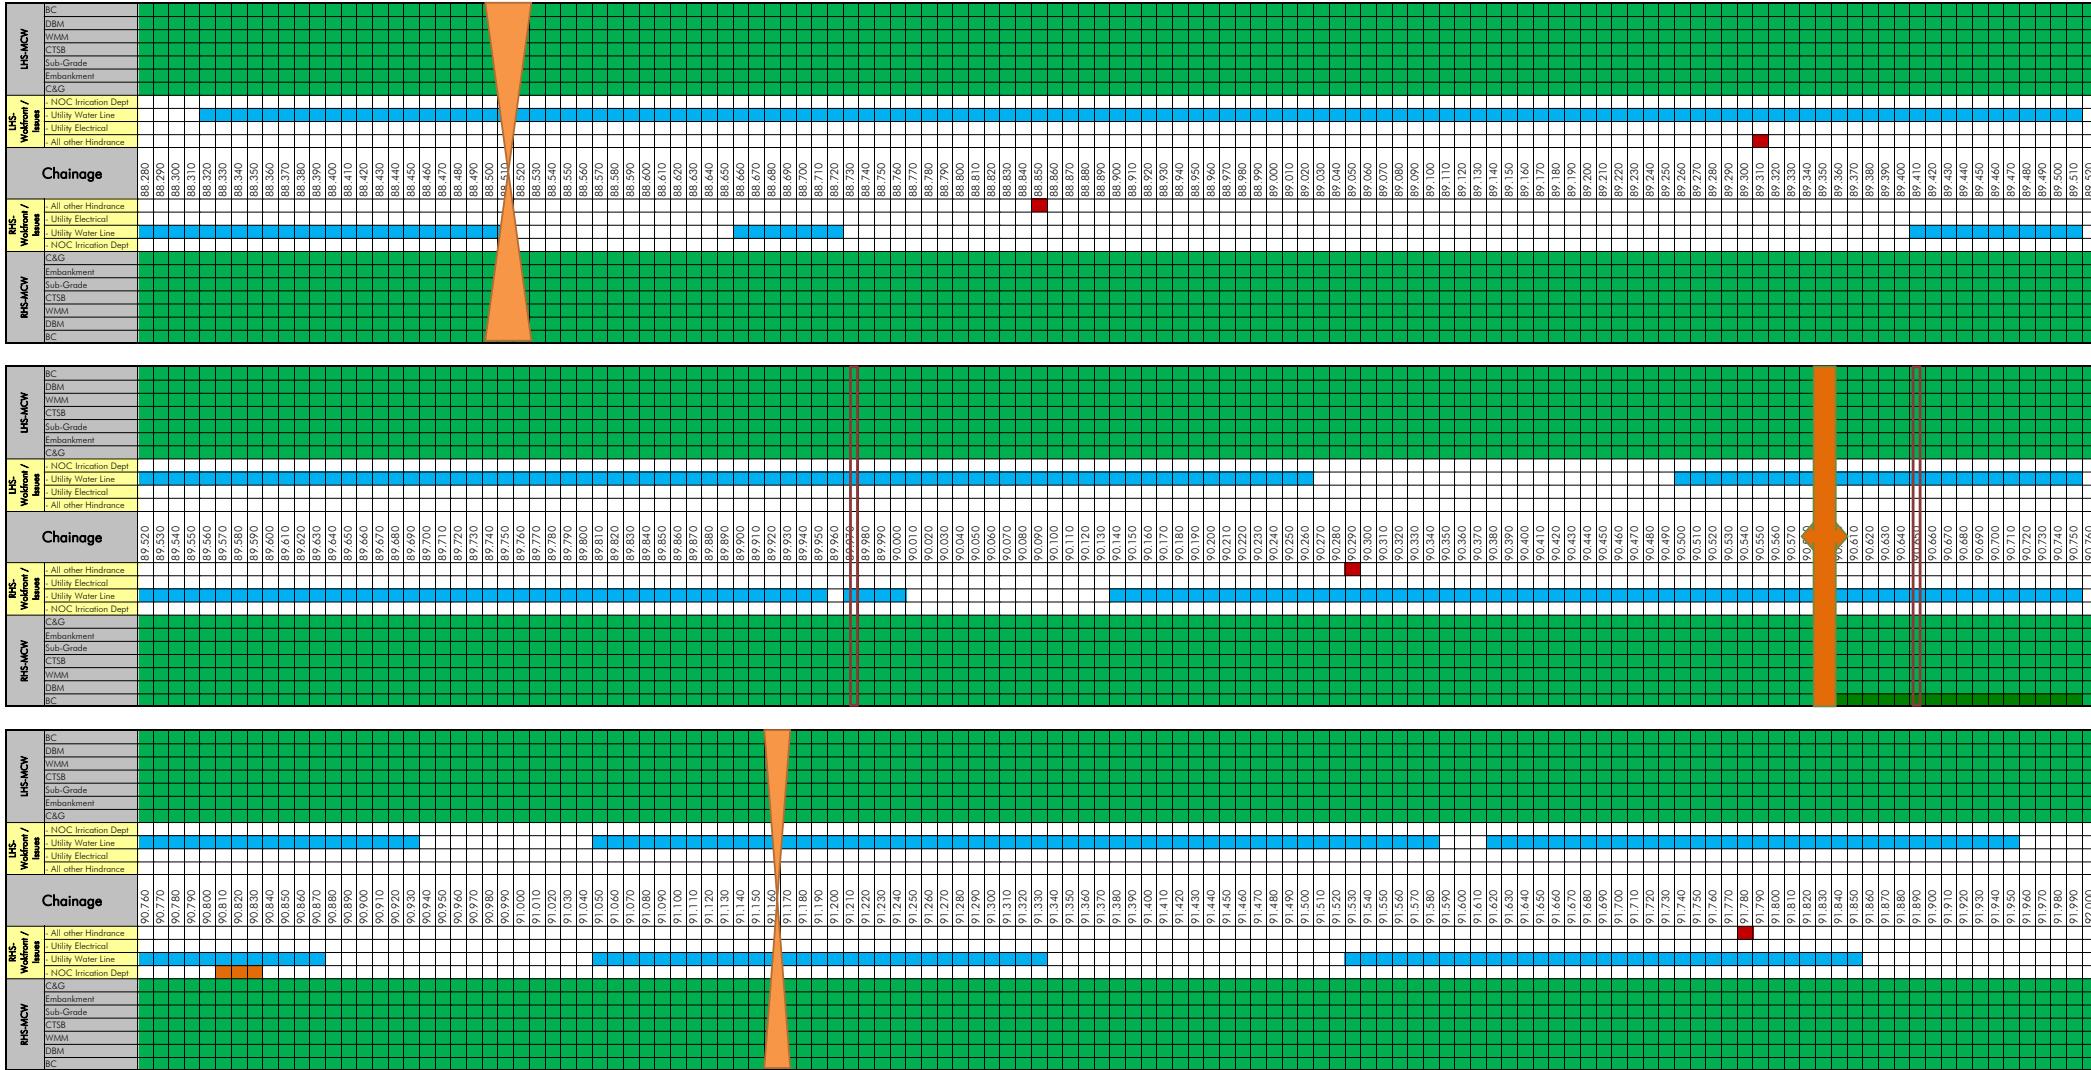


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend

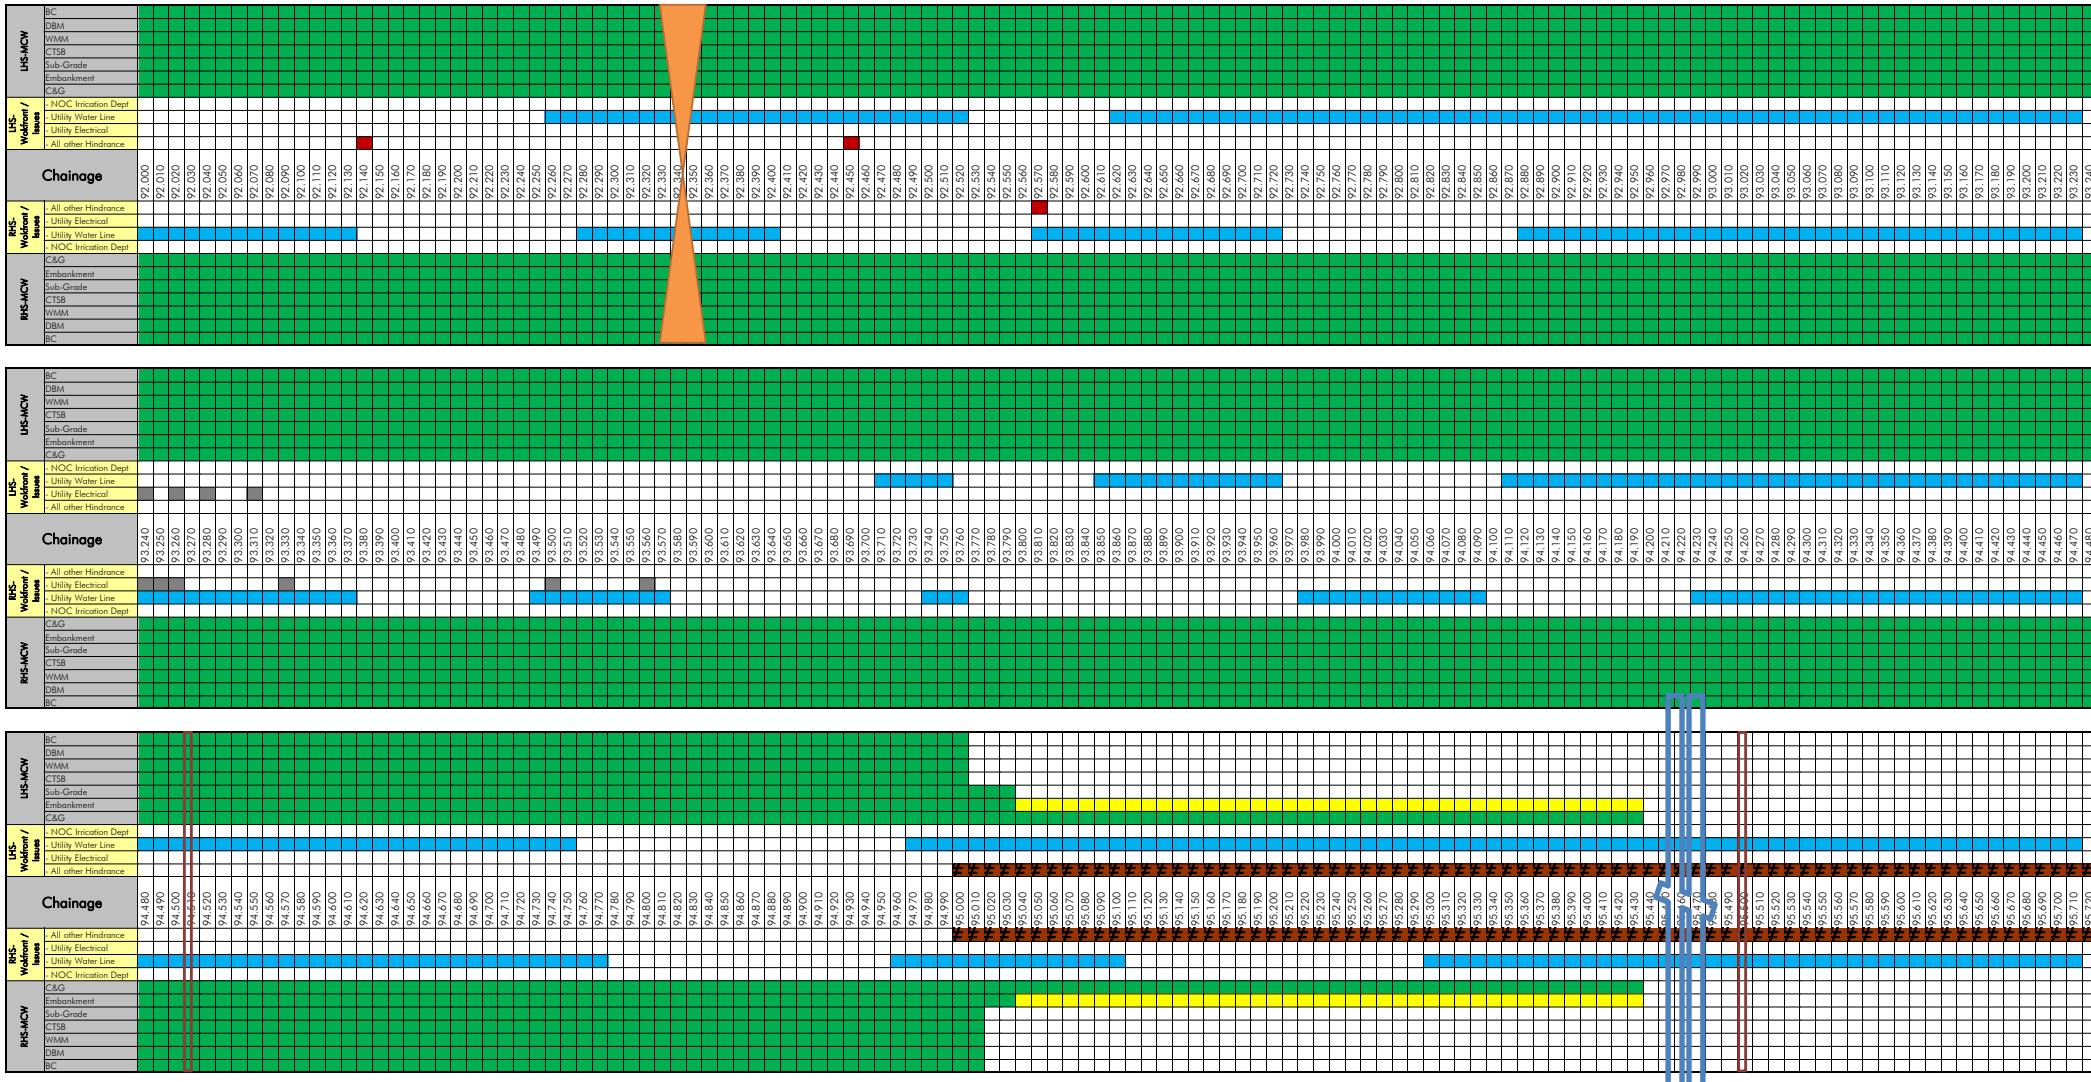


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023


Legend

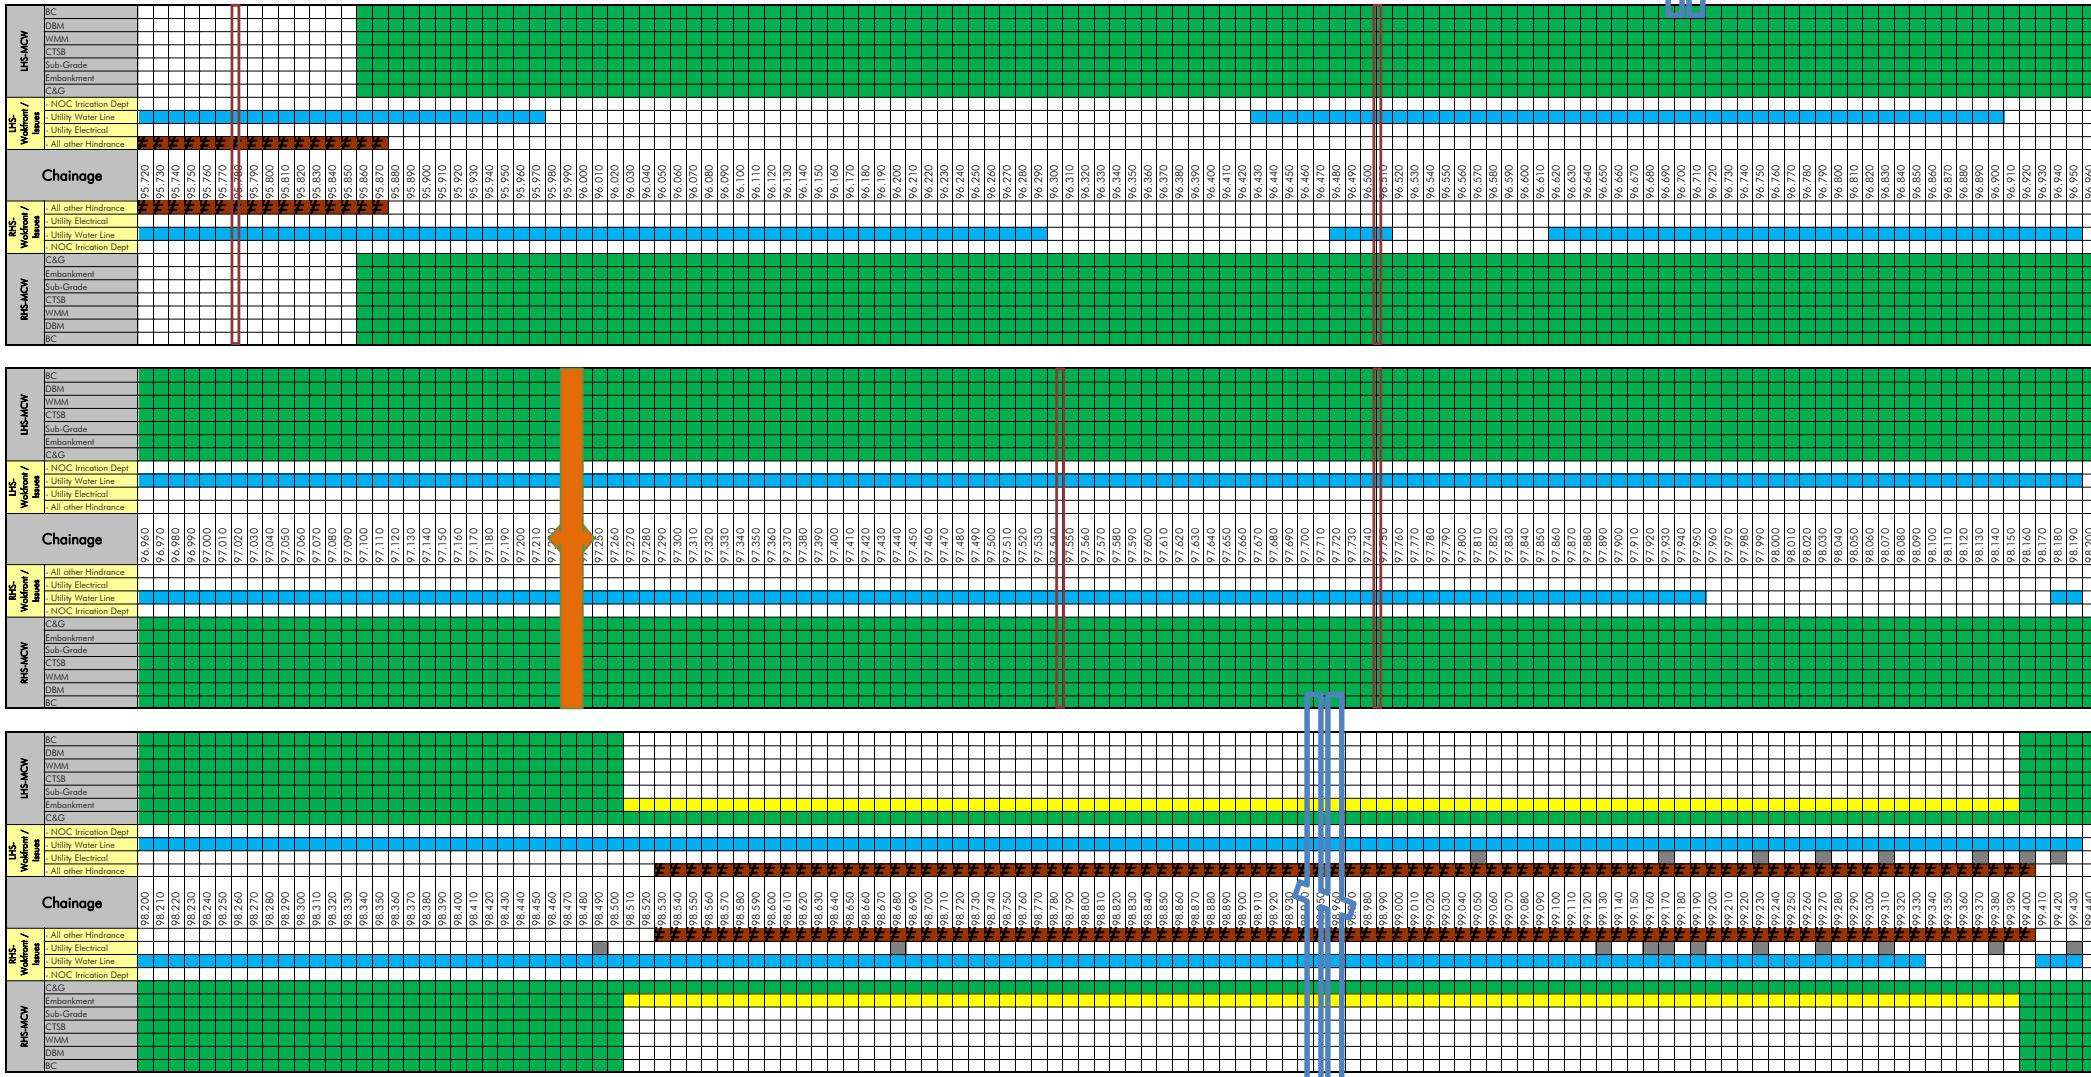

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

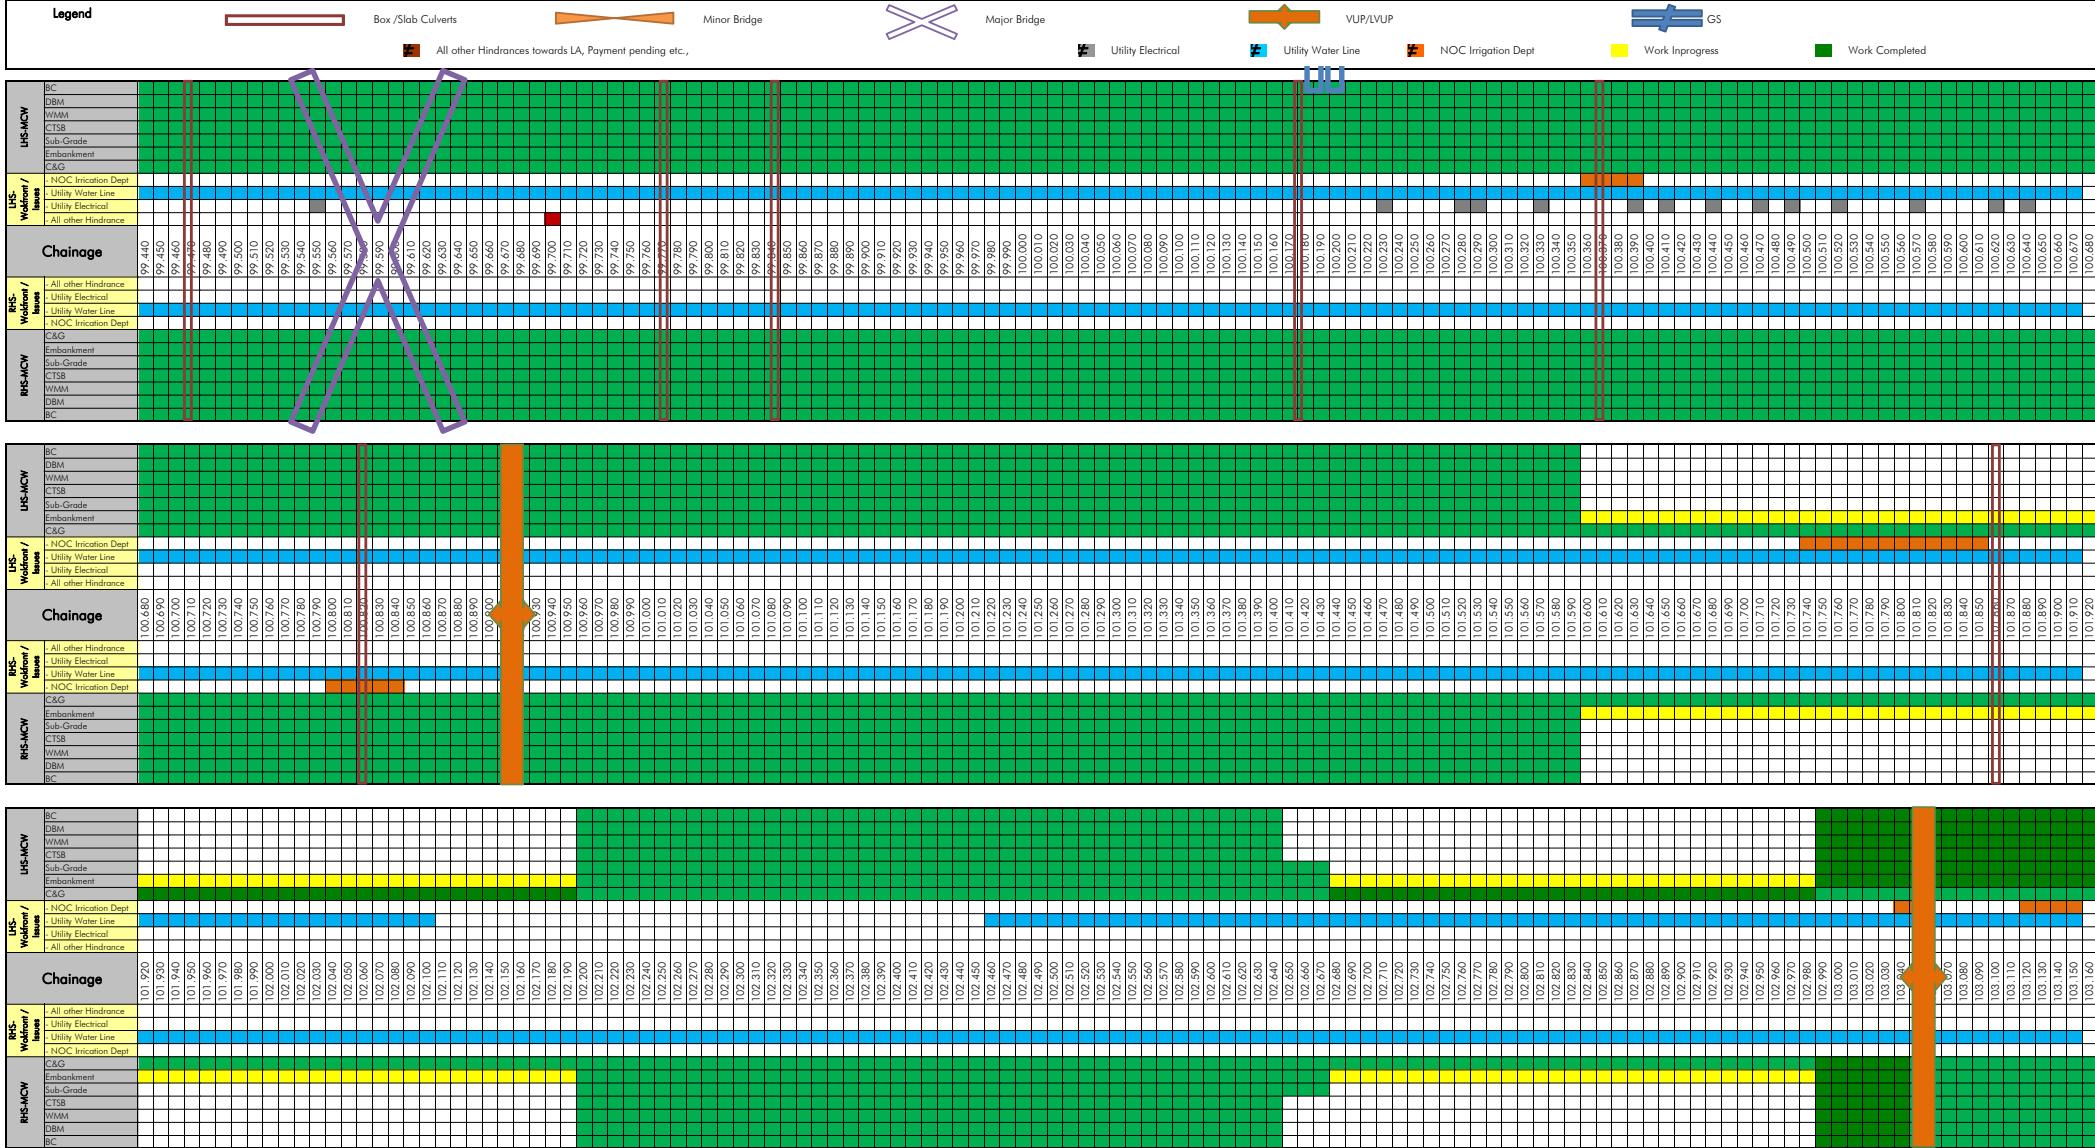


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

Sethiyahopu - Cholapuram Road Project


Strip Plan for MCW as on 31.08.2023

Legend

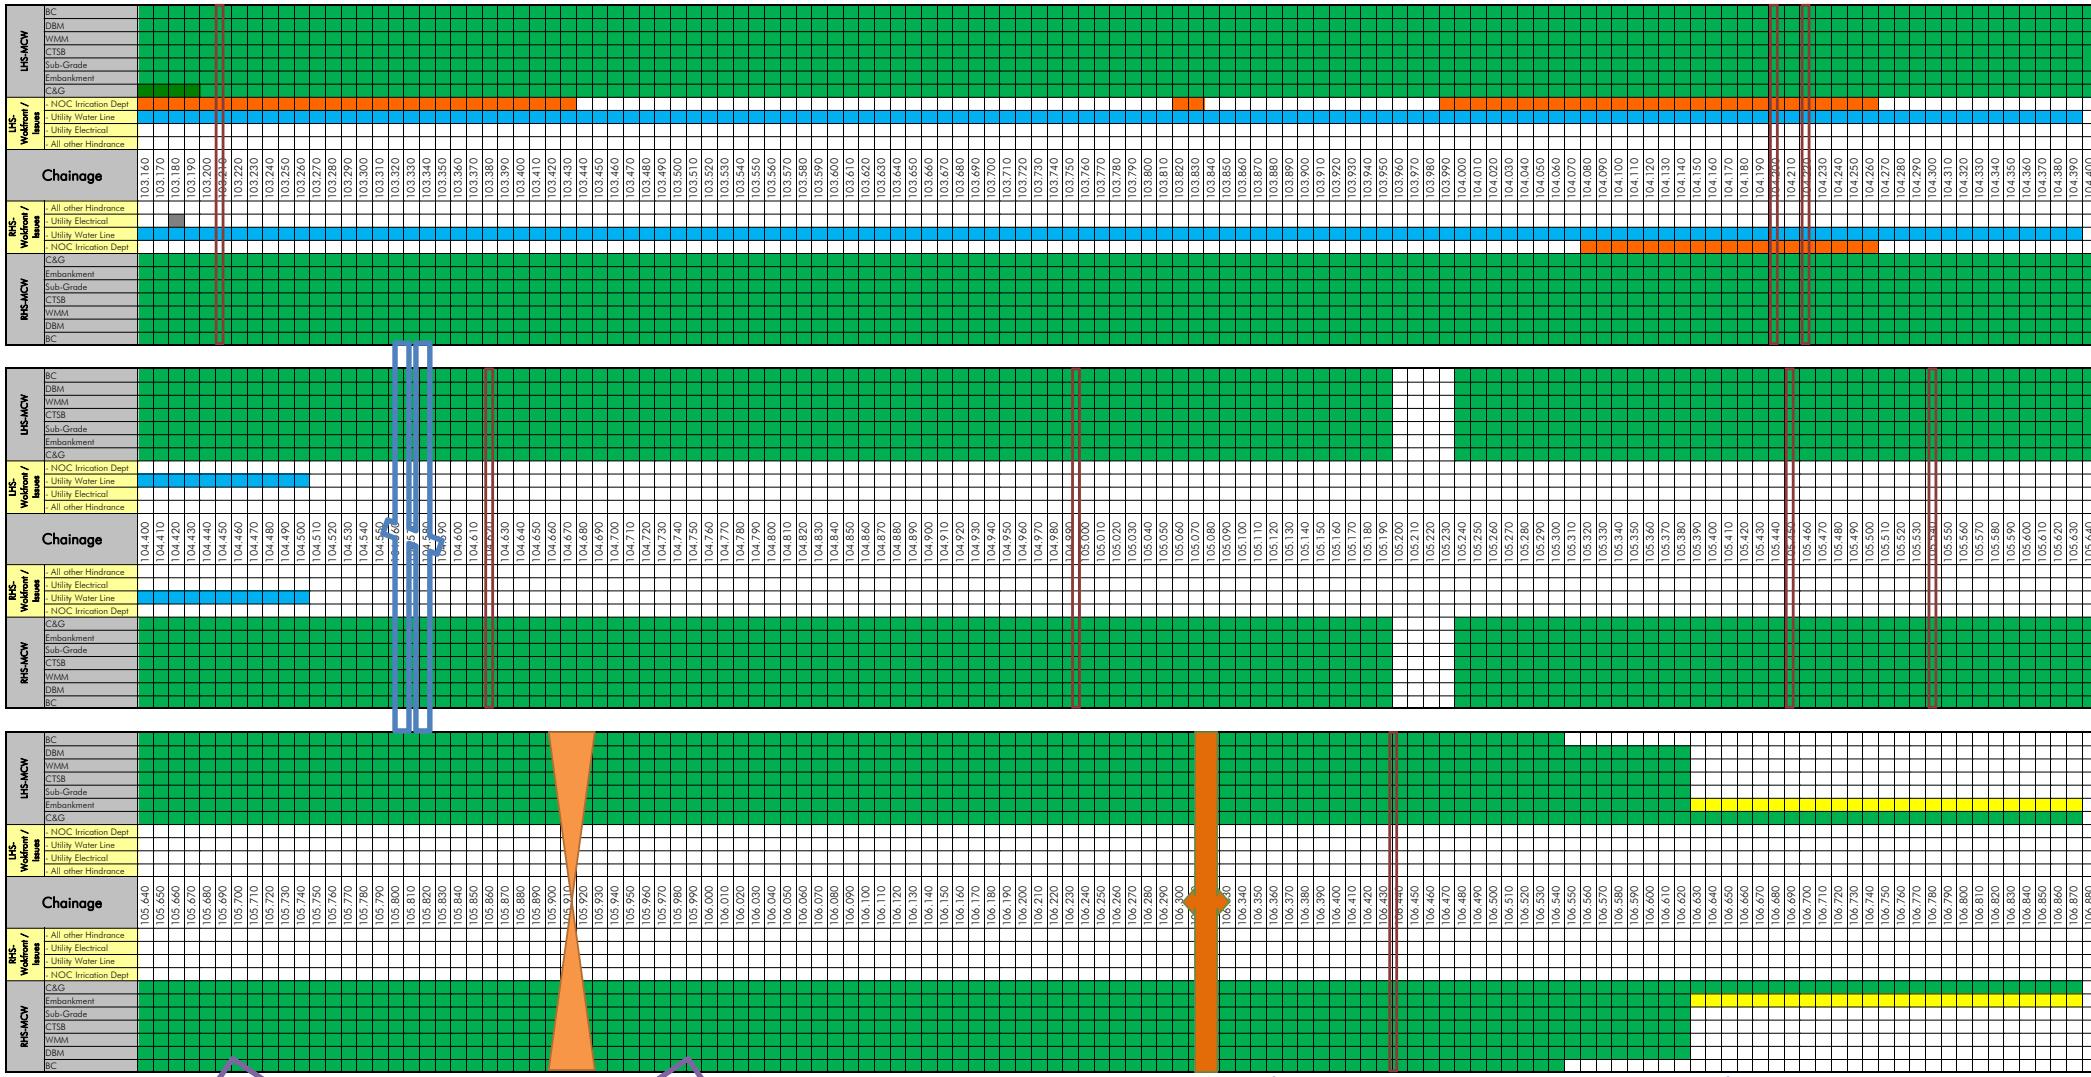

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDPL Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

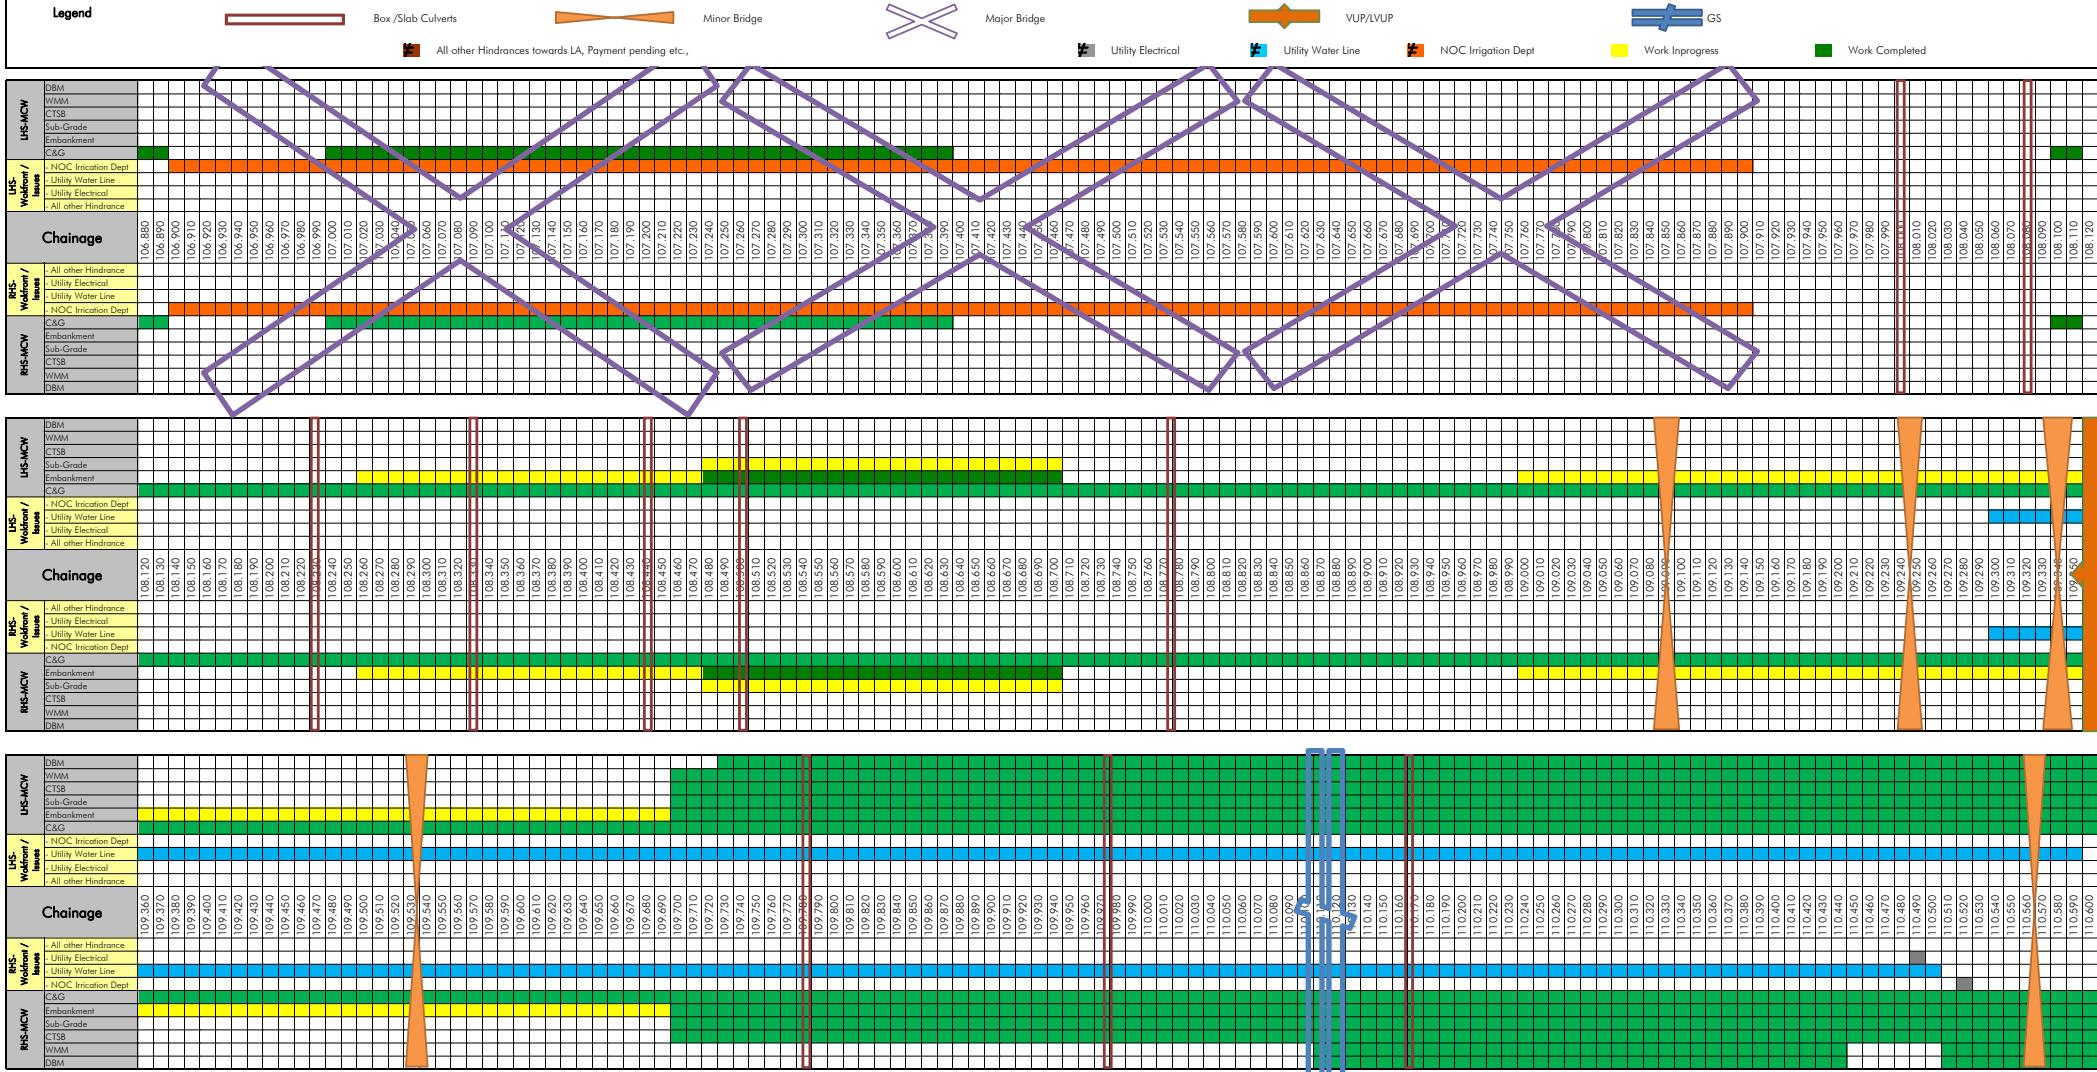


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.


Sethiyahopu - Cholapuram Road Project

Strip Plan for MCW as on 31.08.2023

Legend

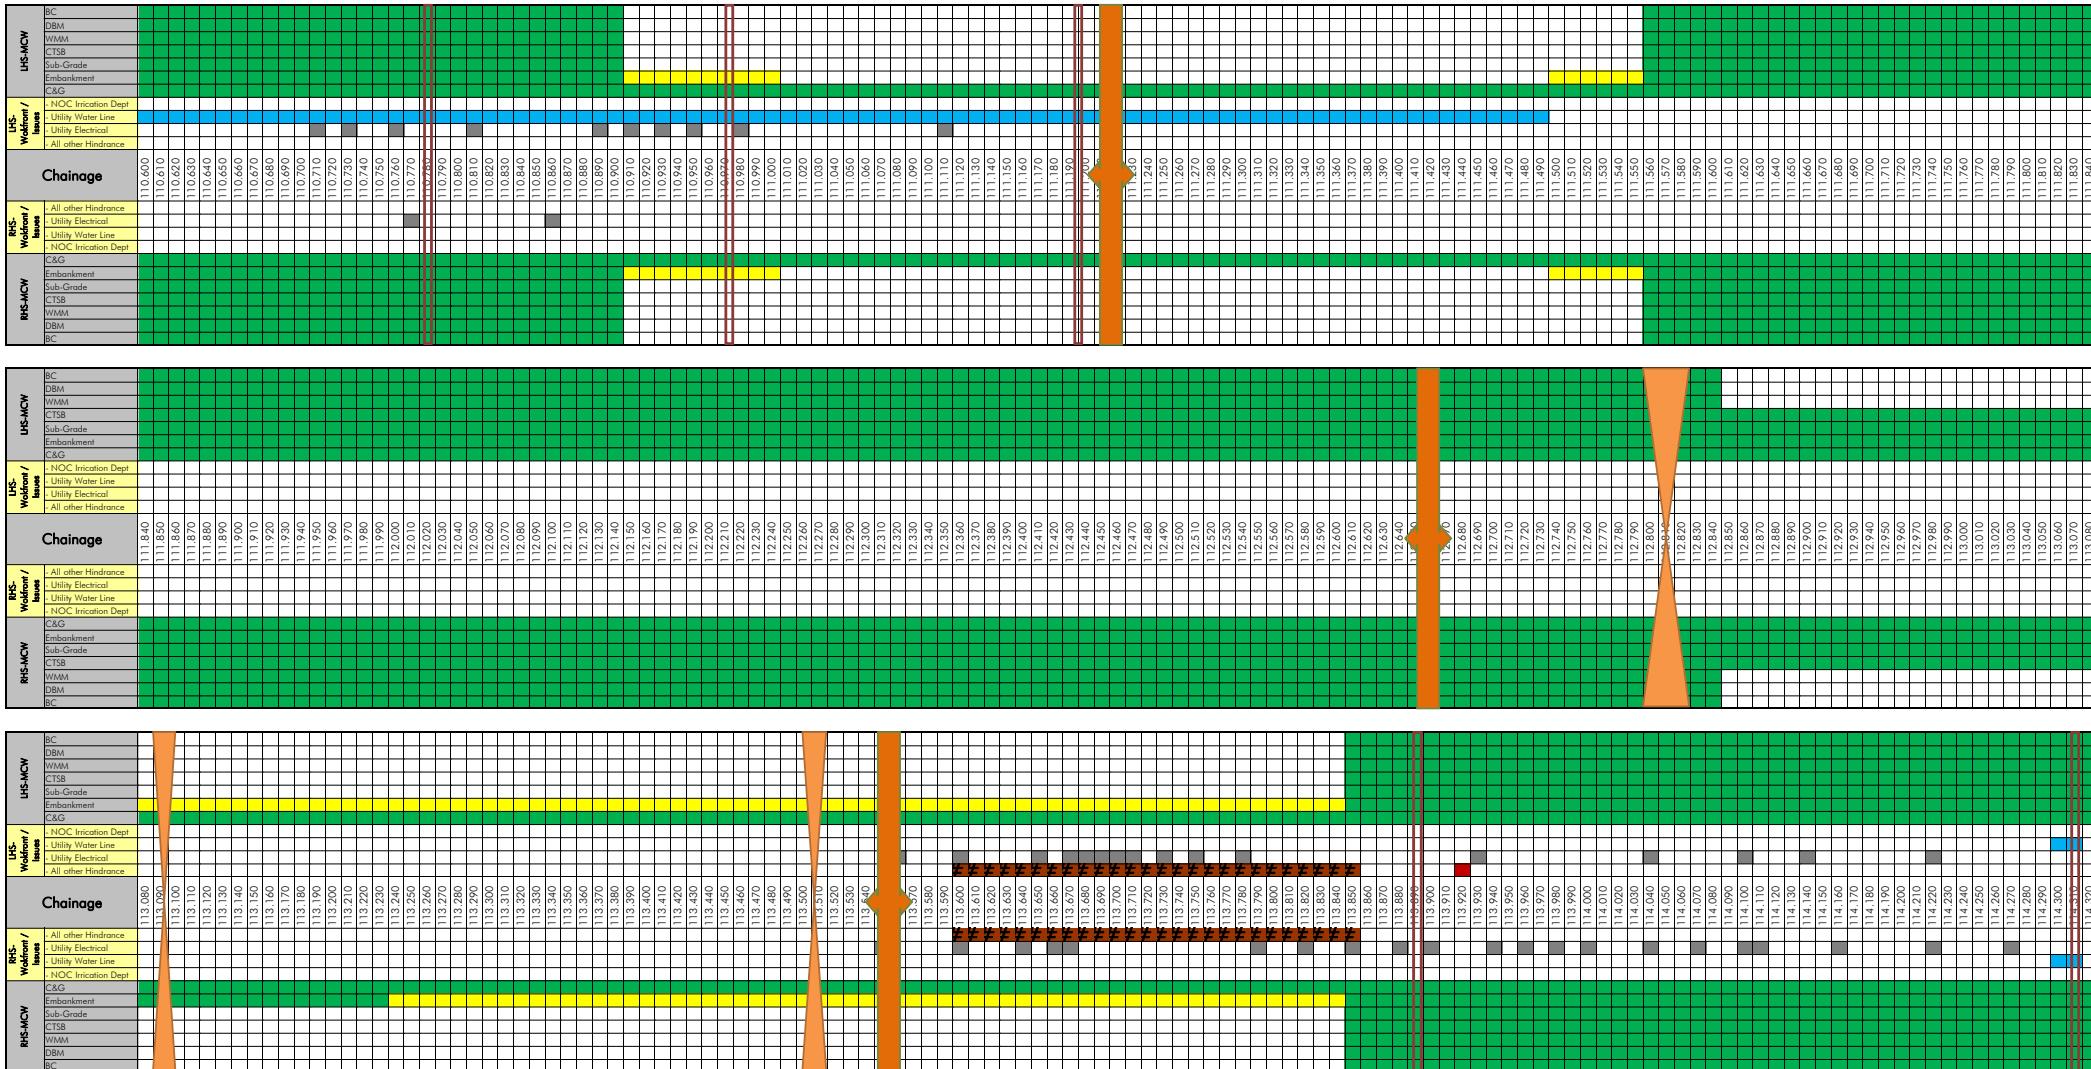


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

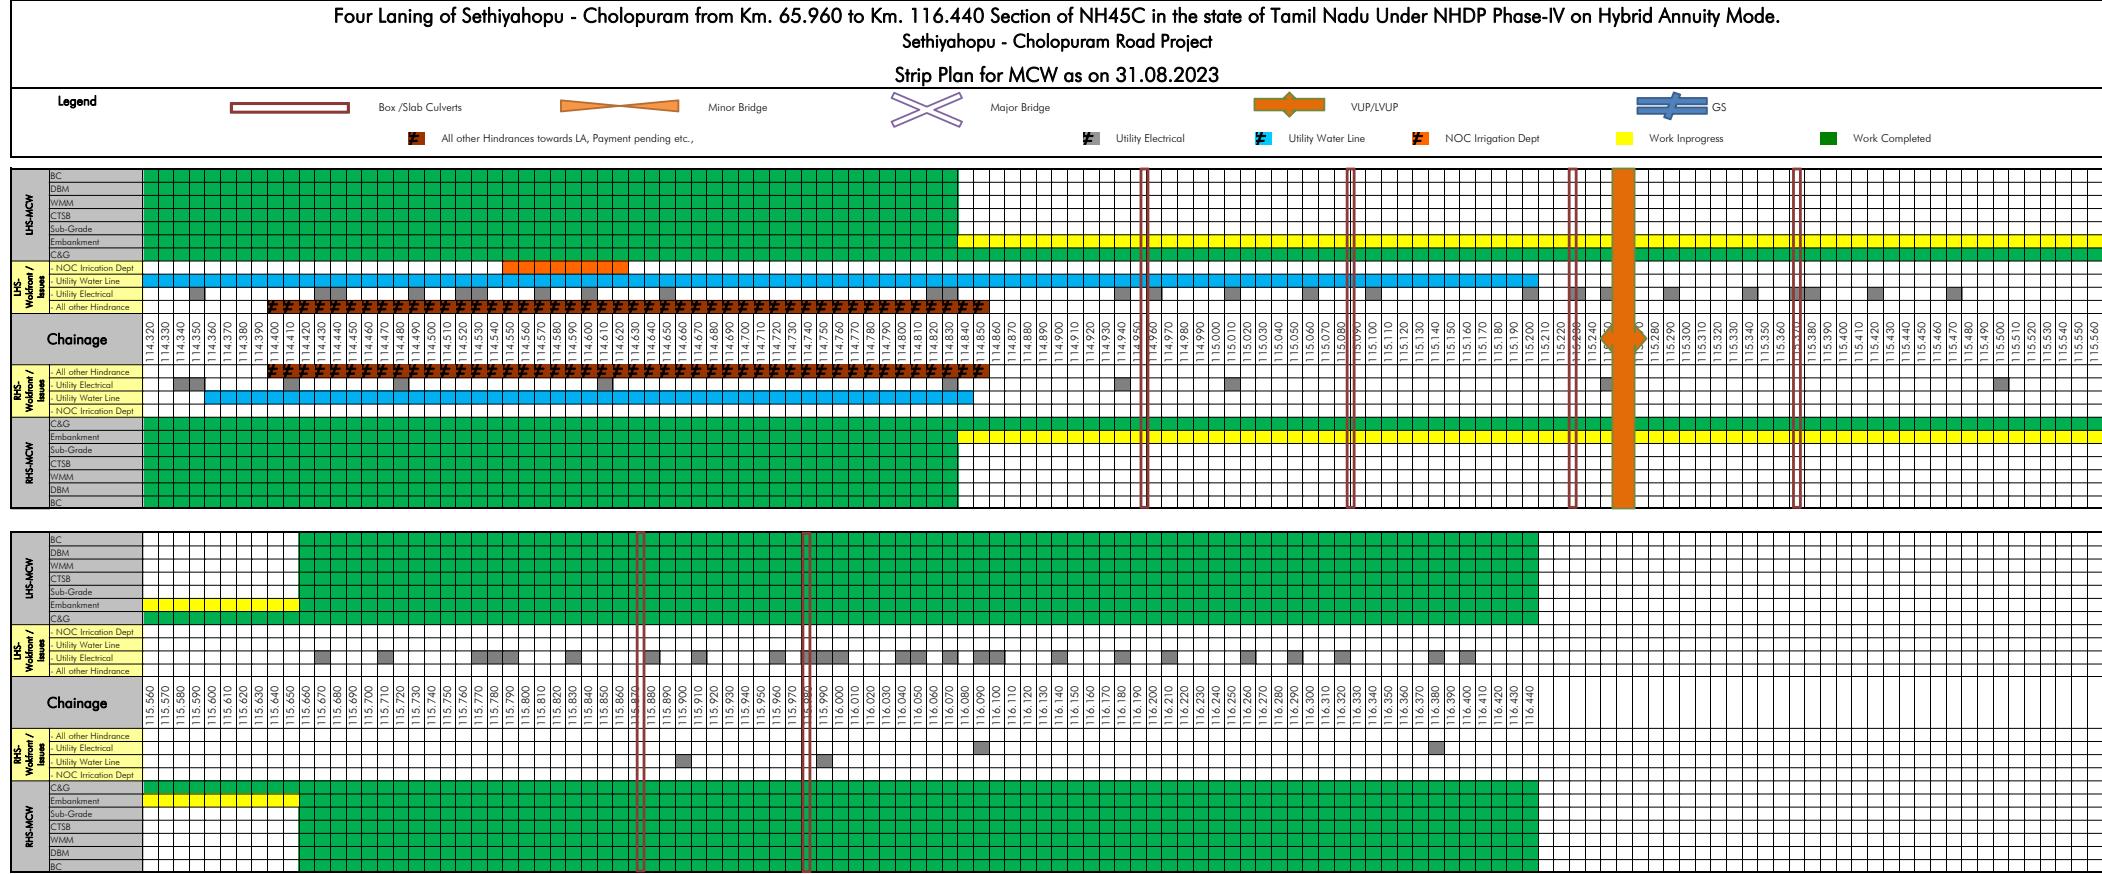


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

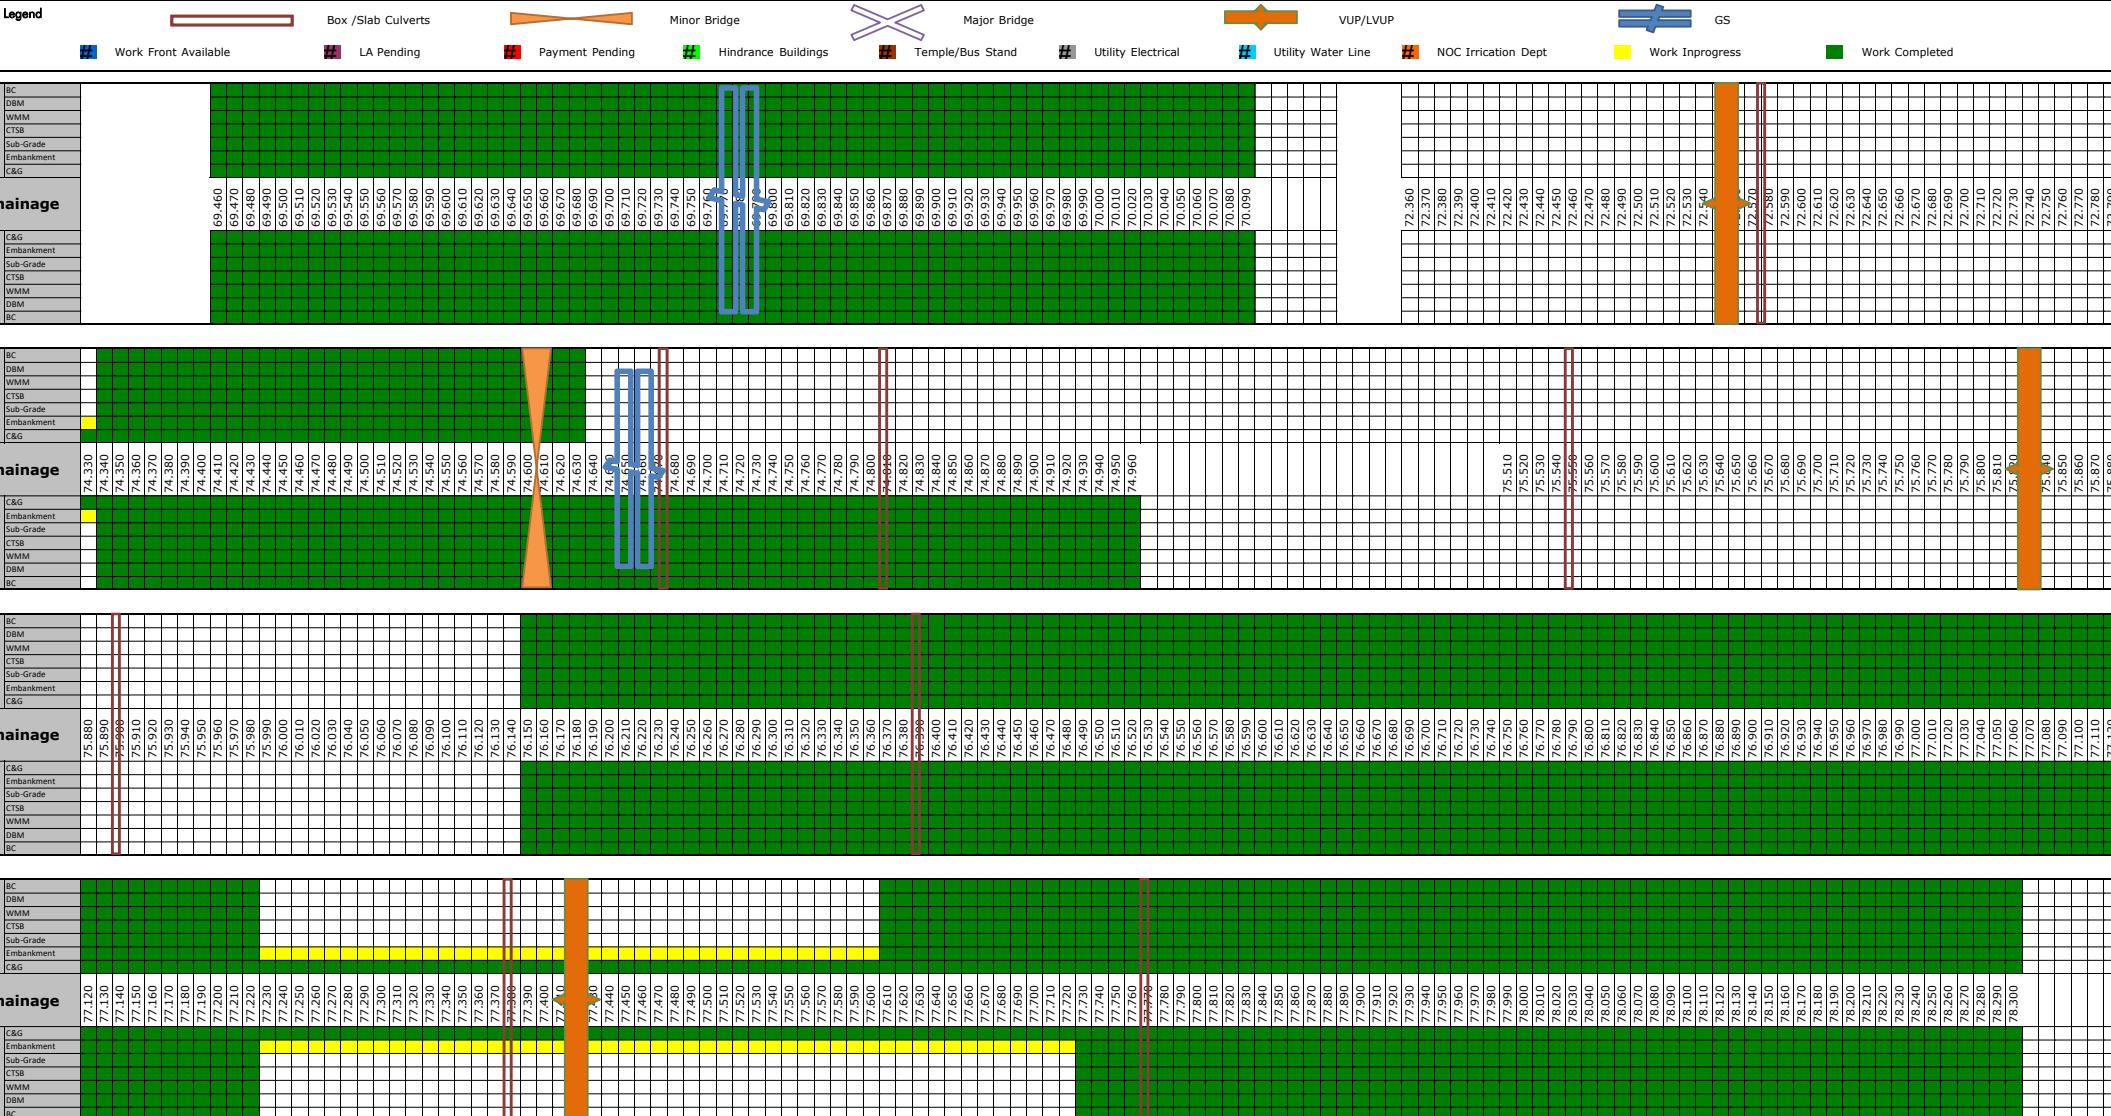


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

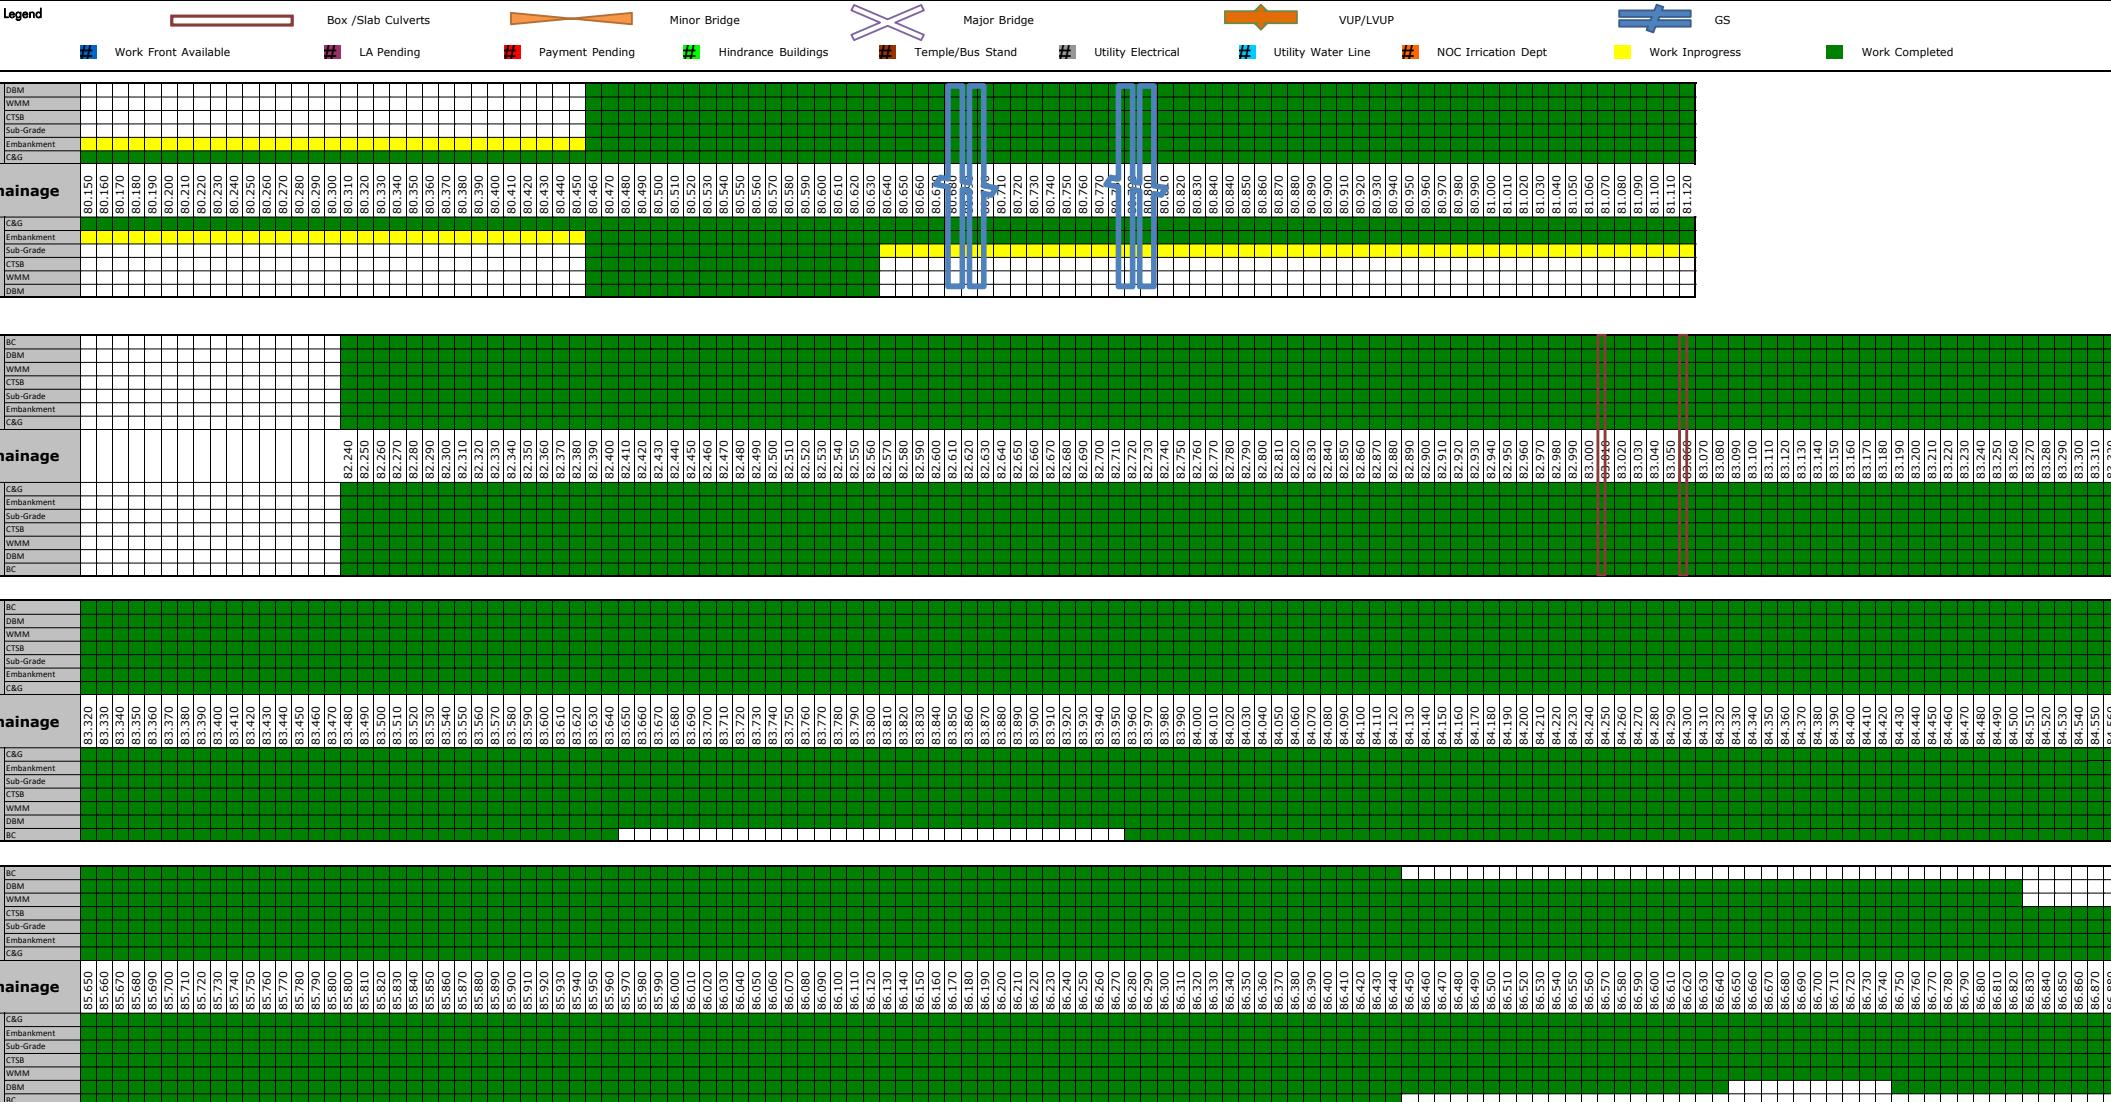


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

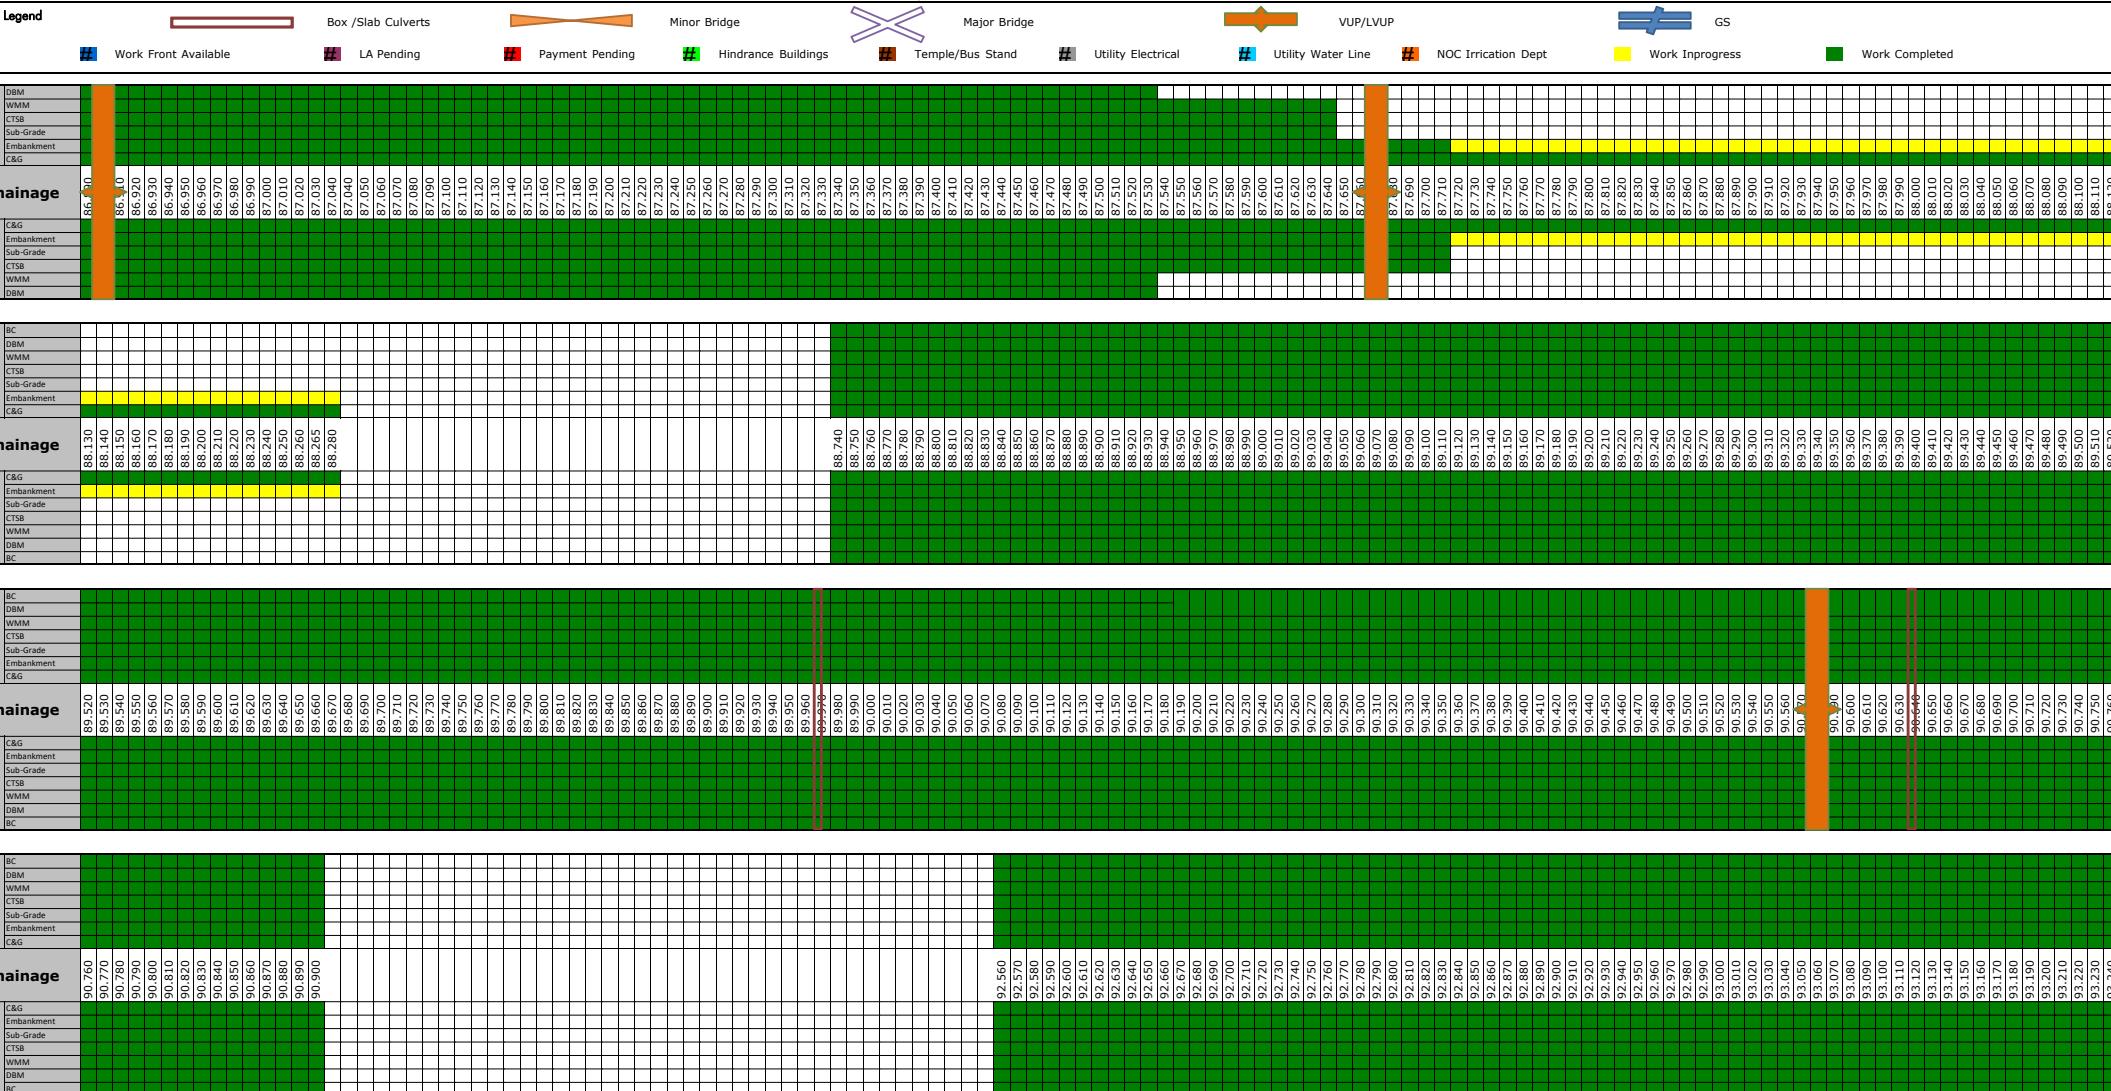


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

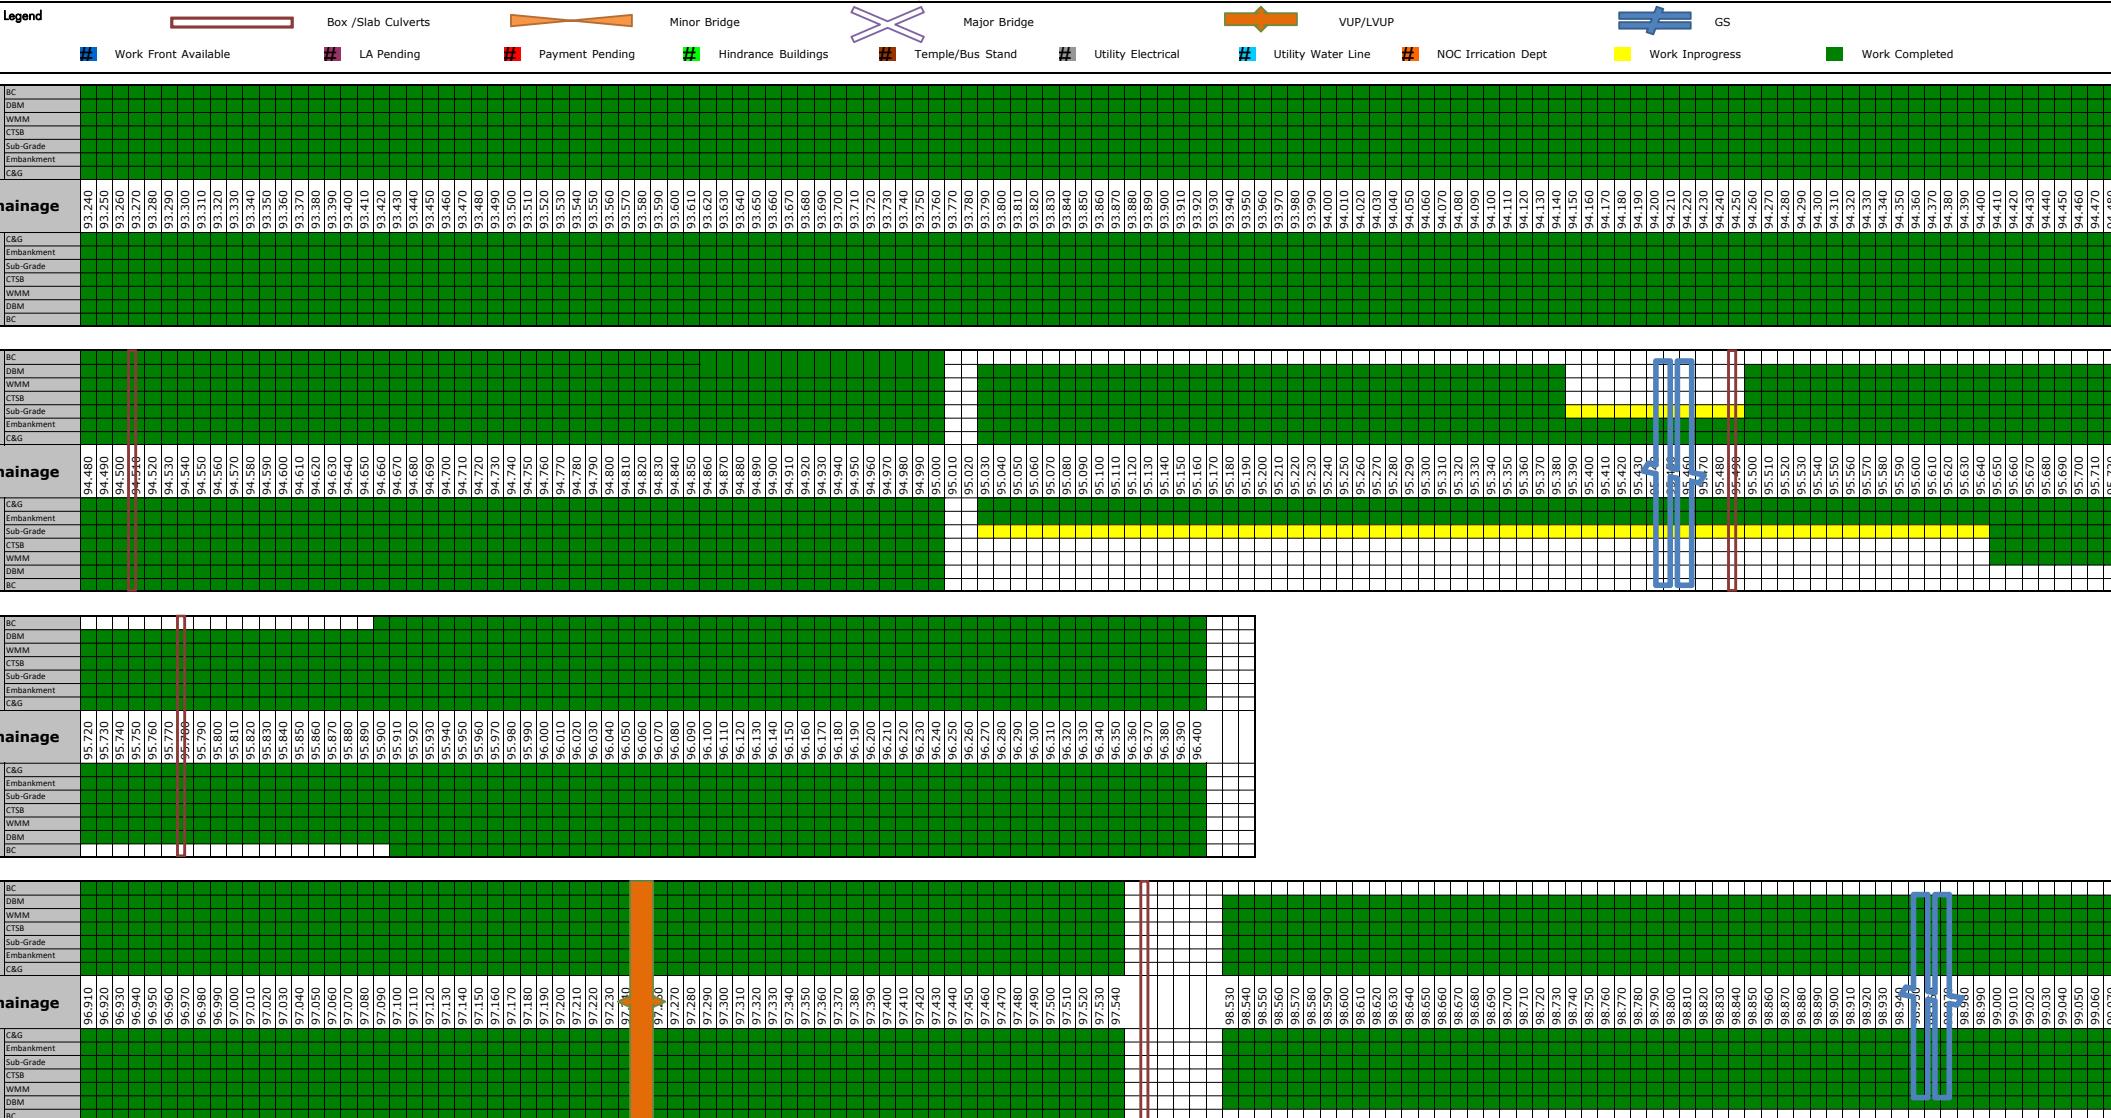


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

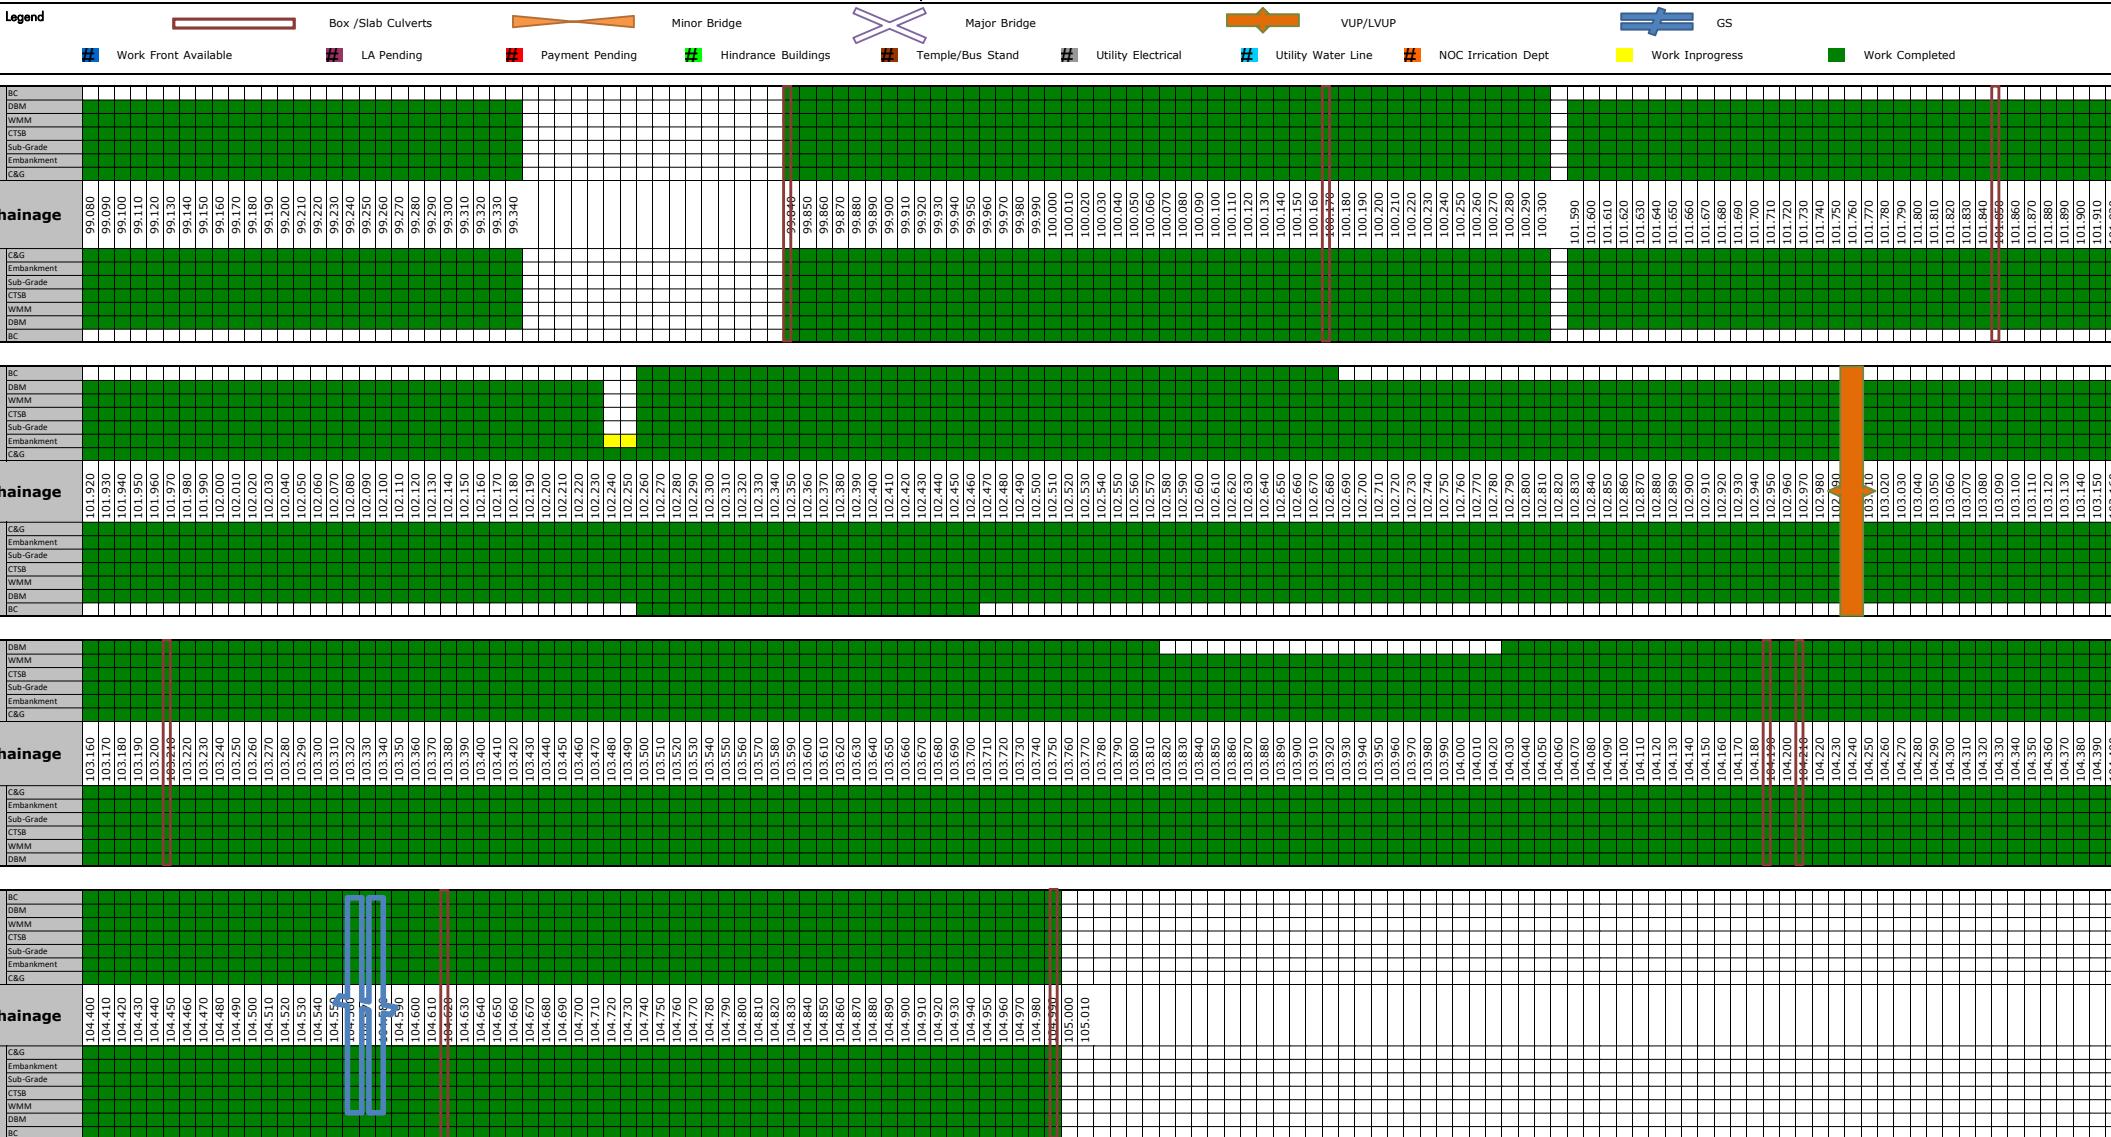

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to Km. 116.440 Section of NH45C in the state of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.
Sethiyahopu - Cholapuram Road Project

Strip Plan for SR as on 31.08.2023

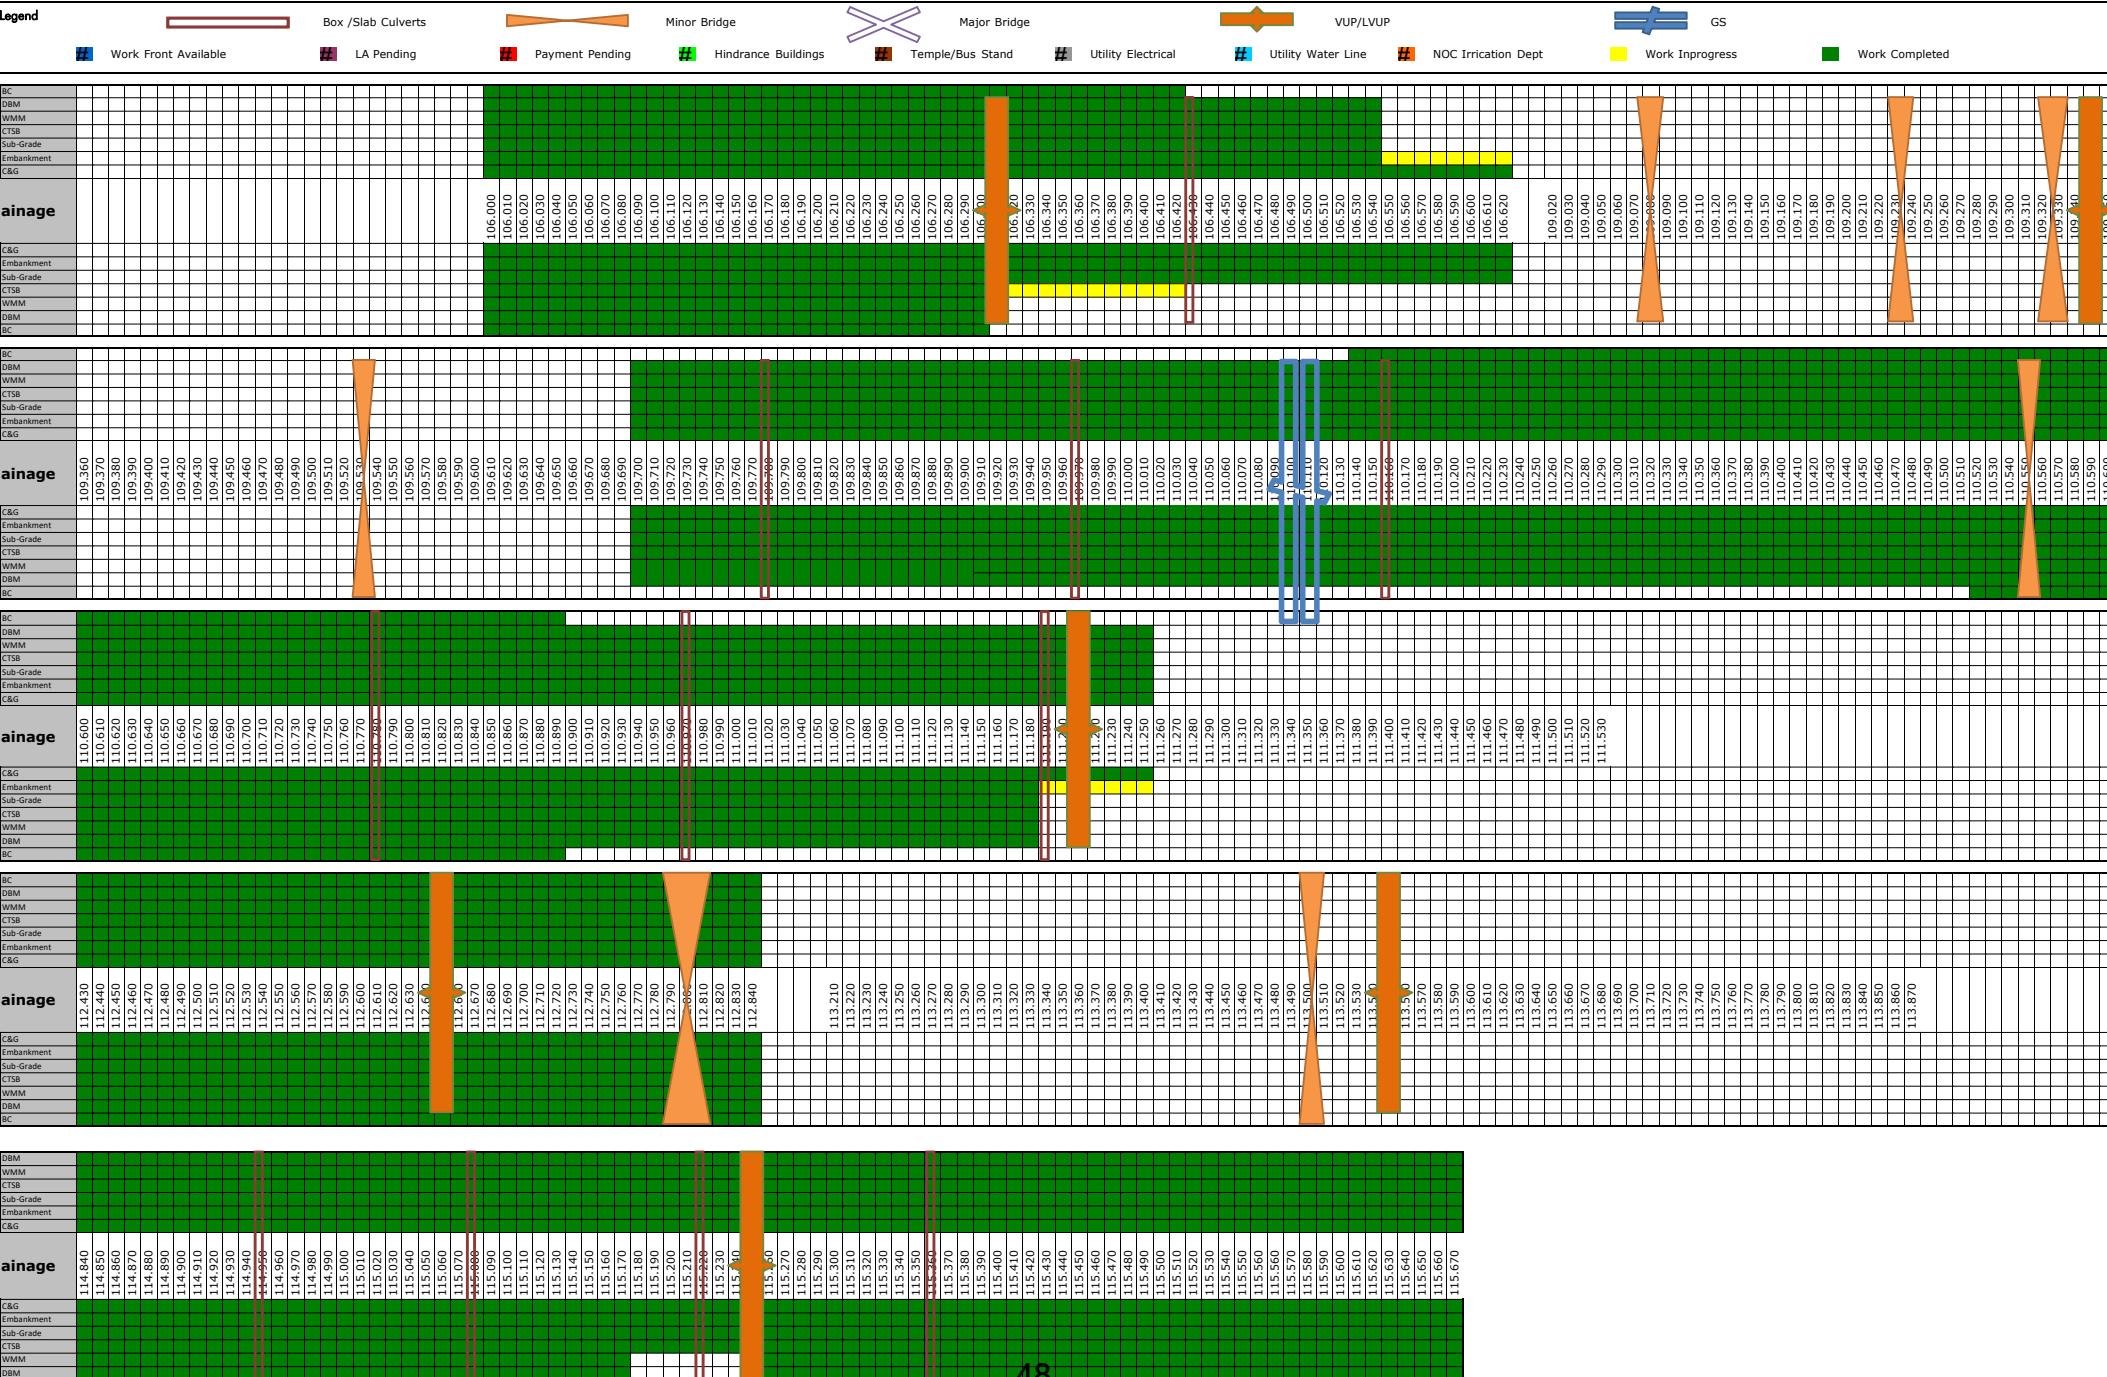

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF BOX CULVERTS ON EXISTING ROAD - MCW | | | | | | | Completed | | | | | | In Progress | | | | | | | | | |
|--|-------------------|---------------------------|----------|--------------------------------|-------------------------|-------------------|-----------------|---------------|------|------|------|-----|------------------|------------|------------|------------------|-----|------|------|------|---------------|-----------------|
| Status Upto | 31.08.2023 | | | | | | LHS | | | | | | RHS | | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | | Number and Length of Spans (m) | Remarks | Type of Structure | Protection Work | Fly wing wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Fly wing wall | Protection Work |
| 1 | 74+675 | 74.670 | EXISTING | 1 x 3.0m x 2.0m | New Construction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 2 | 74+800 | 74.808 | EXISTING | 1 x 1.20m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 3 | 75+558 | 75.555 | EXISTING | 1x3.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 4 | 75+902 | 75.897 | EXISTING | 1 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 5 | 76+390 | 76.387 | EXISTING | 1 x 3.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 6 | 77+382 | 77.379 | EXISTING | 1 x 4.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 7 | 77+767 | 77.764 | EXISTING | 1 x 2.0m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 8 | 81+868 | 81.867 | EXISTING | 1 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 9 | 81+913 | 81.910 | EXISTING | 1 x 1.95m x 1.0m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 10 | 83+012 | 83.007 | EXISTING | 2 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 11 | 83+065 | 83.062 | EXISTING | 1 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 12 | 89+973 | 89.969 | EXISTING | 4 x 0.75m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 13 | 90+640 | 90.637 | EXISTING | 1 x 1.20m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 14 | 94+509 | 94.509 | EXISTING | 1 x 3.6m x 1.6m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 15 | 95+495 | 95.490 | EXISTING | 1 x 1.2m x 0.9m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 16 | 95+794 | 95.787 | EXISTING | 1 x 1.20m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 17 | 96+511 | 96.505 | EXISTING | 1 x 5.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 18 | 97+530 | 97.534 | EXISTING | 1x2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 19 | 97+742 | 97.738 | EXISTING | 1 x 3.0m x 1.0m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 20 | 99+471 | 99.467 | EXISTING | 1 x 3.0m x 4.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 21 | 99+776 | 99.769 | EXISTING | 1 x 2.0m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 22 | 99+840 | 99.838 | EXISTING | 1 x 1.5m x 1.5m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 23 | 100+177 | 100.173 | EXISTING | 1 x 1m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 24 | 100+364 | 100.358 | EXISTING | 1 x 10m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 25 | 100+823 | 100.817 | EXISTING | 1 x 3.5m x 2.5m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 26 | 101+851 | 101.851 | EXISTING | 1 x 1.5m x 1.5m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 27 | 103+220 | 103.214 | EXISTING | 1 x 4.0m x 2.5m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 28 | 104+197 | 104.190 | EXISTING | 1 x 1.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 29 | 104+215 | 104.208 | EXISTING | 1 x 1.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 30 | 109+786 | 109.779 | EXISTING | 1 x 1.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 31 | 109+975 | 109.967 | EXISTING | 1 x 2.0m x 1.7m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 32 | 110+167 | 110.160 | EXISTING | 2 x 1.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 33 | 110+795 | 110.795 | EXISTING | 1 x 1.2m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 34 | 110+980 | 110.971 | EXISTING | 1 x 1.5m x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 35 | 113+897 | 113.885 | EXISTING | 1 x 1.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 36 | 114+313 | 114.300 | EXISTING | 1 x 1.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 37 | 114+954 | 114.952 | EXISTING | 1 x 1.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 38 | 115+097 | 115.087 | EXISTING | 2 x 1.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 39 | 115+232 | 115.221 | EXISTING | 1 x 2.0m x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 40 | 115+381 | 115.368 | EXISTING | 1 x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 41 | 115+884 | 115.872 | EXISTING | 2 x 1.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 42 | 115+978 | 115.978 | EXISTING | 1 x 2.0m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLPURAM PROJECT - STATUS OF BOX CULVERTS ON EXISTING ROAD - SERVICE ROAD | | | | | | | Completed | | | | | In Progress | | | | | | | | | | |
|--|-------------------|---------------------------|----------|--------------------------------|-------------------------|-------------------|-----------------|---------------|------|------|------|-------------|------------------|------------|------------|------------------|-----|------|------|------|---------------|-----------------|
| Status Upto | 31.08.2023 | | | | | | LHS | | | | | RHS | | | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | | Number and Length of Spans (m) | Remarks | Type of Structure | Protection Work | Fly wing wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Fly wing wall | Protection Work |
| 1 | 74+675 | 74.670 | EXISTING | 1 x 3.0m x 2.0m | New Construction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 2 | 74+800 | 74.808 | EXISTING | 1 x 1.20m | Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 3 | 75+558 | 75.555 | EXISTING | 1x3.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 4 | 75+902 | 75.897 | EXISTING | 1 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 5 | 76+390 | 76.387 | EXISTING | 1 x 3.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 6 | 77+382 | 77.379 | EXISTING | 1 x 4.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 7 | 77+767 | 77.764 | EXISTING | 1 x 2.0m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 8 | 83+012 | 83.007 | EXISTING | 2 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 9 | 83+065 | 83.062 | EXISTING | 1 x 2.0m x 2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 10 | 89+973 | 89.969 | EXISTING | 4 x 0.75m | Widening | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 11 | 90+640 | 90.637 | EXISTING | 1 x 1.20m | Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 12 | 94+509 | 94.509 | EXISTING | 1 x 3.6m x 1.6m | Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 13 | 95+495 | 95.490 | EXISTING | 1 x 1.2m x 0.9m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 14 | 95+794 | 95.787 | EXISTING | 1 x 1.20m | Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 15 | 96+511 | 96.505 | EXISTING | 1 x 5.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 16 | 97+530 | 97.534 | EXISTING | 1x2.0m | Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 17 | 99+776 | 99.769 | EXISTING | 1 x 2.0m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 18 | 99+840 | 99.838 | EXISTING | 1 x 1.5m x 1.5m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 19 | 100+177 | 100.173 | EXISTING | 1 x 1m | Repair & Widening | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 20 | 100+364 | 100.358 | EXISTING | 1 x 10m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 21 | 101+851 | 101.851 | EXISTING | 1 x 1.5m x 1.5m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 22 | 103+220 | 103.214 | EXISTING | 1 x 4.0m x 2.5m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 23 | 104+197 | 104.190 | EXISTING | 1 x 1.0m | Repair & Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 24 | 104+215 | 104.208 | EXISTING | 1 x 1.0m | Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 25 | 109+786 | 109.779 | EXISTING | 1 x 1.0m | Repair & Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 26 | 109+975 | 109.967 | EXISTING | 1 x 2.0m x 1.7m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 27 | 110+167 | 110.160 | EXISTING | 2 x 1.0m | Repair & Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 28 | 110+795 | 110.785 | EXISTING | 1 x 1.2m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |
| 29 | 110+980 | 110.971 | EXISTING | 1 x 1.5m x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 30 | 113+897 | 113.885 | EXISTING | 1 x 1.0m | Repair & Widening | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 31 | 114+313 | 114.300 | EXISTING | 1 x 1.0m | Repair & Widening | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 32 | 114+954 | 114.952 | EXISTING | 1 x 1.0m | Repair & Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 33 | 115+097 | 115.087 | EXISTING | 2 x 1.0m | Repair & Reconstruction | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 34 | 115+232 | 115.221 | EXISTING | 1 x 2.0m x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 35 | 115+381 | 115.368 | EXISTING | 1 x 2.0m | Repair & Reconstruction | BOX CULVERT | | | | | | | | | | | | | | | | |
| 36 | 115+884 | 115.872 | EXISTING | 2 x 1.0m | Repair & Widening | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 37 | 115+978 | 115.978 | EXISTING | 1 x 2.0m x 2.0m | Repair & Widening | BOX CULVERT | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF BOX CULVERTS ON BYPASS - MCW | | | | | Completed | | | | | | In Progress | | | | | | | | | | |
|--|----------------------|---------------------------------|--------|--------------------------------------|-------------------|--------------------|---------------|------|------|------|-------------|---------------------|------------|------------|---------------------|-----|------|------|------|---------------|--------------------|
| Status Upto | 31.08.2023 | | | | LHS | | | | | | | RHS | | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | | Number and Length of Spans (m) | Type of Structure | Protection Work | Fly wing wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Fly wing wall | Protection Work |
| 1 | 66+357 | 66.383 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 2 | 67+068 | 67.068 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 3 | 69+357 | 69.357 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 4 | 72+570 | 72.578 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 5 | 73+755 | 73.755 | BYPASS | 1x1.2.0mx2.0m | PIPE CULVERT | | | | | | | | | | | | | | | | |
| 6 | 104+622 | 104.618 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 7 | 104+998 | 104.992 | BYPASS | 1 x 4.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 8 | 105+440 | 105.440 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 9 | 105+536 | 105.525 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 10 | 106+442 | 106.432 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 11 | 108+002 | 107.994 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 12 | 108+080 | 108.070 | BYPASS | 1 x 4.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 13 | 108+225 | 108.225 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 14 | 108+345 | 108.334 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 15 | 108+441 | 108.441 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 16 | 108+540 | 108.500 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 17 | 108+767 | 108.767 | BYPASS | 1 x 4.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 18 | 111+205 | 111.196 | BYPASS | 1 x 1.0m | PIPE CULVERT | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF BOX CULVERTS ON BYPASS - SERVICE ROAD | | | | | Completed | | | | | | In Progress | | | | | | | | | | |
|---|----------------------|---------------------------------|--------|--------------------------------------|-------------------|--------------------|---------------|------|------|------|-------------|---------------------|------------|------------|---------------------|-----|------|------|------|---------------|--------------------|
| Status Upto | 31.08.2023 | LHS | | | | | | RHS | | | | | | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | | Number and Length of Spans (m) | Type of Structure | Protection Work | Fly wing wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Fly wing wall | Protection Work |
| 1 | 72+570 | 72.578 | BYPASS | 1 x 3.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 2 | 104+622 | 104.618 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 3 | 104+998 | 104.992 | BYPASS | 1 x 4.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 4 | 106+442 | 106.432 | BYPASS | 1 x 2.0m x 2.0m | BOX CULVERT | | | | | | | | | | | | | | | | |
| 5 | 111+205 | 111.196 | BYPASS | 1 x 1.0m | PIPE CULVERT | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF MNB-BOX TYPE - MCW | | | | | | Completed | | | | | | In Progress | | | | | | | | | |
|---|-------------------|---------------------------|--------------------------------|-------------------|-----------|-----------------|----------------|------|------|------|-----|------------------|------------|------------|------------------|-----|------|------|------|----------------|-----------------|
| Status Upto | 31.08.2023 | | | | | LHS | | | | | | RHS | | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | Number and Length of Spans (m) | Type of Structure | | Protection Work | Retaining wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Retaining wall | Protection Work |
| 1 | 79+716 | 79.715 | 1 x 12.50m | MNBB | Widening | | | | | | | | | | | | | | | | |
| 2 | 79+795 | 79.795 | 2 x 12.50m | MNBB | Re-Const. | | | | | | | | | | | | | | | | |
| 3 | 82+007 | 82.006 | 2 x 12.50m | MNBB | Widening | | | | | | | | | | | | | | | | |
| 4 | 85+144 | 85.144 | 2 x 12.50m | MNBB | Re-Const. | | | | | | | | | | | | | | | | |
| 5 | 85+435 | 85.432 | 1 x 12.50m | MNBB | Widening | | | | | | | | | | | | | | | | |
| 6 | 88+513 | 88.513 | 1 x 12.50m | MNBB | Widening | | | | | | | | | | | | | | | | |
| 7 | 91+164 | 91.165 | 2 x 12.50m | MNBB | Re-Const. | | | | | | | | | | | | | | | | |
| 8 | 92+343 | 92.342 | 1 x 12.50m | MNBB | Widening | | | | | | | | | | | | | | | | |
| 9 | 101+101 | 101.100 | | MNBB | EXISTING | | | | | | | | | | | NA | NA | NA | NA | NA | NA |
| 10 | 66+757 | 66.730 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 11 | 68+644 | 68.650 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 12 | 74+173 | 74.175 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 13 | 74+605 | 74.600 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 14 | 105+915 | 105.915 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 15 | 109+090 | 109.088 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 16 | 109+195 | 109.208 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 17 | 109+365 | 109.365 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 18 | 109+540 | 109.540 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 19 | 111+563 | 111.565 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 20 | 112+807 | 112.807 | 1 x 25m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 21 | 113+100 | 113.100 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | |
| 22 | 113+505 | 113.505 | 2 x 12.5m | MNBB | BYPASS | | Yellow | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF MNB-BOX TYPE - SERVICE ROAD | | | | | | | Completed | | | | | | | In Progress | | | | | | | | |
|--|-------------------|---------------------------|--------------------------------|-------------------|--------|-----------------|----------------|------|------|------|-----|------------------|------------|-------------|------------|------------------|-----|------|------|------|----------------|-----------------|
| Status Upto | 31.08.2023 | | | | | | LHS | | | | | | | RHS | | | | | | | | |
| Sr. No. | As Approved by IE | Design Chainage As per CA | Number and Length of Spans (m) | Type of Structure | | Protection Work | Retaining wall | Slab | Wall | Raft | PCC | Granular Filling | Excavation | | Excavation | Granular Filling | PCC | Raft | Wall | Slab | Retaining wall | Protection Work |
| 1 | 74+605 | 74.600 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 2 | 105+915 | 105.915 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 3 | 109+090 | 109.088 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 4 | 109+195 | 109.208 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 5 | 109+365 | 109.365 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 6 | 109+540 | 109.540 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 7 | 111+563 | 111.565 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 8 | 112+807 | 112.807 | 1 x 25m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 9 | 113+100 | 113.100 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |
| 10 | 113+505 | 113.505 | 2 x 12.5m | MNBB | BYPASS | | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF LVUP & PUP | | | | | Completed | | | | In Progress | | | | | | | |
|---|-------------------|--------------------------------|-------------------|----------|-----------------|-------|--------|-------|-------------|------------|------------|-------|-------|-------|-------|-----------------|
| Status Upto | 31.08.2023 | LHS | | | | RHS | | | | | | | | | | |
| Sr. No. | As Approved by IE | Number and Length of Spans (m) | Type of Structure | | Protection Work | Slab | Wall | Raft | PCC | Excavation | Excavation | PCC | Raft | Wall | Slab | Protection Work |
| 1 | 77+420 | 1 X 10.5 | LVUP | EXISTING | | | Yellow | | | | | | | | | |
| 2 | 112+643 | 1 X 10.5 | LVUP | BYPASS | Green | Green | Green | Green | Green | Green | Green | Green | Green | Green | Green | Green |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF MNB - GIRDER TYPE | | | | | Completed | | | | | | In Progress | | | | | | | | | | | |
|--|-----------------|--------|----------|----|---------------|------|------------------|----------------|-----------------|----------|-----------------|-----|------------|------------|-----|-----------------|----------|-----------------|----------------|------------------|------|---------------|
| Status upto | 31.08.2023 | | | | LHS | | | | | | RHS | | | | | | | | | | | |
| Sr. No. | MNB at Chainage | Span | | | Crash Barrier | Slab | Girder Launching | Girder Casting | Piercap /Abicap | Pier/Abt | Open Foundation | PCC | Excavation | Excavation | PCC | Open Foundation | Pier/Abt | Piercap /Abicap | Girder Casting | Girder Launching | Slab | Crash Barrier |
| 1 | 70+185 | 2 x 20 | BYPASS | A1 | | | | | | | | | | | | | | | | | | |
| | | | | P1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 2 | 73+815 | 1 x 15 | BYPASS | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 3 | 84+725 | 1 x 15 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 4 | 84+987 | 2 x 15 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | P1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF MJB | | | | | | | | | Completed | | |
|--|---------------|------|------------------|---------------------|------------------|----------|----------|------|-------------|----------|---------------------------|
| MJB at Chainage 66+530 (8x30) - BYPASS | | | | | | | | | In Progress | | |
| Status Upto 31.08.2023 | LHS/LSR | | | | | | | | RHS/RSR | | |
| | Crash Barrier | Slab | Girder Launching | Girder Casting Pier | Pier Cap/Abt Cap | Pier/Abt | Pile Cap | Pile | Pile | Pile Cap | Pier/Abt Pier Cap/Abt Cap |
| A1 | | | | | | | | | | | |
| P1 | | | | | | | | | | | |
| P2 | | | | | | | | | | | |
| P3 | | | | | | | | | | | |
| P4 | | | | | | | | | | | |
| P5 | | | | | | | | | | | |
| P6 | | | | | | | | | | | |
| P7 | | | | | | | | | | | |
| A2 | | | | | | | | | | | |
| MJB at Chainage 73+340 (9x30) - BYPASS | | | | | | | | | Completed | | |
| Status Upto 31.08.2023 | LHS/LSR | | | | | | | | RHS/RSR | | |
| | Crash Barrier | Slab | Girder Launching | Girder Casting Pier | Pier Cap/Abt Cap | Pier/Abt | Pile Cap | Pile | Pile | Pile Cap | Pier/Abt Pier Cap/Abt Cap |
| A1 | Yellow | | | | | | | | | | |
| P1 | Yellow | | | | | | | | | | |
| P2 | Yellow | | | | | | | | | | |
| P3 | Yellow | | | | | | | | | | |
| P4 | Yellow | | | | | | | | | | |
| P5 | Yellow | | | | | | | | | | |
| P6 | Yellow | | | | | | | | | | |
| P7 | Yellow | | | | | | | | | | |
| P8 | Yellow | | | | | | | | | | |
| A2 | Yellow | | | | | | | | | | |

| MJB at Chainage 99+583 (3x25) - EXISTING ROAD | | | | | | | | | | | | | | | |
|---|---------------|------|------------------|---------------------|------------------|----------|----------|------|------|----------|---------------------------|----------------|------------------|------|---------------|
| Status Upto 31.08.2023 | LHS/LSR | | | | | RHS/RSR | | | | | | | | | |
| | Crash Barrier | Slab | Girder Launching | Girder Casting Pier | Pier Cap/Abt Cap | Pier/Abt | Pile Cap | Pile | Pile | Pile Cap | Pier/Abt Pier Cap/Abt Cap | Girder Casting | Girder Launching | Slab | Crash Barrier |
| A1 | | | | | | | | | | | | | | | |
| P1 | | | | | | | | | | | | | | | |
| P2 | | | | | | | | | | | | | | | |
| A2 | | | | | | | | | | | | | | | |
| MJB at Chainage 107+400 - BYPASS | | | | | | | | | | | | | | | |
| Status Upto 31.08.2023 | LHS/LSR | | | | | RHS/RSR | | | | | | | | | |
| A1 | | | | | | | | | | | | | | | |
| P1 | | | | | | | | | | | | | | | |
| P2 | | | | | | | | | | | | | | | |
| P3 | | | | | | | | | | | | | | | |
| P4 | | | | | | | | | | | | | | | |
| P5 | | | | | | | | | | | | | | | |
| P6 | | | | | | | | | | | | | | | |
| P7 | | | | | | | | | | | | | | | |
| P8 | | | | | | | | | | | | | | | |
| P9 | | | | | | | | | | | | | | | |
| P10 | | | | | | | | | | | | | | | |
| P11 | | | | | | | | | | | | | | | |
| P12 | | | | | | | | | | | | | | | |
| P13 | | | | | | | | | | | | | | | |
| P14 | | | | | | | | | | | | | | | |
| P15 | | | | | | | | | | | | | | | |
| P16 | | | | | | | | | | | | | | | |
| P17 | Yellow | | | | | | | | | | | | | | |
| P18 | | | | | | | | | | | | | | | |
| P19 | | | | | | | | | | | | | | | |
| A2 | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLPURAM PROJECT - STATUS OF FLYOVER | | | | | Completed | | | | | | | In Progress | | | | | | | | | | |
|---|----------------|------|-----------------|----|--------------------------|------|------------------|----------------|-----------------|-----------|----------|--------------------------|------|------|-----|----------|-----------|-----------------|----------------|------------------|------|---------------|
| Status upto | 31.08.2023 | | | | LHS | | | | | | | RHS | | | | | | | | | | |
| Sr.No. | FO at Chainage | Span | | | Crash Barrier | Slab | Girder Launching | Girder Casting | Piercap /Abtcap | Abr Shaft | Pile Cap | PCC | Pile | Pile | PCC | Pile Cap | Abr Shaft | Piercap /Abtcap | Girder Casting | Girder Launching | Slab | Crash Barrier |
| 1 | 69+785 | 1x30 | BYPASS | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 2 | 74+655 | 1x30 | BYPASS+EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 3 | 80+556 | 1x30 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 4 | 80+720 | 1x30 | EXISTING | A1 | Negative Change of Scope | | | | | | | Negative Change of Scope | | | | | | | | | | |
| 5 | 95+455 | 2x30 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | P1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 6 | 98+950 | 2x30 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | P1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 7 | 104+570 | 1x30 | BYPASS | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |
| 8 | 110+110 | 1x30 | EXISTING | A1 | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | |

| SETHIYAHOPU CHOLOPURAM PROJECT - STATUS OF VUP | | | | Completed | | | | | | | In Progress | | | | | | | | | | | | | | | | | | |
|--|-----------------|------|-----------------|---------------|------|------------------|----------------|-----------------|-----------|----------|-------------|------|------|-----|----------|-----------|-----------------|----------------|------------------|------|---------------|--|--|--|--|--|--|--|--|
| Status upto | 31.08.2023 | LHS | | | | | | | | | | | | | | RHS | | | | | | | | | | | | | |
| SR.NO. | VUP at Chainage | Span | | Cross Barrier | Slab | Girder Launching | Girder Casting | Piercap /Abtcap | Abt Shaft | Pile Cap | PCC | Pile | Pile | PCC | Pile Cap | Abt Shaft | Piercap /Abtcap | Girder Casting | Girder Launching | Slab | Cross Barrier | | | | | | | | |
| 1 | 72+545 | 1x25 | BYPASS | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | 75+830 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | 86+900 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | 87+670 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | 90+580 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | 97+225 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | 101+910 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | 102+975 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | 106+318 | 1x25 | BYPASS | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | 109+350 | 1x25 | BYPASS | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | 111+235 | 1x25 | BYPASS+EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | 113+550 | 1x25 | BYPASS+EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | 115+258 | 1x25 | EXISTING | A1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | A2 | | | | | | | | | | | | | | | | | | | | | | | | | |

Negative Change of Scope


5. Financial & Physical Progress of Work

Figure 3a: Financial Progress - Planned vs Achieved - S Curve

Figure 3b: Physical Progress - Planned vs Achieved - S Curve


Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to 116.440 Section of NH45C in the state of Tamilnadu under NHDP-IV on Hybrid Annuity Mode.

Fig. 03a- Financial Progress (Revised S-Curve) as per Settlement Agreement signed on dated 20.03.2023.

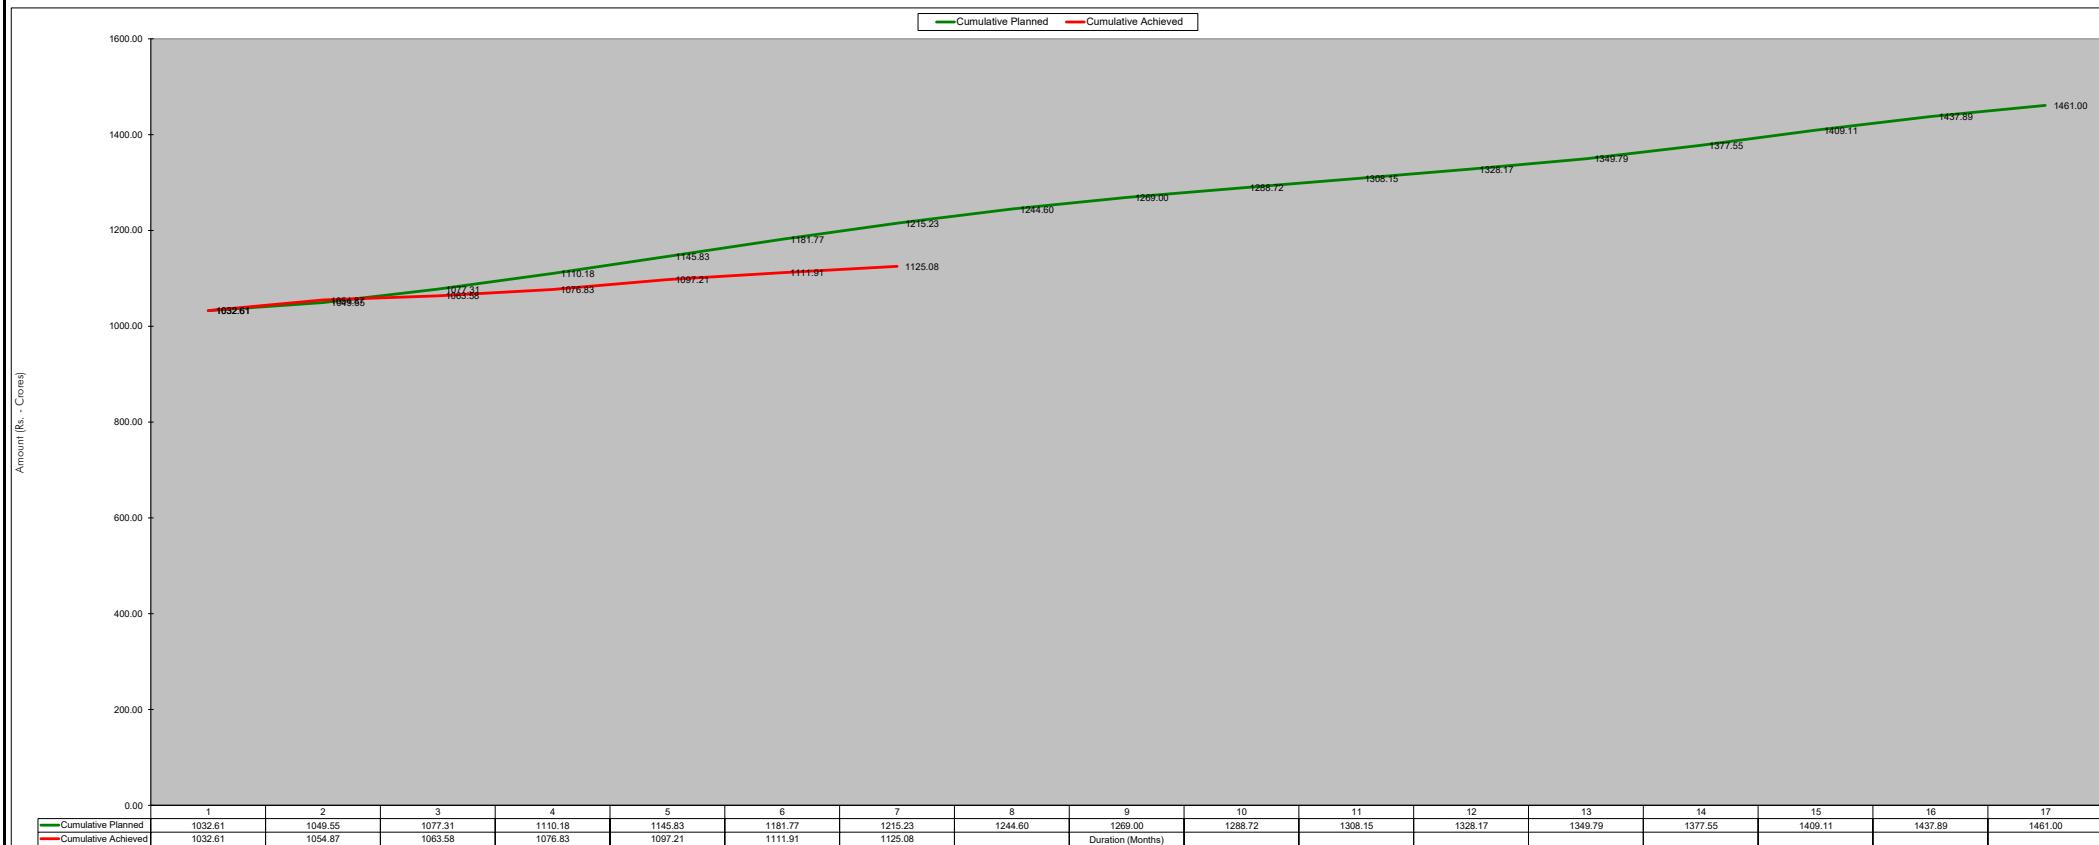

| | Schedule | 2023 | | | | | | | | | | | | 2024 | | | | | |
|---|-------------------------|----------------|---------|---------|---------|---------|---------|---------|---------|-----------|---------|----------|----------|---------|----------|---------|---------|---------|------|
| | | Up to February | | March | April | May | June | July | August | September | October | November | December | January | February | March | April | May | June |
| | | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | |
| Revised Target vs Achieved as per Revised Target set forth in the Settlement Agreement signed on dated 20.03.2023 | Monthly Planned | 1032.61 | 16.95 | 27.76 | 32.87 | 35.65 | 35.94 | 33.46 | 29.37 | 24.40 | 19.72 | 19.43 | 20.02 | 21.62 | 27.76 | 31.56 | 28.78 | 23.11 | |
| | Monthly Achieved | 1032.61 | 22.26 | 8.71 | 13.25 | 20.37 | 14.70 | 13.17 | | | | | | | | | | | |
| | Cumulative Planned | 1032.61 | 1049.55 | 1077.31 | 1110.18 | 1145.83 | 1181.77 | 1215.23 | 1244.60 | 1269.00 | 1288.72 | 1308.15 | 1328.17 | 1349.79 | 1377.55 | 1409.11 | 1437.89 | 1461.00 | |
| | Cumulative Achieved | 1032.61 | 1054.87 | 1063.58 | 1076.83 | 1097.21 | 1111.91 | 1125.08 | | | | | | | | | | | |
| | Monthly Planned (%) | 70.68% | 1.2% | 1.9% | 2.3% | 2.4% | 2.5% | 2.3% | 2.0% | 1.7% | 1.4% | 1.3% | 1.4% | 1.5% | 1.9% | 2.2% | 2.0% | 1.6% | |
| | Monthly Achieved (%) | 70.68% | 1.5% | 0.6% | 0.9% | 1.4% | 1.0% | 0.9% | | | | | | | | | | | |
| | Cumulative Planned (%) | 70.68% | 71.8% | 73.7% | 76.0% | 78.4% | 80.9% | 83.2% | 85.2% | 86.9% | 88.2% | 89.5% | 90.9% | 92.4% | 94.3% | 96.4% | 98.4% | 100.0% | |
| | Cumulative Achieved (%) | 70.68% | 72.20% | 72.80% | 73.71% | 75.10% | 76.11% | 77.01% | | | | | | | | | | | |

Fig. 03b- Physical Progress (Revised S-Curve) as per Settlement Agreement signed on dated 20.03.2023.

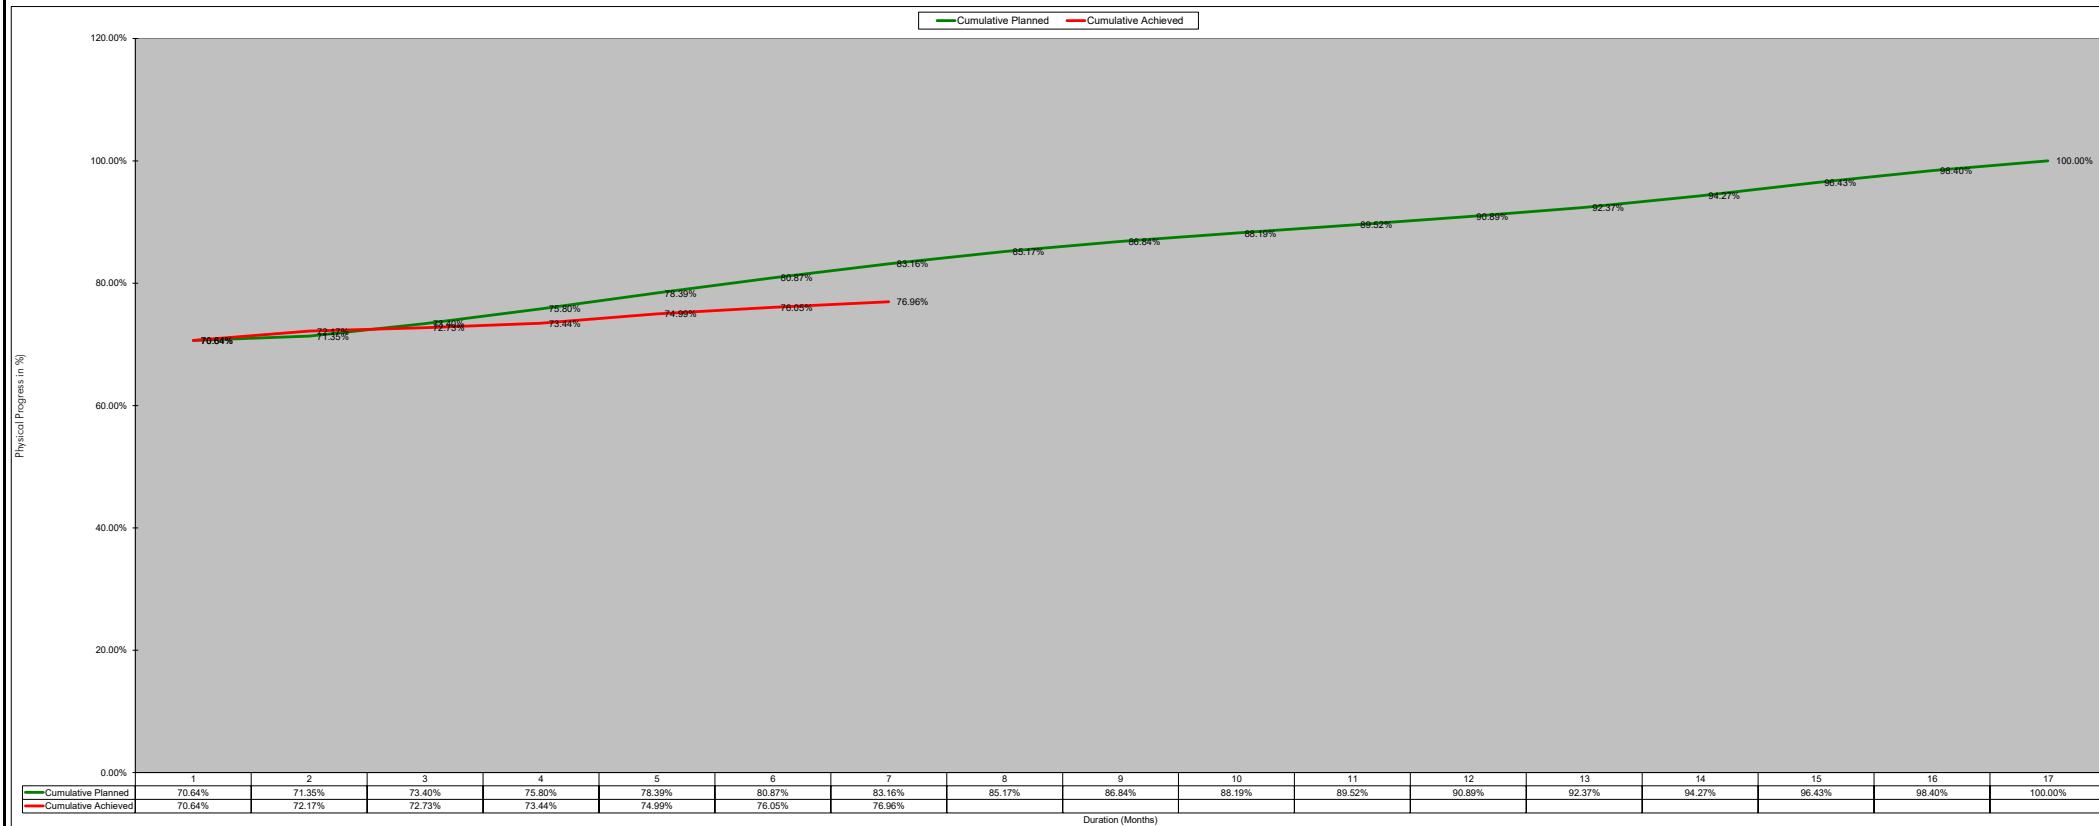

| | Schedule | 2023 | | | | | | | | | | | | 2024 | | | | | |
|---|---------------------|----------------|--------|--------|--------|--------|--------|--------|-----------|---------|----------|----------|---------|----------|--------|--------|--------|---------|--|
| | | Up to February | March | April | May | June | July | August | September | October | November | December | January | February | March | April | May | June | |
| | | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | |
| Revised Target vs Achieved as per Revised Target set forth in the Settlement Agreement signed on dated 20.03.2023 | Monthly Planned | 70.64% | 0.71% | 2.05% | 2.40% | 2.59% | 2.48% | 2.29% | 2.01% | 1.67% | 1.35% | 1.33% | 1.37% | 1.48% | 1.90% | 2.16% | 1.97% | 1.60% | |
| | Monthly Achieved | 70.64% | 1.53% | 0.56% | 0.71% | 1.55% | 1.06% | 0.91% | | | | | | | | | | | |
| | Cumulative Planned | 70.64% | 71.35% | 73.40% | 75.80% | 78.39% | 80.87% | 83.16% | 85.17% | 86.84% | 88.19% | 89.52% | 90.89% | 92.37% | 94.27% | 96.43% | 98.40% | 100.00% | |
| | Cumulative Achieved | 70.64% | 72.17% | 72.73% | 73.44% | 74.99% | 76.05% | 76.96% | | | | | | | | | | | |

5.1 Escrow Details/Financial Expenses Details

The Escrow Details / Financial Expenses details up to the month of August 2023 are given below in the tabular form:-

Table 5.1- 1 Pen Picture Escrow

| Total Project Cost (Cr.) | Cumulative inflow to Escrow till August-2023 (Cr.) | Cumulative out flow from escrow till August-2023 (Cr.) | Inflow to Escrow During August-2023 (Cr.) | Outflow from Escrow during August-2023 (Cr.) |
|--------------------------|--|--|---|--|
| 1,461.00 | 1,478.56 | 1,475.76 | 19.15 | 19.63 |

Table 5.1- 2 Escrow Details

| Total Project Cost (Cr.) | Cumulative expenses till August-2023 (Cr.) | Escrow Plan till August-2023 - Debt (HAM) (Cr.) | Escrow Plan till August-2023 - Equity (HAM) (Cr.) | Escrow Plan till August-2023 - VGF (HAM) (Cr.) | Escrow actual till August-2023 - Debt (HAM) (Cr.) | Escrow actual till August-2023 - Equity (HAM) (Cr.) | Escrow actual till August-2023 - VGF (HAM) (Cr.) |
|--------------------------|--|---|---|--|---|---|--|
| 1,461.00 | 1,110.29 | 701.28 | 175.32 | 584.40 | 472.48 | 127.58 | 501.36 |

6. Quality Control and Quality Assurance

6.1. List of Lab Equipment's

A site laboratory has been set up with all equipments required for testing soil, GSB, WMM, Bitumen, aggregate and concrete. Following tables represents the list of QA/QC equipment's available at Annaikarai & Meensurity Lab.

Table 6.1 - 1 QA/QC Lab Equipment's at Annaikarai Lab

| SI. NO | EQUIPMENT LIST'S | QUANTITY |
|-----------|--|----------|
| 1 | Compression testing machine 2000 kN | 1 |
| 2 | Cement mortar vibrating machine | 1 |
| 3 | AlV Apparatus | 1 |
| 4 | Electronic weighing balance (50 kg) | 1 |
| 5 | Electronic weighing balance (600 gm) | 1 |
| 6 | Hot Air Oven(250° c) | 1 |
| 7 | Hot plate | 1 |
| 8 | Rain Gauge | 1 |
| 9 | Sieve: as per IS: 460-1962 200 dia Brass frame | |
| 10 | 4.75 mm | 1 |
| 11 | 1.18 mm | 1 |
| 12 | 600 mic | 1 |
| 13 | 300 mic | 1 |
| 14 | 90 mic | 1 |
| 15 | 75 mic | 1 |
| 16 | Pan with Lid | 1 |
| 17 | Sieve: as per IS: 460-1962 200 dia GI frame | |
| 18 | 40 mm | 1 |
| 19 | 20 mm | 1 |
| 20 | 12.5 mm | 1 |
| 21 | 10 mm | 1 |
| 22 | 4.75 mm | 1 |
| 23 | 2.36 mm | 1 |
| 24 | Pan with Lid | 1 |
| 25 | Thickness Gauge | 1 |
| 26 | Glass Rain measuring jar (200CM ²) | 2 |
| 27 | GI Tray (18 x24 x50) | 5 |
| 28 | Enamel Tray (medium) | 4 |
| 29 | Enamel Tray (small) | 6 |
| 30 | Spatula wooden handle | 8 |
| 31 | GI Tray () | 1 |
| 32 | Iron tray | 1 |
| 33 | Slump cone apparatus with tamping rod | 2 |

Table 6.1 - 2 QA/QC Lab Equipment's at Meensurity Lab

| SI. NO | EQUIPMENT LIST'S | QUANTITY |
|-----------|--|----------|
| 1 | Test Sieves Set 450mm internal diameter as per IS complete with lid & pan of hole sizes | |
| a | 100mm | 2 Nos |
| b | 75mm | 2 Nos |
| c | 90mm | 2 Nos |
| d | 63mm | 2 Nos |
| e | 53mm | 2 Nos |
| f | 50mm | 2 Nos |
| g | 45mm | 2 Nos |
| h | 40mm | 2 Nos |
| i | 37.5mm | 2 Nos |
| j | 31.5mm | 2 Nos |
| k | 26.5mm | 2 Nos |
| l | 25mm | 2 Nos |
| m | 22.4mm | 2 Nos |
| n | 20.0mm | 2 Nos |
| o | 19.0mm | 2 Nos |
| p | 18mm | 2 Nos |
| q | 16mm | 2 Nos |
| r | 14mm | 2 Nos |
| s | 13.2mm | 2 Nos |
| t | 12.5mm | 2 Nos |
| v | 11.2mm | 2 Nos |
| u | 10mm | 2 Nos |
| w | 9.5mm | 2 Nos |
| x | 6.3mm | 2 Nos |
| y | 5.6mm | 2 Nos |
| z | 4.75mm | 2 Nos |
| 2 | Test Sieves Set 200mm internal diameter (Brass frame & steel or brass wire cloth mesh) as per IS complete with lid & pan of sieve | |
| a | 37.5mm | 2 Nos |
| b | 26.5mm | 2 Nos |
| c | 22.4mm | 2 Nos |
| d | 19mm | 2 Nos |
| e | 16mm | 2 Nos |
| f | 14mm | 2 Nos |
| g | 13.2mm | 2 Nos |
| h | 12.5 | 2 Nos |
| i | 11.2mm | 2 Nos |
| j | 10mm | 2 Nos |
| k | 9.5mm | 2 Nos |
| l | 4.75mm | 2 Nos |

| | | |
|----|---|--------|
| m | 2.8mm | 2 Nos |
| n | 2.36mm | 2 Nos |
| o | 2.0mm | 2 Nos |
| p | 1.80mm | 2 Nos |
| q | 1.7mm | 2 Nos |
| r | 1.4mm | 2 Nos |
| s | 1.18mm | 2 Nos |
| t | 1.0mm | 3 Nos |
| v | 0.600mm | 2 Nos |
| u | 0.425mm | 2 Nos |
| w | 0.355mm | 2 Nos |
| x | 0.300mm | 2 Nos |
| y | 0.180 | 2 Nos |
| z | 0.090mm | 2 Nos |
| aa | 0.075mm | 6 Nos |
| 3 | Measuring Cylinder - Borosilicate glass - 100ML | 40 Nos |
| 4 | Glass Thermometer 00c to 3000c | 10 Nos |
| 5 | Flash filtering borosil glass - 2000ML | 1 No |
| 6 | Flash filtering borosil glass - 5000ML | 1 No |
| 7 | Round hot Plate | 2 Nos |
| 8 | Measuring cylinder - Borosilicate glass - 1000ML | 4 Nos |
| 9 | Measuring cylinder - Borosilicate glass - 250ML | 4 Nos |
| 10 | Measuring cylinder- Borosilicate glass - 500ML | 4 Nos |
| 11 | Beakers - glass borosil - low from cap 600ML | 4 Nos |
| 12 | Compaction pedestal - 4" | 4 Nos |
| 13 | Extractor plate - 6" dia for marshal test | 1 No |
| 14 | Rammer marshal - 4" | 4 Nos |
| 15 | Thermometer Infra red - MTX - 2 | 2 Nos |
| 16 | LE - Chatlier mould one set of six | 2 Nos |
| 17 | Cone penetrometer | 1 No |
| 18 | Los angeles abrasion testing machine | 1 No |
| 19 | Marshal Mould - 4" dia | 51 nos |
| 20 | G.I Tray - 1500*1500*100MM | 4 Nos |
| 21 | Compaction pedestal - 6" | 1 No |
| 22 | Marshal stability apparatus | 1 No |
| 23 | Measuring cylinder- Plastic - 50ML | 4 Nos |
| 24 | Measuring cylinder- Plastic - 250ML | 2 Nos |
| 25 | Measuring cylinder- Plastic - 500ML | 2 Nos |
| 26 | Measuring cylinder- Plastic - 1000ML | 2 Nos |
| 27 | Vibrating machine with digital timer | 1 No |
| 28 | Hot Air Oven - Thermostatic - NoN Digital - 45*45*45 CM | 1 No |
| 29 | Hot Air Oven - Thermostatic - NoN Digital - 90*60*60 CM | 1 No |
| 30 | Penetration cup - 55*70 MM | 2 Nos |
| 31 | Penetration cup - 55*35MM | 6 Nos |
| 32 | Standard Penetrometer - Automatic with digital timer | 1 No |

| | | |
|----|--|---------|
| 33 | Proctor compaction mould 100mm dia with 2.69 kg Rammer mid steel | 4 Nos |
| 34 | Proctor compaction mould 150mm dia with 4.89 kg Rammer mid steel | 6 Nos |
| 35 | Proving ring compression type 10kn | 1 Nos |
| 36 | Proving ring compression type 2.5kn | 1 Nos |
| 37 | Proving ring compression type 25kn | 1 Nos |
| 38 | Proving ring compression type 50kn | 1 Nos |
| 39 | Pycnometer bottle | 4 Nos |
| 40 | Rapid moisture meter-0-25% | 4 Nos |
| 41 | Riffle sample divider -G.I-20mm , no of slot ;16 | 1 nos |
| 42 | Riffle sample divider -G.I-40mm , no of slot ;12 | 1 Nos |
| 43 | Pipette borosilicate glass - 10 ml | 4 Nos |
| 44 | Sand equivalent value test apparatus with accessories | 1 Nos |
| 45 | Field density test app - sand replacement method small | 2 Set |
| 46 | Shrinkage limit set W/O mercury | 1 Nos |
| 47 | Mercury 250 Gm | 1 Nos |
| 48 | Buoyancy balance | 1 Nos |
| 49 | Spatula 8" | 10 Nos |
| 50 | Spatula 4" | 10 Nos |
| 51 | Standard sand - grade III - Bag of 25 kg | 2 Nos |
| 52 | Standard sand - grade I - Bag of 25 kg | 2 Bag |
| 53 | Standard sand - grade II - Bag of 25 kg | 2 Bag |
| 54 | Standard penetrometer - automatic with digital timer | 1 Nos |
| 55 | Beaking head assembly - 6' | 1 Nos |
| 56 | Bulk density cylindrical metal measure - 15 LTR | 1 Nos |
| 57 | Bulk density cylindrical metal measure - 5 LTR | 1 Nos |
| 58 | Bulk density cylindrical metal measure - 30 LTR | 1 Nos |
| 59 | Calcium carbide - 500 GM for rapid moisture meter | 10 Nos |
| 60 | Liquid limits device - hand operated | 1 Nos |
| 61 | CBR mould mild steel 150mm dia eith collar and base plate | 60 Nos |
| 62 | Perforated plate - for CBR test AS per 1377 | 57 Nos |
| 63 | Spacer disc - for CBR test | 4 nos |
| 64 | Surcharge weight 2.5kg annular for cbr test | 120 nos |
| 65 | CBR load frame electrical single speed | 1 nos |
| 66 | Chisel 25mm wide *300mm long | 20 nos |
| 67 | Compression testing machine 2000kn digital manual pace | 1 nos |
| 68 | Cube moulds 7.06cm isi marked for cement | 12 |
| 69 | Concrete mixer - Tilting drum type | 1 No |
| 70 | Constant temperature water bath for marshal test with digital | 2 Nos |
| 71 | Core drilling machine with diesel engine | 1 No |
| 72 | Electronic weighing balance - 10KG | 1 No |
| 73 | Cube moulds - 10CM | 18 Nos |
| 74 | Cube moulds - 5CM | 12 Nos |
| 75 | Electronic weighing balance - 600Gms | 2 Nos |
| 76 | Dial gauge 0.01*30mm | 4 Nos |

| | | |
|-----|--|--------|
| 77 | Electronic platform balance - 100KG | 1 Nos |
| 78 | Electronic weighing balance - 30KG | 2 Nos |
| 79 | Electronic weighing balance - 50KG | 2 Nos |
| 80 | Electronic weighing balance - 5KG | 1 No |
| 81 | Stop watch - digital | 4 Nos |
| 82 | Direct shear apparatus | 1 No |
| 83 | Bottle wash plastic - 1000ML | 4 Nos |
| 84 | Length gauge | 1 No |
| 85 | Tray - G.I 300*300MM (12"*12") | 6 Nos |
| 86 | Enamel tray -300*250*40 mm (10"*12") | 9 Nos |
| 87 | Tray G.I -300*250*40 mm (10"*12") | 9 Nos |
| 88 | Enamel tray -450*600*40 mm (18"*12") | 12 Nos |
| 89 | Field density test app -sand replacement method medium | 2 Set |
| 90 | Field density test app -sand replacement method Large | 2 Set |
| 91 | Filter paper for marshal test 100mm dia | 10 PKT |
| 92 | Filter paper for CBR test 15cm dia PKT of 100 circles | 10 PKT |
| 93 | Flakiness gauge - M.S .Chrome / powder coated | 1 Nos |
| 94 | Pensky marten flash pivot apparatus | 1 Nos |
| 95 | Flexural strength testing machine curve | 1 Nos |
| 96 | French curve | 2 Nos |
| 97 | Slump test apparatus with tamping rod 16mm dia *600mm long | 9 Nos |
| 98 | Thermometer dial 100mm dia * 300mm long 00 - 3000c | 10 Nos |
| 99 | Tripod stand for CBR test | 4 Nos |
| 100 | Gauging trowel 6" (150mm) | 4 Nos |
| 101 | U tube glass viscometer | 1 Nos |
| 102 | Saybolt viscometer with energy regulator | 1 Nos |
| 103 | Vacuum pump -Singal Stage | 1 Nos |
| 104 | Vibrating table -60*60 CM | 1 Nos |
| 105 | Needle final setting time for vicat needle apparatus | 1 Nos |
| 106 | Needle Initial setting time for vicat needle apparatus | 1 Nos |
| 107 | Vicat Needle apparatus | 2 Nos |
| 108 | Hammer with Handle - 1000 GM | 4 Nos |
| 109 | Aggregate Impact testing machine | 1 Nos |
| 110 | Beakers - glass borosil - low form cap ; 600ML | 2 Nos |
| 111 | Beam mould -15*15*70 CM - Mild steel | 17 Nos |

6.2. Quality Control Test Summary

GSB material, soil samples from borrow areas, aggregates, cement and bitumen are being tested regularly. Trial mix design for concrete with different admixtures is also in progress.

The detailed list of quality control test conducted up to the month of August - 2023 are tabulated below:-

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | Tests conducted during reporting month August 2023 | | | | | | Tests conducted upto this month | | | |
|--|------------------------------|-------------------------|-----------------------------|--|--------|--------|---------------------------------|---|----|------------------------------|----|------------------------------|----|--|--------|--------|---------------------------------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested Concessio naire | IE | Passed Concessio naire | IE | Failed Concessio naire | IE | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE |
| 1.0 Tests on OGL | | | | | | | | | | | | | | | | | |
| 1.1 | Grain size analysis | IS:2720 (Part4) | 1 test /250 meters | 345 | 345 | 0 | 97 | 0 | 0 | 0 | 0 | 0 | 0 | 345 | 345 | 0 | 97 |
| 1.2 | Atterberg Limits | IS:2720 (Part5) | 1 test /250 meters | 345 | 345 | 0 | 97 | 0 | 0 | 0 | 0 | 0 | 0 | 345 | 345 | 0 | 97 |
| 1.3 | Proctor | IS:2720 (Part8) | 1 test /250 meters | 345 | 345 | 0 | 97 | 0 | 0 | 0 | 0 | 0 | 0 | 345 | 345 | 0 | 97 |
| 1.4 | Free Swell index | IS:2720 (Part40) | 1 test /250 meters | 345 | 338 | 7 | 97 | 0 | 0 | 0 | 0 | 0 | 0 | 345 | 338 | 7 | 97 |
| 1.5 | California bearing ratio | IS:2720 (Part16) | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 2.0 Borrow Area for Embankment/Subgrade (MoRT&H 305) | | | | | | | | | | | | | | | | | |
| 2.1 | Grain size analysis | IS:2720 (Part4) | 1 test /1500 m ³ | 1820 | 1820 | 0 | 982 | 20 | 10 | 20 | 10 | 0 | 0 | 1840 | 1840 | 0 | 992 |
| 2.2 | Atterberg Limits | IS:2720 (Part5) | 1 test /1500 m ³ | 1820 | 1820 | 0 | 982 | 20 | 10 | 20 | 10 | 0 | 0 | 1840 | 1840 | 0 | 992 |
| 2.3 | Proctor | IS:2720 (Part8) | 1 test /1500 m ³ | 1820 | 1820 | 0 | 982 | 20 | 10 | 20 | 10 | 0 | 0 | 1840 | 1840 | 0 | 992 |
| 2.4 | Free Swell index | IS:2720 (Part40) | 1 test /1500 m ³ | 1820 | 1820 | 0 | 982 | 20 | 10 | 20 | 10 | 0 | 0 | 1840 | 1840 | 0 | 992 |
| 2.5 | California bearing ratio | IS:2720 (Part16) | 1 test /3000 m ³ | 528 | 514 | 16 | 278 | 10 | 5 | 10 | 5 | 0 | 0 | 538 | 524 | 16 | 283 |
| 2.6 | Direct shear Test | IS:2720 (Part13) | 1 test /3000 m ³ | 383 | 380 | 3 | 196 | 10 | 5 | 10 | 5 | 0 | 0 | 393 | 390 | 3 | 201 |
| 3.0 Cutting & Existing portion for Embankment/Subgrade site sampling (MoRT&H 305) | | | | | | | | | | | | | | | | | |
| 3.1 | Grain size analysis | IS:2720 (Part4) | 1 test /1500 m ³ | 133 | 131 | 2 | 62 | 15 | 7 | 15 | 7 | 0 | 0 | 148 | 146 | 2 | 69 |
| 3.2 | Atterberg Limits | IS:2720 (Part5) | 1 test /1500 m ³ | 133 | 131 | 2 | 62 | 15 | 7 | 15 | 7 | 0 | 0 | 148 | 146 | 2 | 69 |
| 3.3 | Proctor | IS:2720 (Part8) | 1 test /1500 m ³ | 133 | 131 | 2 | 62 | 15 | 7 | 15 | 7 | 0 | 0 | 148 | 146 | 2 | 69 |
| 3.4 | Free Swell index | IS:2720 (Part40) | 1 test /1500 m ³ | 133 | 131 | 2 | 62 | 15 | 7 | 15 | 7 | 0 | 0 | 148 | 146 | 2 | 69 |
| 3.5 | California bearing ratio | IS:2720 (Part16) | 1 test /3000 m ³ | 46 | 44 | 2 | 26 | 0 | 0 | 0 | 0 | 0 | 0 | 46 | 44 | 2 | 26 |
| 3.6 | Direct shear Test | IS:2720 (Part13) | 1 test /3000 m ³ | 25 | 25 | 0 | 11 | 15 | 7 | 15 | 7 | 0 | 0 | 40 | 40 | 0 | 18 |
| 4.0 Service Road | | | | | | | | | | | | | | | | | |
| 4.1 | Grain size analysis | IS:2720 (Part4) | 1 test /1500 m ³ | 27 | 27 | 0 | 20 | 0 | 0 | 0 | 0 | 0 | 0 | 27 | 27 | 0 | 20 |
| 4.2 | Atterberg Limits | IS:2720 (Part5) | 1 test /1500 m ³ | 27 | 27 | 0 | 20 | 0 | 0 | 0 | 0 | 0 | 0 | 27 | 27 | 0 | 20 |
| 4.3 | Proctor | IS:2720 (Part8) | 1 test /1500 m ³ | 27 | 27 | 0 | 20 | 0 | 0 | 0 | 0 | 0 | 0 | 27 | 27 | 0 | 20 |
| 4.4 | Free Swell index | IS:2720 (Part40) | 1 test /1500 m ³ | 27 | 27 | 0 | 20 | 0 | 0 | 0 | 0 | 0 | 0 | 27 | 27 | 0 | 20 |
| 4.5 | California bearing ratio | IS:2720 (Part16) | 1 test /3000 m ³ | 8 | 8 | 0 | 8 | 0 | 0 | 0 | 0 | 0 | 0 | 8 | 8 | 0 | 8 |
| 4.6 | Direct shear Test | IS:2720 (Part13) | 1 test /3000 m ³ | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 5.0 Flyash for Embankment | | | | | | | | | | | | | | | | | |
| 5.1 | Liquid Limit & Plastic limit | TABLE-1 | 1 test /1500 m ³ | 497 | 497 | 0 | 282 | 0 | 0 | 0 | 0 | 0 | 0 | 497 | 497 | 0 | 282 |
| 5.2 | Maximum Dry Density | Clause 5.2 | 1 test /1500 m ³ | 497 | 497 | 0 | 294 | 0 | 0 | 0 | 0 | 0 | 0 | 497 | 497 | 0 | 294 |
| 5.3 | Grain size analysis | IS:2720 (Part4) | 1 test /3000 m ³ | 357 | 357 | 0 | 206 | 0 | 0 | 0 | 0 | 0 | 0 | 357 | 357 | 0 | 206 |
| 5.4 | Direct shear Test | IS:2720 (Part13) | 1 test /3000 m ³ | 227 | 227 | 0 | 126 | 0 | 0 | 0 | 0 | 0 | 0 | 227 | 227 | 0 | 126 |

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | Tests conducted during reporting month August 2023 | | | | | | Tests conducted upto this month | | | |
|--|--|-------------------------|-----------------------------|--|--------|--------|------------------------------|---|-----------------|------|--------|-----------------|----|---------------------------------|--|--------|--------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested | Concessio naire | IE | Passed | Concessio naire | IE | Failed | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed |
| 6.0 Field Density Test (MoRT&H 305) | | | | | | | | | | | | | | | | | |
| 6.1 | Field density (OGL) | IS:2720 (Part28) | 1 test /3000 sqm | 4492 | 4369 | 123 | 1098 | 10 | 2 | 10 | 2 | 0 | 0 | 4502 | 4379 | 123 | 1100 |
| 6.2 | EMB field density | IS:2720 (Part28) | 1 test /3000 sqm | 109375 | 105934 | 3441 | 19132 | 4592 | 546 | 4340 | 510 | 252 | 36 | 113967 | 110274 | 3693 | 19678 |
| 6.3 | SG field density | IS:2720 (Part28) | 1 test /2000 sqm | 21916 | 21313 | 603 | 6796 | 95 | 36 | 80 | 30 | 15 | 6 | 22011 | 21393 | 618 | 6832 |
| 6.4 | Shoulder field density | IS:2720 (Part28) | 1 test /2000 sqm | 1213 | 1170 | 43 | 135 | 0 | 0 | 0 | 0 | 0 | 0 | 1213 | 1170 | 43 | 135 |
| 6.5 | Ground improvement (Soil) | IS:2720 (Part28) | 1 test /2000 sqm | 7112 | 6978 | 134 | 724 | 140 | 30 | 140 | 30 | 0 | 0 | 7252 | 7118 | 134 | 754 |
| 6.6 | Ground improvement & Median filling (Flyash) | IS:2720 (Part28) | 1 test /2000 sqm | 43627 | 41969 | 1658 | 5547 | 2247 | 199 | 2220 | 190 | 27 | 9 | 45874 | 44189 | 1685 | 5746 |
| 7.0 Filter Media & Back filling (MoRT&H 2500) | | | | | | | | | | | | | | | | | |
| 7.1 | Gradation | | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 7.2 | Backfilling field density | | 1 test /1000 m ³ | 993 | 990 | 3 | 58 | 0 | 0 | 0 | 0 | 0 | 0 | 993 | 990 | 3 | 58 |
| 7.3 | RE Wall field density | | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 8.0 Safe Bearing capacity of soil | | | | | | | | | | | | | | | | | |
| 8.1 | Free Swell index | IS:2720 (Part40) | As required | 115 | 102 | 13 | 99 | 0 | 0 | 0 | 0 | 0 | 0 | 115 | 102 | 13 | 99 |
| 8.2 | Grain size analysis | IS:2720 (Part4) | As required | 115 | 108 | 7 | 99 | 0 | 0 | 0 | 0 | 0 | 0 | 115 | 108 | 7 | 99 |
| 8.3 | Proctor | IS:2720 (Part8) | As required | 115 | 108 | 7 | 99 | 0 | 0 | 0 | 0 | 0 | 0 | 115 | 108 | 7 | 99 |
| 8.4 | Direct shear Test | IS:2720 (Part13) | As required | 115 | 96 | 19 | 99 | 0 | 0 | 0 | 0 | 0 | 0 | 115 | 96 | 19 | 99 |
| 8.5 | Bearing Capacity / Plate Load Test | IS:6403 / IS:1888 | As required | 112 | 58 | 54 | 68 | 0 | 0 | 0 | 0 | 0 | 0 | 112 | 58 | 54 | 68 |
| 9.0 CTSB Mix Design/Site Frequency (MoRT&H 403) | | | | | | | | | | | | | | | | | |
| 9.1 | Gradation | Table 400-4 | 1 test/400m ³ | 1394 | 1394 | 0 | 578 | 16 | 13 | 16 | 13 | 0 | 0 | 1410 | 1410 | 0 | 591 |
| 9.2 | Atterberg Limits | IS:2720 (Part5) | 1 test/400m ³ | 1273 | 1273 | 0 | 501 | 16 | 13 | 16 | 13 | 0 | 0 | 1289 | 1289 | 0 | 514 |
| 9.3 | Proctor | IS:2720 (Part8) | As required | 72 | 72 | 0 | 70 | 2 | 2 | 2 | 2 | 0 | 0 | 74 | 74 | 0 | 72 |
| 9.4 | CBR Test or unconfined compressive strength test | IS:2720 (Part16) | As required | 1 | 1 | 0 | 1 | 0 | 0 | 0 | 0 | 0 | 0 | 1 | 1 | 0 | 1 |
| 9.5 | Quality of cement | | Minimum 1 test/5 tons | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 |
| 9.6 | Aggregate Impact value | IS:2386 (Part4) | As required | 28 | 28 | 0 | 17 | 0 | 0 | 0 | 0 | 0 | 0 | 28 | 28 | 0 | 17 |
| 9.7 | Field Density | IS:2720 (Part28) | 1 set of 2 Test per 500 Sqm | 7170 | 7170 | 0 | 3925 | 33 | 13 | 33 | 13 | 0 | 0 | 7203 | 7203 | 0 | 3938 |
| 9.8 | Specific gravity & Water absorption | IS:2386 (Part2) | As required | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 |
| 9.9 | Cubes | IRC:SP:89 (2010) | 1 set 400MT | 2395 | 2395 | 0 | 912 | 14 | 11 | 14 | 11 | 0 | 0 | 2409 | 2409 | 0 | 923 |
| 10.0 Granular Bedding Material (For Structures-Ground Improvement)-Mix Design | | | | | | | | | | | | | | | | | |
| 10.1 | Gradation | Table 400-1 | 1 test/400m ³ | 5 | 5 | 0 | 5 | 0 | 0 | 0 | 0 | 0 | 0 | 5 | 5 | 0 | 5 |
| 10.2 | Atterberg Limits | IS:2720 (Part5) | 1 test/400m ³ | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 |
| 10.3 | Proctor | IS:2720 (Part8) | As required | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 |
| 10.4 | CBR Test | IS:2720 (Part16) | As required | 1 | 1 | 0 | 1 | 0 | 0 | 0 | 0 | 0 | 0 | 1 | 1 | 0 | 1 |
| 10.5 | Aggregate Impact value | IS:2386 (Part4) | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 10.6 | Field Density | IS:2720 (Part28) | 1 Test per 1000 Sqm | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | Tests conducted during reporting month August 2023 | | | | | | Tests conducted upto this month | | | | |
|--|--------------------------------|-------------------------|----------------------------------|--|--------|--------|------------------------------|---|--------|--------|--|--------|--------|---------------------------------|--|--------|--------|------------------------------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested | Passed | Failed | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE |
| 11.0 Granular Bedding Material (For Structures-Ground Improvement)-Site Frequency | | | | | | | | | | | | | | | | | | |
| 11.1 | Gradation | Table 400-1 | 1 test/400m ³ | 3 | 3 | 0 | 3 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 3 | 3 | 0 | 3 |
| 11.2 | Atterberg Limits | IS:2720 (Part5) | 1 test/400m ³ | 3 | 3 | 0 | 3 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 3 | 3 | 0 | 3 |
| 11.3 | Proctor | IS:2720 (Part8) | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 11.4 | CBR Test | IS:2720 (Part16) | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 11.5 | Aggregate Impact value | IS:2386 (Part4) | As required | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 11.6 | Field Density | IS:2720 (Part28) | 1 Test per 1000 Sqm | 90 | 90 | 0 | 21 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 90 | 90 | 0 | 21 |
| 12.0 WMM Mix Design (MoRT&H 406) | | | | | | | | | | | | | | | | | | |
| 12.1 | Gradation | Table 400-3 | 1 test/200m ³ | 61 | 61 | 0 | 61 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 61 | 61 | 0 | 61 |
| 12.2 | Aggregate Impact Value | IS:2386 (Part4) | 1 test/1000m ³ | 13 | 13 | 0 | 13 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 13 | 13 | 0 | 13 |
| 12.3 | Flakiness & Elongation index | IS:2386 (Part1) | 1 test/500m ³ | 12 | 12 | 0 | 12 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 12 | 12 | 0 | 12 |
| 12.4 | Atterberg Limits | IS:2720 (Part5) | 1 test/200m ³ | 12 | 12 | 0 | 12 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 12 | 12 | 0 | 12 |
| 12.5 | Water absorption & Sp. Gravity | IS:2386 (Part2) | As required | 8 | 8 | 0 | 8 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 8 | 8 | 0 | 8 |
| 12.6 | Proctor | IS:2720 (Part8) | As required | 4 | 4 | 0 | 4 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 4 | 4 | 0 | 4 |
| 12.7 | CBR | IS:2720 (Part16) | As required | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 |
| 13.0 WMM Site Frequency (MoRT&H 406) | | | | | | | | | | | | | | | | | | |
| 13.1 | Gradation | Table 400-3 | 1 test/200m ³ | 893 | 893 | 0 | 367 | 10 | 7 | 10 | 7 | 0 | 0 | 903 | 903 | 0 | 374 | |
| 13.2 | Aggregate Impact Value | IS:2386 (Part4) | 1 test/1000m ³ | 537 | 537 | 0 | 219 | 8 | 5 | 8 | 5 | 0 | 0 | 545 | 545 | 0 | 224 | |
| 13.3 | Flakiness & Elongation index | IS:2386 (Part1) | 1 test/500m ³ | 551 | 551 | 0 | 205 | 8 | 5 | 8 | 5 | 0 | 0 | 559 | 559 | 0 | 210 | |
| 13.4 | Atterberg Limits | IS:2720 (Part5) | 1 test/200m ³ | 856 | 856 | 0 | 333 | 10 | 7 | 10 | 7 | 0 | p | 866 | 866 | 0 | 340 | |
| 13.5 | Water absorption | IS:2386 (Part2) | As required | 4 | 4 | 0 | 4 | 0 | 0 | 0 | 0 | 0 | 0 | 4 | 4 | 0 | 4 | |
| 13.6 | Proctor | IS:2720 (Part8) | As required | 34 | 34 | 0 | 32 | 1 | 1 | 1 | 1 | 0 | 0 | 35 | 35 | 0 | 33 | |
| 13.7 | CBR | IS:2720 (Part16) | As required | 1 | 1 | 0 | 1 | 0 | 0 | 0 | 0 | 0 | 0 | 1 | 1 | 0 | 1 | |
| 13.8 | Field Density | IS:2720 (Part28) | 1 set Test per 1000 Sqm / 3 pits | 1964 | 1964 | 0 | 1050 | 31 | 7 | 31 | 7 | 0 | 0 | 1995 | 1995 | 0 | 1057 | |
| 14.0 Dense Bituminous Macadam (Grade - II) | | | | | | | | | | | | | | | | | | |
| 14.1 | Bitumen Extraction & Gradation | | 1 Test/400MT | 535 | 535 | 0 | 256 | 6 | 6 | 6 | 6 | 0 | 0 | 541 | 541 | 0 | 262 | |
| 14.2 | Combined Gradation | Table 500 - 18, Grad.II | 1 Test/400MT | 522 | 522 | 0 | 233 | 6 | 6 | 6 | 6 | 0 | 0 | 528 | 528 | 0 | 239 | |
| 14.3 | Individual Gradation Sets | Table 500 - 18, Grad.II | 1 Test/400MT | 521 | 521 | 0 | 236 | 6 | 6 | 6 | 6 | 0 | 0 | 527 | 527 | 0 | 242 | |
| 14.4 | Flakiness & Elongation index | MoRT&H Table 900 - 4 | 1 test/350m ³ | 332 | 332 | 0 | 153 | 3 | 3 | 3 | 3 | 0 | 0 | 335 | 335 | 0 | 156 | |
| 14.5 | Aggregate Impact Value | MoRT&H Table 900 - 4 | 1 test/350m ³ | 379 | 379 | 0 | 173 | 3 | 3 | 3 | 3 | 0 | 0 | 382 | 382 | 0 | 176 | |
| 14.6 | Marshall Density | ASTM D 2726 | 1 Set/400MT | 556 | 556 | 0 | 259 | 6 | 6 | 6 | 6 | 0 | 0 | 562 | 562 | 0 | 265 | |
| 14.7 | GMM | MoRT&H Table 900 - 4 | 1 Test/400MT | 527 | 527 | 0 | 245 | 6 | 6 | 6 | 6 | 0 | 0 | 533 | 533 | 0 | 251 | |
| 14.8 | DBM Core Cutting | MoRT&H Table 900 - 4 | 1 Test/700M ² | 1555 | 1555 | 0 | 928 | 14 | 14 | 14 | 14 | 0 | 0 | 1569 | 1569 | 0 | 942 | |
| Bitumen test (VG-40) | | | | | | | | | | | | | | | | | | |
| 14.9 | Softening Point | IS:1205 - 1978 | 1 Test/ 1 lot | 258 | 258 | 0 | 119 | 2 | 2 | 2 | 2 | 0 | 0 | 260 | 260 | 0 | 121 | |
| 14.10 | Penetration | IS:1205 - 1978 | 1 Test/ 1 lot | 258 | 258 | 0 | 119 | 2 | 2 | 2 | 2 | 0 | 0 | 260 | 260 | 0 | 121 | |
| 14.11 | Viscosity | IS:1205 - 1978 | 1 Test/ 1 lot | 258 | 258 | 0 | 119 | 2 | 2 | 2 | 2 | 0 | 0 | 260 | 260 | 0 | 121 | |

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | Tests conducted during reporting month August 2023 | | | | | | Tests conducted upto this month | | | |
|--|-------------------------------------|-------------------------|--------------------------|--|--------|--------|------------------------------|---|-----------------|----|--------|-----------------|----|---------------------------------|--|--------|--------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested | Concessio naire | IE | Passed | Concessio naire | IE | Failed | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed |
| 15.0 Bituminous Concrete (Grade - II) PMB MCW | | | | | | | | | | | | | | | | | |
| 15.1 | Bitumen Extraction & Gradation | IRC:SP:11 | 1 Test/400MT | 299 | 299 | 0 | 173 | 2 | 2 | 2 | 2 | 0 | 0 | 301 | 301 | 0 | 175 |
| 15.2 | Combined Gradation | Table 500 - 17, Grad.II | 1 Test/400MT | 299 | 299 | 0 | 187 | 2 | 2 | 2 | 2 | 0 | 0 | 301 | 301 | 0 | 189 |
| 15.3 | Individual Gradation Sets | Table 500 - 17, Grad.II | 1 Test/400MT | 299 | 299 | 0 | 187 | 2 | 2 | 2 | 2 | 0 | 0 | 301 | 301 | 0 | 189 |
| 15.4 | Flakiness & Elongation index | MoRT&H Table 900 - 4 | 1 test/350m ³ | 149 | 149 | 0 | 86 | 1 | 1 | 1 | 1 | 0 | 0 | 150 | 150 | 0 | 87 |
| 15.5 | Aggregate Impact Value | MoRT&H Table 900 - 4 | 1 test/350m ³ | 151 | 151 | 0 | 88 | 1 | 1 | 1 | 1 | 0 | 0 | 152 | 152 | 0 | 89 |
| 15.6 | Marshall Density | ASTM D 2726 | 1 Set/400MT | 295 | 295 | 0 | 162 | 2 | 2 | 2 | 2 | 0 | 0 | 297 | 297 | 0 | 164 |
| 15.7 | GMM | MoRT&H Table 900 - 4 | 1 Test/400MT | 298 | 298 | 0 | 165 | 2 | 2 | 2 | 2 | 0 | 0 | 300 | 300 | 0 | 167 |
| 15.8 | BC Core Cutting | MoRT&H Table 900 - 4 | 1 Test/700M ² | 1121 | 1121 | 0 | 586 | 7 | 7 | 7 | 7 | 0 | 0 | 1128 | 1128 | 0 | 593 |
| 16.0 Bituminous Concrete (Grade - II) VG-40 S/R | | | | | | | | | | | | | | | | | |
| 16.1 | Bitumen Extraction & Gradation | IRC:SP:11 | 1 Test/400MT | 76 | 76 | 0 | 37 | 0 | 0 | 0 | 0 | 0 | 0 | 76 | 76 | 0 | 37 |
| 16.2 | Combined Gradation | Table 500 - 17, Grad.II | 1 Test/400MT | 73 | 73 | 0 | 36 | 0 | 0 | 0 | 0 | 0 | 0 | 73 | 73 | 0 | 36 |
| 16.3 | Individual Gradation Sets | Table 500 - 17, Grad.II | 1 Test/400MT | 73 | 73 | 0 | 36 | 0 | 0 | 0 | 0 | 0 | 0 | 73 | 73 | 0 | 36 |
| 16.4 | Flakiness & Elongation index | MoRT&H Table 900 - 4 | 1 test/350m ³ | 42 | 42 | 0 | 23 | 0 | 0 | 0 | 0 | 0 | 0 | 42 | 42 | 0 | 23 |
| 16.5 | Aggregate Impact Value | MoRT&H Table 900 - 4 | 1 test/350m ³ | 42 | 42 | 0 | 23 | 0 | 0 | 0 | 0 | 0 | 0 | 42 | 42 | 0 | 23 |
| 16.6 | Marshall Density | ASTM D 2726 | 1 Set/400MT | 73 | 73 | 0 | 36 | 0 | 0 | 0 | 0 | 0 | 0 | 73 | 73 | 0 | 36 |
| 16.7 | GMM | MoRT&H Table 900 - 4 | 1 Test/400MT | 73 | 73 | 0 | 36 | 0 | 0 | 0 | 0 | 0 | 0 | 73 | 73 | 0 | 36 |
| 16.8 | BC Core Cutting | MoRT&H Table 900 - 4 | 1 Test/700M ² | 258 | 258 | 0 | 158 | 0 | 0 | 0 | 0 | 0 | 0 | 258 | 258 | 0 | 158 |
| Bitumen test (PMB) | | | | | | | | | | | | | | | | | |
| 16.9 | Softening Point | IS:1205 - 1978 | 1 Test/ 1 lot | 174 | 174 | 0 | 75 | 0 | 0 | 0 | 0 | 0 | 0 | 174 | 174 | 0 | 75 |
| 16.10 | Elastic recovery | IS:15462 - 2019 | 1 Test/ 1 lot | 174 | 174 | 0 | 75 | 0 | 0 | 0 | 0 | 0 | 0 | 174 | 174 | 0 | 75 |
| 17.0 Prime Coat | | | | | | | | | | | | | | | | | |
| 17.0 | Rate of Spread of Binder | | Three tests per day | 1153 | 1153 | 0 | 500 | 12 | 6 | 12 | 6 | 0 | 0 | 1165 | 1165 | 0 | 506 |
| 17.1 Emulsion Test (SS-1) | | | | | | | | | | | | | | | | | |
| 17.1 | Say bolt Viscometer | IS:8887-2004 | 1 Test/ 1 lot | 27 | 27 | 0 | 20 | 0 | 0 | 0 | 0 | 0 | 0 | 27 | 27 | 0 | 20 |
| 17.2 Tack Coat | | | | | | | | | | | | | | | | | |
| 17.2 | Rate of Spread of Binder | | Three tests per day | 1601 | 1601 | 0 | 576 | 18 | 6 | 18 | 6 | 0 | 0 | 1619 | 1619 | 0 | 582 |
| 17.3 Emulsion Test (RS-1) | | | | | | | | | | | | | | | | | |
| 17.3 | Say bolt Viscometer | IS:8887-2004 | 1 Test/ 1 lot | 17 | 17 | 0 | 14 | 0 | 0 | 0 | 0 | 0 | 0 | 17 | 17 | 0 | 14 |
| 18.0 Fine Aggregate (MoRT&H 1008) | | | | | | | | | | | | | | | | | |
| 18.1 | Gradation/ Sieve analysis | IS:2386 (Part1) | 1 test per day | 2479 | 2479 | 0 | 887 | 25 | 7 | 25 | 7 | 0 | 0 | 2504 | 2504 | 0 | 894 |
| 18.2 | Specific gravity & Water absorption | IS:2386 (Part3) | As required | 16 | 16 | 0 | 15 | 0 | 0 | 0 | 0 | 0 | 0 | 16 | 16 | 0 | 15 |
| 18.3 | Fineness Modulus | MoRT&H Sec. 1008 & 383 | 1 test per day | 2337 | 2337 | 0 | 815 | 25 | 7 | 25 | 7 | 0 | 0 | 2362 | 2362 | 0 | 822 |
| 18.4 | Alkali aggregate reactivity test | IS:2386 (Part7) IS:456 | 1 test per source | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 18.5 | Deleterious material/silt | IS:2386 (Part2) | 1 test per source | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | | Tests conducted during reporting month August 2023 | | | | | | | | Tests conducted upto this month | | | |
|--|-------------------------------------|-----------------------------|--------------------------------|--|--------|--------|------------------------------|--------|--|----|--------|-----------------|------|--------|-----------------|-----|--|--------|--------|------------------------------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested | Concessio naire | IE | Passed | Concessio naire | IE | Failed | Concessio naire | IE | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE |
| 19.0 Coarse Aggregate (MoRT&H 1007) | | | | | | | | | | | | | | | | | | | | |
| 19.1 | Gradation | IS:2386 (Part1) | 1 test per day | 2393 | 2393 | 0 | 887 | 25 | 7 | 25 | 7 | 0 | 0 | 2418 | 2418 | 0 | 894 | | | |
| 19.2 | Specific gravity & Water absorption | IS:2386 (Part3) | As required | 18 | 18 | 0 | 15 | 0 | 0 | 0 | 0 | 0 | 0 | 18 | 18 | 0 | 15 | | | |
| 19.3 | Aggregate Impact Value | IS:2386 (Part4) | 1 test / each source & monthly | 603 | 603 | 0 | 292 | 5 | 5 | 5 | 5 | 0 | 0 | 608 | 608 | 0 | 297 | | | |
| 19.4 | Flakiness index | IS:2386 (Part1) | 1 test / each source & monthly | 568 | 568 | 0 | 275 | 5 | 5 | 5 | 5 | 0 | 0 | 573 | 573 | 0 | 280 | | | |
| 19.5 | Soundness | IS:2386 (Part5) | As required | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 | | | |
| 19.6 | Alkali aggregate reactivity test | IS:2386 (Part7) IS:456 | 1 test per source | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 | | | |
| 19.7 | Deleterious constituents | IS:2386 (Part2) | 1 test per source | 2 | 2 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 2 | 2 | 0 | 2 | | | |
| 19.8 | Petrographic Examination | IS:2386 (Part8) | 1 test per source | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 20.0 Cement (MoRT&H 1006) | | | | | | | | | | | | | | | | | | | | |
| 20.1 | Chemical test / Physical test | IS:4031, 4032 | 1 test per source | 14 | 14 | 0 | 9 | 0 | 0 | 0 | 0 | 0 | 0 | 14 | 14 | 0 | 9 | | | |
| 20.2 | Fineness | IS:4031 (Part1) | Every batch | 646 | 646 | 0 | 306 | 5 | 2 | 5 | 2 | 0 | 0 | 651 | 651 | 0 | 308 | | | |
| 20.3 | Normal Consistency | IS:4031 (Part4) | Every batch | 618 | 618 | 0 | 306 | 5 | 2 | 5 | 2 | 0 | 0 | 623 | 623 | 0 | 308 | | | |
| 20.4 | Initial & Final setting time | IS:4031 (Part5) | Every batch | 618 | 618 | 0 | 306 | 5 | 2 | 5 | 2 | 0 | 0 | 623 | 623 | 0 | 308 | | | |
| 20.5 | Soundness of Cement | IS:4031 (Part3) | Every batch | 562 | 562 | 0 | 272 | 5 | 2 | 5 | 2 | 0 | 0 | 567 | 567 | 0 | 274 | | | |
| 20.6 | Compressive Strength-set | IS:4031 (Part6) | | | | | | | | | | | | | | | | | | |
| | 3 days | | 1 test per Lot | 578 | 578 | 0 | 255 | 5 | 1 | 5 | 1 | 0 | 0 | 583 | 583 | 0 | 256 | | | |
| | 7 days | | 1 test per Lot | 570 | 570 | 0 | 253 | 6 | 3 | 6 | 3 | 0 | 0 | 576 | 576 | 0 | 256 | | | |
| | 28 days | | 1 test per Lot | 563 | 563 | 0 | 241 | 8 | 6 | 8 | 6 | 0 | 0 | 571 | 571 | 0 | 247 | | | |
| 21.0 Concrete Cube Strength | | | | | | | | | | | | | | | | | | | | |
| M15 PCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 913 | 913 | 0 | 304 | 18 | 10 | 18 | 10 | 0 | 0 | 931 | 931 | 0 | 314 | | | | |
| 28Days Compressive Strength | | | 1491 | 1491 | 0 | 650 | 32 | 14 | 32 | 14 | 0 | 0 | 1523 | 1523 | 0 | 664 | | | | |
| M20 KERB | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 364 | 364 | 0 | 87 | 4 | 1 | 4 | 1 | 0 | 0 | 368 | 368 | 0 | 88 | | | | |
| 28Days Compressive Strength | | | 930 | 930 | 0 | 222 | 5 | 2 | 5 | 2 | 0 | 0 | 935 | 935 | 0 | 224 | | | | |
| M20 RCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 536 | 536 | 0 | 160 | 21 | 6 | 21 | 6 | 0 | 0 | 557 | 557 | 0 | 166 | | | | |
| 28Days Compressive Strength | | | 996 | 996 | 0 | 300 | 54 | 15 | 54 | 15 | 0 | 0 | 1050 | 1050 | 0 | 315 | | | | |
| M20 PCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 44 | 44 | 0 | 19 | 0 | 0 | 0 | 0 | 0 | 0 | 44 | 44 | 0 | 19 | | | | |
| 28Days Compressive Strength | | | 57 | 57 | 0 | 23 | 0 | 0 | 0 | 0 | 0 | 0 | 57 | 57 | 0 | 23 | | | | |
| M25 RCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 82 | 82 | 0 | 22 | 0 | 0 | 0 | 0 | 0 | 0 | 82 | 82 | 0 | 22 | | | | |
| 28Days Compressive Strength | | | 146 | 146 | 0 | 84 | 0 | 0 | 0 | 0 | 0 | 0 | 146 | 146 | 0 | 84 | | | | |
| M30 RCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 941 | 941 | 0 | 329 | 0 | 0 | 0 | 0 | 0 | 0 | 941 | 941 | 0 | 329 | | | | |
| 28Days Compressive Strength | | | 1561 | 1561 | 0 | 625 | 8 | 2 | 8 | 2 | 0 | 0 | 1569 | 1569 | 0 | 627 | | | | |

Monthly Progress Report : Summary of Quality Control Report : Month of August - 2023

| Sr. No. | Description | IS Specification Clause | Frequency of Tests | Tests conducted upto Previous month | | | | | Tests conducted during reporting month August 2023 | | | | | | Tests conducted upto this month | | | | | |
|-------------------------------|-------------|-------------------------|--------------------|--|-----------------------------|--------|------------------------------|--------|---|----|--------|-----------------|----|--------|---------------------------------|------|--|--------|--------|------------------------------|
| | | | | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE | Tested | Concessio naire | IE | Passed | Concessio naire | IE | Failed | Concessio naire | IE | Nos. of test Conducted EPC/ Concessionaire | Passed | Failed | Nos. of test witnessed by IE |
| M30 RCC PUMPABLE | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 218 | 218 | 0 | 89 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 218 | 218 | 0 | 89 |
| 28Days Compressive Strength | | | | | | 546 | 546 | 0 | 275 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 546 | 546 | 0 | 275 |
| M35 RCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 418 | 418 | 0 | 196 | 2 | 1 | 2 | 1 | 0 | 0 | 420 | 420 | 0 | 197 | |
| 28Days Compressive Strength | | | | | | 862 | 862 | 0 | 444 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 862 | 862 | 0 | 444 |
| M35 PILING | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 1019 | 1019 | 0 | 537 | 0 | 0 | 0 | 0 | 0 | 0 | 1019 | 1019 | 0 | 537 | |
| 28Days Compressive Strength | | | | | | 3004 | 3004 | 0 | 1638 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 3004 | 3004 | 0 | 1638 |
| M35 RCC PUMPABLE | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 1444 | 1444 | 0 | 602 | 17 | 6 | 17 | 6 | 0 | 0 | 1461 | 1461 | 0 | 608 | |
| 28Days Compressive Strength | | | | | | 4345 | 4345 | 0 | 2170 | 29 | 19 | 29 | 19 | 0 | 0 | 4374 | 4374 | 0 | 2189 | |
| M35 RE BLOCK | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 792 | 792 | 0 | 228 | 0 | 0 | 0 | 0 | 0 | 0 | 792 | 792 | 0 | 228 | |
| 28Days Compressive Strength | | | | | | 2270 | 2270 | 0 | 728 | 0 | 0 | 0 | 0 | 0 | 0 | 2270 | 2270 | 0 | 728 | |
| M40 PUMP & M40 RCC | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 1082 | 1082 | 0 | 408 | 38 | 8 | 38 | 8 | 0 | 0 | 1120 | 1120 | 0 | 416 | |
| 28Days Compressive Strength | | | | | | 2354 | 2354 | 0 | 980 | 48 | 10 | 48 | 10 | 0 | 0 | 2402 | 2402 | 0 | 990 | |
| M40 PQC | | | | | | | | | | | | | | | | | | | | |
| 7 Days Flexural Strength | | | | As Per IS:516 | As Per IS:516 | 12 | 12 | 0 | 12 | 0 | 0 | 0 | 0 | 0 | 0 | 12 | 12 | 0 | 12 | |
| 28 Days Flexural Strength | | | | | | 30 | 30 | 0 | 30 | 0 | 0 | 0 | 0 | 0 | 0 | 30 | 30 | 0 | 30 | |
| 7Days Compressive Strength | | | | As Per IS:516 | As Per IS:516 | 12 | 12 | 0 | 12 | 0 | 0 | 0 | 0 | 0 | 0 | 12 | 12 | 0 | 12 | |
| 28Days Compressive Strength | | | | | | 30 | 30 | 0 | 30 | 0 | 0 | 0 | 0 | 0 | 0 | 30 | 30 | 0 | 30 | |
| M40 PILING | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 306 | 306 | 0 | 92 | 0 | 0 | 0 | 0 | 0 | 0 | 306 | 306 | 0 | 92 | |
| 28Days Compressive Strength | | | | | | 997 | 997 | 0 | 271 | 0 | 0 | 0 | 0 | 0 | 0 | 997 | 997 | 0 | 271 | |
| M45 PUMP | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 455 | 455 | 0 | 194 | 0 | 0 | 0 | 0 | 0 | 0 | 455 | 455 | 0 | 194 | |
| 28Days Compressive Strength | | | | | | 1143 | 1143 | 0 | 453 | 4 | 4 | 4 | 4 | 0 | 0 | 1147 | 1147 | 0 | 457 | |
| M50 RCC PUMP | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 19 | 19 | 0 | 12 | 0 | 0 | 0 | 0 | 0 | 0 | 19 | 19 | 0 | 12 | |
| 28Days Compressive Strength | | | | | | 29 | 29 | 0 | 23 | 0 | 0 | 0 | 0 | 0 | 0 | 29 | 29 | 0 | 23 | |
| M60 PUMP | | | | | | | | | | | | | | | | | | | | |
| 7Days Compressive Strength | | | | MoRT&H Sec. 1700 | MoRT&H Sec. 1700 No of sets | 661 | 661 | 0 | 220 | 13 | 4 | 13 | 4 | 0 | 0 | 674 | 674 | 0 | 224 | |
| 28Days Compressive Strength | | | | | | 2266 | 2266 | 0 | 743 | 14 | 12 | 14 | 12 | 0 | 0 | 2280 | 2280 | 0 | 755 | |

PATEL SETHIYAHOPU CHOLOPURAM HIGHWAY PVT. LTD.

Four Laning of Sethiyahopu - Cholapuram from Km. 65.960 to 116.440 section of NH-45C in the state of Tamil Nadu under NHDP Phase-IV on Hybrid Annuity Mode

| STATUS OF NCR | | | | | | | | | |
|---------------|----------|------------|---|----|---|--|--------------------------------|-----------------------|---------|
| SI No | NCR No. | Date | Location | | Description of NCR | NCR Issued reference | Concessionaire Reply Reference | NCR Closed Reference | Remarks |
| | | | From | To | | | | | |
| 1 | NCR - 01 | 30.01.2019 | Box Culver at Km:76+390 (LHS) | | Improper Ground Improvement for Box culvert at Km:76+390 | Lr.No.221_30.01.2019 | Lr.No.280_14.02.2019 | Lr.No.258_20.03.2019 | Closed |
| 2 | NCR - 02 | 23.05.2019 | Minor Bridge at Km:79+795 (LHS) | | a) Improper compaction/vibration f Abtment -1 wall 2nd lift lead to honey combs. b) No cover to the reinforcement in Abutment -1 wall 2nd lift | Lr.No.304_23.05.2019 | Lr.No.956_13.08.2021 | Lr.No.630A_13.08.2021 | Closed |
| 3 | NCR - 03 | 23.05.2019 | Abutment A2 of Minor Bridge at Km:85+435 (LHS) | | Improper alignment (plumb) of Abutment-2 wall 2nd lift | Lr.No.305_23.05.2019 | Lr.No.958_15.08.2021 | Lr.No.631A_21.08.2021 | Closed |
| 4 | NCR - 04 | 23.05.2019 | Pile cap for Abutment A2 of VUP at Km.102+975 LHS | | Honey combs in Pile cap for Abutment A2 of VUP at Km. 102+975 LHS | Lr.No.306_23.05.2019 | Lr.No.959_15.08.2021 | Lr.No.632A_31.08.2021 | Closed |
| 5 | NCR - 05 | 15.11.2019 | HW between Km:93+900 to Km.94+200 (RHS) | | Rectification required in Median kerb | Lr.No.403_15.11.2019 Lr.No.478_09.07.2020 | Lr.No.1008_22.11.2021 | Lr.No.646_26.11.2021 | Closed |
| 6 | NCR - 06 | 13.12.2019 | HW between Km:82+850 to Km.82+970 (RHS) | | WMM segregation | Lr.No.429_13.12.2019 | Lr.No.786_23.12.2020 | Lr.No.551_29.01.2021 | Closed |
| 7 | NCR - 07 | 09.07.2020 | Diversion road damaged at Km:97+300 to Km:97+600 | | Diversion road damaged | Lr.No.476_09.07.2020 | Lr.No.727_02.10.2020 | Lr.No.509_14.10.2020 | Closed |
| 8 | NCR - 08 | 23.07.2020 | 95+990 to 96+100(RHS) 96+230 to Km:96+300(RHS) | | Improper laying of Kerb and not as per approved drawings | Lr.No.482_23.07.2020 | Lr.No.1009_22.11.2021 | Lr.No.647_26.11.2021 | Closed |
| 9 | NCR - 09 | 31.07.2020 | 96+300 to 96+400(RHS) | | Kerb mould is not as per the approved drawings | Lr.No.484_31.07.2020 | Lr.No.1010_22.11.2021 | Lr.No.648_27.11.2021 | Closed |
| 10 | NCR - 10 | 18.08.2020 | 96+100 to 96+220(RHS) | | Kerb mould is not as per the approved drawings | Lr.No.489_18.08.2020 | Lr.No.1011_22.11.2021 | Lr.No.649_29.11.2021 | Closed |
| 11 | NCR - 11 | 12.11.2020 | Km.83+950 to Km.84+100 | | Excavated Embankment fill and used in Subgrade layer | Lr.No.523_12.11.2020 | Lr.No.774_02.12.2020 | Lr.No.552_29.01.2021 | Closed |
| 12 | NCR - 12 | 02.12.2021 | Km.83+940 to Km.84+080 (LHS) | | Median kerb laying is not in line and level | Lr.No.531_02.12.2021 | Lr.No.1012_22.11.2021 | Lr.No.650_29.11.2021 | Closed |
| 13 | NCR - 13 | 03.04.2021 | Box Culvert at Km:77+766 (LHS) | | Box Culvert without proper shuttering and reinforcement exposed. | Lr.No.587_03.04.2021 | Lr.No.888_12.05.2021 | Lr.No.597A_12.05.2021 | Closed |
| 14 | NCR - 14 | 05.05.2021 | RE wall of VUP at Km:90+580 | | Unsuitable soil is used in RE wall embankment filling at Km:90+580 (VUP) | Lr.No.596_05.05.2021 | Lr.No.892_18.05.2021 | Lr.No.603_22.06.2021 | Closed |
| 15 | NCR - 15 | 20.09.2022 | Km 70+160 to 70+200 | | Mismatching of FRL with approved Plan & Profile | Lr.No.788_20.09.2022 | Lr.No.1323_07.01.2023 | Lr.No.829_10.01.2023 | Closed |

Four Laning of Sethiyahopu - Cholapuram From Km 65.960 to Km 116.440 Section of NH-45C in the State of Tamil Nadu Under NHDP Phase-IV on Hybrid Annuity Mode.

SOURCE APPROVAL SUMMARY

| Sr. No. | Item | Source | Submission Letter No | Approved Letter No | Remarks |
|---------|------------------------------|--|--|---|------------------------|
| 1 | Quality Assurance Plan (QAP) | M/s Patel Infrastructure Ltd | PSCHPL/SCP/IE/2018/019 | TES/IE/SC/PIL/2018/034 | Approved |
| 2 | Cement | M/s Ramco Cements Limited, Chennai. | PSCHPL/SCP/IE/2018/012 | TES/IE/SC/PIL/2018/005 | Approved |
| | | M/s Dalmia Bharat Cement, Ariyalur | PSCHPL/SCP/IE/2018/009 | TES/IE/SC/PIL/2018/006 | Approved |
| | | M/s Ultratech | PSCHPL/SCP/IE/2018/090 | TES/IE/SC/PIL/2018/060 | Approved |
| | | M/s India Cement (Coremendal) | PSCHPL/SCP/IE/2018/063 | TES/IE/SC/PIL/2018/040 | Approved |
| | | M/s Chettinad Cement, Chennai. | PSCHPL/SCP/IE/2018/009 | TES/IE/SC/PIL/2018/052 | Approved |
| | | M/s Barathi Cement | PSCHPL/SCP/IE/2018/154 | TES/IE/SC/PIL/2018/128 | Approved |
| 3 | Steel | M/s JSW Cement | PSCHPL/SCP/IE/2018/294 | TES/IE/SC/PIL/2018/257 | Approved |
| | | M/s Jindal Steel & Power Limited, New Delhi. | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/010 | Approved |
| | | M/s shyam Steel | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/016 | Approved |
| | | M/s Kamachi Industries limited, Chennai. | PSCHPL/SCP/IE/2018/301 | TES/IE/SC/PIL/2018/056 | Approved |
| | | M/s SAIL | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/173 | Approved |
| | | M/s VIZAG STEEL | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/173 | Approved |
| | | M/s Tata Steel Limited | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/173 | Approved |
| | | M/s Essar Steel Ltd | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/173 | Approved |
| | | M/s Electrosteel Steels Limited, | PSCHPL/SCP/IE/2018/202 | TES/IE/SC/PIL/2018/173 | Approved |
| 4 | HT strands | M/s Agarwal Foundries pvt Limited, | PSCHPL/SCP/IE/2019/516 | TES/IE/SC/PIL/2019/402 | Approved |
| | | M/s Usha Martin Limited | PSCHPL/SCP/IE/2018/286 | | Factory visit Required |
| | | M/s D.P.Wires Limited | PSCHPL/SCP/IE/2018/045 | | |
| 5 | Prestressing Agency | M/s Dynamic Prestressing India Pvt. Ltd | PSCHPL/SCP/IE/2018/059 | TES/IE/SC/PIL/2018/037 | Approved |
| 6 | Mechanical couplers | M/s Unitech couplers India (P) Ltd., Coimbatore. | PSCHPL/SCP/IE/2018/018 | TES/IE/SC/PIL/2018/009 | Approved |
| | | M/s Splicetek India Pvt Ltd., Mumbai. | PSCHPL/SCP/IE/2018/018 | | Factory visit Required |
| 7 | Chemical Admixture | M/s Fosroc, Bangalore | PSCHPL/SCP/IE/2018/008 | TES/IE/SC/PIL/2018/003 | Approved |
| | | M/s Kunal Conchem Pvt.Ltd, Faridabad | PSCHPL/SCP/IE/2018/008 | TES/IE/SC/PIL/2018/067 | Approved |
| | | M/s Rheoplast Technology Pvt. Ltd, Mumbai | PSCHPL/SCP/IE/2018/008 | TES/IE/SC/PIL/2018/066 | Approved |
| | | M/s BASF India Limited | PSCHPL/SCP/IE/2018/072 | TES/IE/SC/PIL/2018/042 | Approved |
| | | M/s Sika India Pvt Ltd, | PSCHPL/SCP/IE/2018/272 | TES/IE/SC/PIL/2018/234 | Approved |
| | | M/s B&B Specialities India Pvt Ltd, | PSCHPL/SCP/IE/2018/233 | TES/IE/SC/PIL/2018/179 | Approved |
| | | M/S CAC Pvt Ltd, | PSCHPL/SCP/IE/2018/219 | TES/IE/SC/PIL/2018/180 | Approved |
| 8 | Curing Compound | M/s CBS Chemicals, | PSCHPL/SCP/IE/2018/293 | TES/IE/SC/PIL/2018/256 | Approved |
| | | M/s Kunal Conchem Pvt.Ltd, Faridabad | PSCHPL/SCP/IE/2018/094 | TES/IE/SC/PIL/2018/067 | Approved |
| | | M/s CBS Chemicals Pvt.Ltd, Faridabad | PSCHPL/SCP/IE/2019/464 | TES/IE/SC/PIL/2019/369 | Approved |
| 9 | Emulsion | M/s Indian Oil Corporation | PSCHPL/SCP/IE/2018/061 | TES/IE/SC/PIL/2018/039 | Approved |
| | | M/s IWL India Limited | PSCHPL/SCP/IE/2018/073 | TES/IE/SC/PIL/2018/054 | Approved |
| | | M/s Hindustan Colas Private Limited | PSCHPL/SCP/IE/2018/062 | TES/IE/SC/PIL/2018/035 | Approved |
| | | M/s Ooms Polymer Modified Bitumen Pvt Ltd, | PSCHPL/SCP/IE/2018/314 | TES/IE/SC/PIL/2018/254 | Approved |
| | | M/s Tiki Tar and shell india pvt ltd | PSCHPL/SCP/IE/2020/674 | TES/IE/SC/PIL/2020/485 | Approved |
| 10 | Bitumen | M/s Indian Oil Corporation | PSCHPL/SCP/IE/2018/061 | TES/IE/SC/PIL/2018/039 | Approved |
| | | M/s Hindustan Colas Private Limited | PSCHPL/SCP/IE/2018/282 | TES/IE/SC/PIL/2018/0238 | Approved |
| | | M/s IWL India Limited | PSCHPL/SCP/IE/2018/073 | TES/IE/SC/PIL/2018/054 | Approved |
| | | M/s Tiki Tar industries, | PSCHPL/SCP/IE/2018/250 | TES/IE/SC/PIL/2018/0215 | Approved |

| | | | | | |
|----|---------------------------------|--|--|--|-----------------|
| | | M/s Ooms Polymer Modified Bitumen Pvt Ltd, (PMB) | PSCHPL/SCP/IE/2021/806 | <u>Factory visit Required</u> | |
| | | M/s BITCOL Corporation india Pvt.Ltd | PSCHPL/SCP/IE/2021/920 | TES/IE/SC/PIL/2021/611 | Approved |
| | | M/s Hincol (HCPL) PMB 70 H10 | PSCHPL/SCP/IE/2021/810 | TES/IE/SC/PIL/2021/557 | Approved |
| 11 | Mastic Asphalt | M/s IWL India Limited | PSCHPL/SCP/IE/2018/073 | TES/IE/SC/PIL/2018/053 | Approved |
| 12 | Micro Silica | M/s Elkem South Asia pvt Ltd, | PSCHPL/SCP/IE/2018/201 | TES/IE/SC/PIL/2018/170 | Approved |
| 13 | Anti Stripping | M/s HCPL & Tiki Tar Pvt Ltd, | PSCHPL/SCP/IE/2019/495 | TES/IE/SC/PIL/2019/384 | Approved |
| 14 | Micro Fine | M/s Suyag Elements India Pvt Ltd | PSCHPL/SCP/IE/2020/614 | TES/IE/SC/PIL/2020/449 | Approved |
| 15 | Expansion Joint | M/s Kantaflex India Pvt Ltd | PSCHPL/SCP/IE/2020/784 | TES/IE/SC/PIL/2021/544 | Approved |
| | | M/s Sanfield India Ltd | PSCHPL/SCP/IE/2020/781 | TES/IE/SC/PIL/2021/543 | Approved |
| | | M/s Hercules Structural Systems Pvt Ltd | PSCHPL/SCP/IE/2020/782 | TES/IE/SC/PIL/2021/545 | Approved |
| 16 | Road Marking | M/s Solucio iffrasolutions Pvt | PSCHPL/SCP/IE/2021/894 | TES/IE/SC/PIL/2021/607 | Approved |
| 17 | Metal Beam Crash Barrier | M/s Roadshield Pvt | PSCHPL/SCP/IE/2021/893 | TES/IE/SC/PIL/2021/608 | Approved |
| 18 | TRAFFIC SIGN BOARDS | M/s S.N.I Infratech Pvt Ltd | PSCHPL/SCP/IE/2020/744 | TES/IE/SC/PIL/2020/744 | Approved |
| 19 | Elastomeric Bearings | M/s Polymer Products Pvt Ltd | PSCHPL/SCP/IE/2020/595 | TES/IE/SC/PIL/2020/451 | Approved |
| | | M/s Sanfield India Ltd | PSCHPL/SCP/IE/2018/228,168 | TES/IE/SC/PIL/2019/205 | Approved |
| | | M/s Ammenji Rubber pvt Ltd | PSCHPL/SCP/IE/2018/144 | TES/IE/SC/PIL/2018/127 | Approved |
| 20 | Highway Lighting | M/s PCP Powers Pvt Ltd | PSCHPL/SCP/IE/2020/788 | TES/IE/SC/PIL/2021/542 | Approved |
| 21 | Road Studs | M/s 3M Indian Limited | PSCHPL/SCP/IE/2021/987 | | |

Four Laning of Sethiyahopu - Cholopuram from km 65.960 to km 116.440 section of NH-45C in the state of Tamilnadu under NHDP Phase-IV on Hybrid Annuity Mode.

CONSUMPTION OF BORROW AREA (UPTO 31/08/2023)

| Sr. No. | B/A NO. | Location | Lead From NH-45C | Side | Suitable For | Approved Qty In M ³ | Submission Letter No | Approved Letter No | Remarks |
|---------|---------|---------------------------------|------------------|------|----------------|--------------------------------|---|---|----------|
| 1 | 1 | Maruvay 61+090 | 1.5 km | LHS | EMB | 18000 | PSCHPL/SCP/IE/2018/093 | TES/IE/SCP/PIL/2018/059 | Approved |
| 2 | 1 | 61+090 LHS (Maruvai) EX - 01 | 1.5 km | LHS | EMB | 30000 | PSCHPL/SCP/IE/2020/656 | TES/IE/SC/PIL/2020/470 | Approved |
| 3 | 1 | 61+090 LHS (Maruvai) EX - 02 | 1.5 Km | LHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/656 | TES/IE/SC/PIL/2020/470 | Approved |
| 4 | 1 | 61+090 LHS (Maruvai) EX - 03 | 1.5km | LHS | EMB | 30000 | PSCHPL/SCP/IE/2020/670 | TES/IE/SC/PIL/2020/477 | Approved |
| 5 | 1 | 61+090 LHS (Maruvai) EX - 04 | 1.5km | LHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/679 | TES/IE/SC/PIL/2020/486 | Approved |
| 6 | 1 | 61+090 LHS (Maruvai) EX - 05 | 1.5km | LHS | EMB | 30000 | PSCHPL/SCP/IE/2020/679 | TES/IE/SC/PIL/2020/486 | Approved |
| 7 | 1 | 61+090 LHS (Maruvai) EX - 06 | 1.5km | LHS | EMB | 45000 | PSCHPL/SCP/IE/2020/683 | TES/IE/SC/PIL/2020/500 | Approved |
| 8 | 2 | 106+350 RHS Kodali | 4.0 km | RHS | EMB | 18000 | PSCHPL/SCP/IE/2018/084 | TES/IE/SCP/PIL/2018/061 | Approved |
| 9 | 2 | 106+350 RHS (Kodali) EX - 01 | 4.0 km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2020/670 | TES/IE/SC/PIL/2020/477 | Approved |
| 10 | 2 | 106+350 RHS (Kodali) EX - 02 | 4.0 km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2020/689 | TES/IE/SC/PIL/2020/490 | Approved |
| 11 | 3 | 113+250 LHS Paalur | 2.0 km | LHS | EMB | 15000 | PSCHPL/SCP/IE/2018/101 | TES/IE/SCP/PIL/2018/098 | Approved |
| 12 | 4 | 113+250 LHS Kattanakaram | 4.0 km | LHS | EMB | 15000 | PSCHPL/SCP/IE/2018/147 | TES/IE/SCP/PIL/2018/122 | Approved |
| 13 | 5 | 113+250 LHS Manikudi | 5.0 km | LHS | EMB | 15000 | PSCHPL/SCP/IE/2018/116 | TES/IE/SCP/PIL/2018/099 | Approved |
| 14 | 6 | 112+250 RHS Ammiyapan | 8.0 km | RHS | EMB | 15000 | PSCHPL/SCP/IE/2018/160 | TES/IE/SCP/PIL/2018/131 | Approved |
| 15 | 7 | 80+500 RHS Palayan kottai | 6.0 km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2018/160 | TES/IE/SCP/PIL/2018/129 | Approved |
| 16 | 7 | 80+500 RHS Palayan kottai EX-01 | 6.0 km | RHS | EMB | 60000 | PSCHPL/SCP/IE/2019/374 | TES/IE/SCP/PIL/2019/300 | Approved |
| 17 | 7 | 80+500 RHS Palayan kottai EX-02 | 6.0 km | RHS | EMB | 60000 | PSCHPL/SCP/IE/2019/396 | TES/IE/SCP/PIL/2019/315 | Approved |
| 18 | 7 | 80+500 RHS Palayan kottai EX-03 | 6.0 km | RHS | EMB & SUBGRADE | 60000 | PSCHPL/SCP/IE/2019/435 | TES/IE/SCP/PIL/2019/343 | Approved |
| 19 | 7 | 80+500 RHS Palayan kottai EX-04 | 6.0 km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/1005 | TES/IE/SC/PIL/2021/645 | Approved |
| 20 | 7 | 80+500 RHS Palayan kottai EX-05 | 6.0 km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2022/1083 | TES/IE/SC/PIL/2022/682 | Approved |

| | | | | | | | | | |
|----|----|----------------------------------|---------|-----|------------------------|-------|---|---|----------|
| 21 | 7 | 80+500 RHS Palayan kottai EX-06 | 6.0 km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2022/1101 | TES/IE/SC/PIL/2022/736 | Approved |
| 22 | 7 | 80+500 RHS Palayan kottai EX-07 | 6.0 km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2022/1107 | TES/IE/SC/PIL/2022/724 | Approved |
| 23 | 7 | 80+500 RHS Palayan kottai EX-08 | 6.0 km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2023/1449 | TES/IE/SC/PIL/2023/877 | Approved |
| 24 | 7 | 80+500 RHS Palayan kottai EX-09 | 6.0 km | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1685 | TES/IE/SC/PIL/2023/952 | Approved |
| 25 | 8 | 98+950 RHS Ponnery | 5.0 km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2019/302 | TES/IE/SCP/PIL/2019/247 | Approved |
| 26 | 8 | 98+950 RHS Ponnery EX-01 | 5.0 km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2019/488 | TES/IE/SCP/PIL/2019/386 | Approved |
| 27 | 9 | 106+320 RHS (Uthayanatham) | 3.0 km | RHS | EMB | 25500 | PSCHPL/SCP/IE/2019/302 | TES/IE/SCP/PIL/2019/247 | Approved |
| 28 | 9 | 106+320 RHS (Uthayanatham EX-01) | 3.0 km | RHS | EMB | 15000 | PSCHPL/SCP/IE/2019/472 | TES/IE/SCP/PIL/2019/365 | Approved |
| 29 | 10 | 96+600 LHS (Pandianeery) | 3.0 km | LHS | EMB | 34500 | PSCHPL/SCP/IE/2019/302 | TES/IE/SCP/PIL/2019/247 | Approved |
| 30 | 10 | 96+600 LHS (Pandianeery) EX-01 | 3.0 km | LHS | EMB | 30000 | PSCHPL/SCP/IE/2019/345 | TES/IE/SCP/PIL/2018/268 | Approved |
| 31 | 10 | 96+600 LHS (Pandianeery) EX-02 | 3.0 km | LHS | EMB & RE WALL | 18000 | PSCHPL/SCP/IE/2021/950 | TES/IE/SC/PIL/2021/630 | Approved |
| 32 | 11 | 88+550 (Kaduvetti) | 1.0 Km | LHS | EMB | 25500 | PSCHPL/SCP/IE/2019/335 | | Approved |
| 33 | 11 | 88+550 (Kaduvetti) EX - 01 | 1.0 Km | LHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2019/352 | TES/IE/SCP/PIL/2019/280 | Approved |
| 34 | 12 | 90+500 Puthueary | 7.0 Km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2019/390 | TES/IE/SCP/PIL/2019/307 | Approved |
| 35 | 12 | 90+500 Puthueary EX-01 | 7.0 Km | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2019/510 | | |
| 36 | 12 | 90+500 Puthueary EX-02 | 7.0 Km | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/750 | | |
| 37 | 13 | 87+900 Andi Madam | 12.0 Km | RHS | Using For Filter Media | | | | |
| 38 | 14 | 87+900 Vilanthai | 8.0 km | RHS | | | | | |
| 39 | 15 | 87+600 Velaneary | 4.0 km | RHS | EMB | 18000 | PSCHPL/SCP/IE/2019/387 | TES/IE/SCP/PIL/2019/302 | Approved |
| 40 | 16 | 82+900 Aandi Palayam | 2.0 Km | RHS | EMB | 18000 | PSCHPL/SCP/IE/2019/381 | TES/IE/SCP/PIL/2019/299 | Approved |
| 41 | 16 | 82+900 Aandi Palayam EX-01 | 2.0 Km | RHS | RE WALL | 36000 | PSCHPL/SCP/IE/2019/501 | TES/IE/SC/PIL/2019/390 | Approved |
| 42 | 16 | 82+900 Aandi Palayam EX-02 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2020/758 | TES/IE/SC/PIL/2020/528 | Approved |
| 43 | 16 | 82+900 Aandi Palayam EX-03 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2021/937 | TES/IE/SC/PIL/2021/626 | Approved |

| | | | | | | | | | |
|----|----|-------------------------------|--------|-----|--------------------|-------|---|--|----------|
| 44 | 16 | 82+900 Aandi Palayam EX-04 | 2.0 Km | RHS | SUBGRADE & RE WALL | 45000 | PSCHPL/SCP/IE/2021/977 | TES/IE/SC/PIL/2021/637 | Approved |
| 45 | 16 | 82+900 Aandi Palayam EX-05 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1126 | TES/IE/SC/PIL/2022/740 | Approved |
| 46 | 16 | 82+900 Aandi Palayam EX-06 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1139 | TES/IE/SC/PIL/2022/749 | Approved |
| 47 | 16 | 82+900 Aandi Palayam EX-07 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1217 | TES/IE/SC/PIL/2022/797 | Approved |
| 48 | 16 | 82+900 Aandi Palayam EX-08 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2023/1418 | TES/IE/SC/PIL/2023/866 | Approved |
| 49 | 16 | 82+900 Aandi Palayam EX-08 | 2.0 Km | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2023/1619 | TES/IE/SC/PIL/2023/933 | Approved |
| 50 | 17 | 94+400 kundaveli East | 1.0 Km | LHS | EMB | 30000 | PSCHPL/SCP/IE/2019/408 | TES/IE/SC/PIL/2019/320 | Approved |
| 51 | 18 | 83+000 Vanamadevi | 1.0 Km | LHS | EMB | 15000 | PSCHPL/SCP/IE/2019/397 | TES/IE/SC/PIL/2019/314 | Approved |
| 52 | 19 | 101+900 Thaluthalai Medu | 1.0 Km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2019/422 | TES/IE/SC/PIL/2019/355 | Approved |
| 53 | 20 | 110+100 Athipakkam | 6.0 km | RHS | EMB | 15000 | PSCHPL/SCP/IE/2019/452 | TES/IE/SC/PIL/2019/354 | Approved |
| 54 | 21 | 103+200 Vembankudi | 0.5 Km | LHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2019/463 | TES/IE/SC/PIL/2019/362 | Approved |
| 55 | 21 | 103+200 Vembankudi EX-01 | 0.5 Km | LHS | SUBGRADE & RE WALL | 22500 | PSCHPL/SCP/IE/2020/717 | TES/IE/SC/PIL/2020/504 | Approved |
| 56 | 21 | 103+200 Vembankudi EX-02 | 0.5 Km | LHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2020/775 | TES/IE/SC/PIL/2020/538 | Approved |
| 57 | 22 | 97+300 Muthuservamadam | 2.0 Km | RHS | EMB | 30000 | PSCHPL/SCP/IE/2019/447 | TES/IE/SC/PIL/2019/349 | Approved |
| 58 | 23 | 80+500 Kandiyankuppam | 15.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2019/561 | TES/IE/SC/PIL/2019/418 | Approved |
| 59 | 23 | 80+500 Kandiyankuppam EX - 01 | 15.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/626 | TES/IE/SC/PIL/2020/452 | Approved |
| 60 | 23 | 80+500 Kandiyankuppam EX - 02 | 15.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/812 | TES/IE/SC/PIL/2021/555 | Approved |
| 61 | 23 | 80+500 Kandiyankuppam EX - 03 | 15.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/845 | TES/IE/SC/PIL/2021/576 | Approved |
| 62 | 24 | 106+900 Karaikuruchi | 20.00 | RHS | EMB | 15000 | PSCHPL/SCP/IE/2020/636 | TES/IE/SC/PIL/2020/453 | Approved |
| 63 | 24 | 106+900 Karaikuruchi EX - 01 | 20.00 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/691 | TES/IE/SC/PIL/2020/491 | Approved |
| 64 | 24 | 106+900 Karaikuruchi EX - 02 | 20.00 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/961 | TES/IE/SC/PIL/2021/632 | Approved |
| 65 | 24 | 106+900 Karaikuruchi EX - 03 | 20.00 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/1018 | TES/IE/SC/PIL/2021/654 | Approved |

| | | | | | | | | | |
|----|----|----------------------------------|-------|-----|--------------------|-------|---|--|----------|
| 66 | 25 | 90+500 RHS (IDAIPALLAM) | 6.00 | LHS | EMB | 15000 | PSCHPL/SCP/IE/2020/637 | TES/IE/SC/PIL/2020/454 | Approved |
| 67 | 25 | 90+500 RHS (IDAIPALLAM) EX-01 | 6.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/640 | TES/IE/SC/PIL/2020/469 | Approved |
| 68 | 26 | 98+900 LHS (kommedu) | 19.00 | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2020/661 | TES/IE/SC/PIL/2020/472 | Approved |
| 69 | 27 | 91+400RHS (pappakudi) | 0.80 | RHS | EMB | 15000 | PSCHPL/SCP/IE/2020/657 | TES/IE/SC/PIL/2020/471 | Approved |
| 70 | 28 | 92+600 RHS Chokalingapuram | 0.70 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/676 | TES/IE/SC/PIL/2020/471 | Approved |
| 71 | 28 | 92+600 RHS Chokalingapuram EX-01 | 0.70 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/838 | TES/IE/SC/PIL/2020/568 | Approved |
| 72 | 28 | 92+600 RHS Chokalingapuram EX-02 | 0.70 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2022/1165 | TES/IE/SC/PIL/2022/779 | Approved |
| 73 | 29 | 90+580 RHS Irudhayapuram | 10.00 | RHS | EMB | 15000 | PSCHPL/SCP/IE/2020/711 | TES/IE/SC/PIL/2020/501 | Approved |
| 74 | 30 | 80+500 RHS Keelpathi | 6.00 | RHS | EMB & SUBGRADE | 15000 | PSCHPL/SCP/IE/2020/711 | TES/IE/SC/PIL/2020/501 | Approved |
| 75 | 30 | 80+500 RHS Keelpathi EX - 1 | 6.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/926 | TES/IE/SC/PIL/2021/618 | Approved |
| 76 | 30 | 80+500 RHS Keelpathi EX - 2 | 6.00 | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2021/927 | TES/IE/SC/PIL/2021/619 | Approved |
| 77 | 31 | 87+600 RHS Thirukalappur | 10.00 | RHS | SUBGRADE | 30000 | PSCHPL/SCP/IE/2020/717 | TES/IE/SC/PIL/2020/504 | Approved |
| 78 | 32 | 106+300 RHS Keelnatham | 35.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2020/725 | TES/IE/SC/PIL/2020/505 | Approved |
| 79 | 33 | 87+600 RHS Thathur | 10.00 | RHS | EMB & RE WALL | 30000 | PSCHPL/SCP/IE/2020/736 | TES/IE/SC/PIL/2020/511 | Approved |
| 80 | 35 | 115+250 RHS KADAMPANKUDI | 6.00 | RHS | EMB & RE WALL | 30000 | PSCHPL/SCP/IE/2020/812 | | |
| 81 | 36 | Thirukalapur kuppam | 7.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2020/838 | TES/IE/SC/PIL/2020/569 | Approved |
| 82 | 36 | Thirukalapur kuppam Ex - 1 | 7.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2021/887 | TES/IE/SC/PIL/2021/598 | Approved |
| 83 | 36 | Thirukalapur kuppam Ex - 2 | 7.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2021/936 | TES/IE/SC/PIL/2021/625 | Approved |
| 84 | 37 | Manaimedu(109+350) | 10.00 | RHS | EMB | 18000 | PSCHPL/SCP/IE/2021/844 | TES/IE/SC/PIL/2021/574 | Approved |
| 85 | 38 | Melur (98+900) | 18.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2021/847 | TES/IE/SC/PIL/2021/578 | Approved |
| 86 | 38 | Melur (98+900) EX - 1 | 18.00 | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2021/886 | TES/IE/SC/PIL/2021/599 | Approved |
| 87 | 39 | Thirukalapur South (87+600) | 10.00 | RHS | EMB | 18000 | PSCHPL/SCP/IE/2021/853 | TES/IE/SC/PIL/2021/584 | Approved |
| 88 | 40 | Kaduvetti (88+750) | 0.5KM | RHS | EMB & RE WALL | 30000 | PSCHPL/SCP/IE/2021/954 | TES/IE/SC/PIL/2021/631 | Approved |
| 89 | 41 | Simustnam | 17KM | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1062 | TES/IE/SC/PIL/2022/669 | Approved |

| | | | | | | | | | |
|---|----|-------------------|------|-----|--------------------|---------|---|--|----------|
| 90 | 41 | Simustnam (ex-01) | 17KM | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1086 | TES/IE/SC/PIL/2022/686 | Approved |
| 91 | 41 | Simustnam (ex-02) | 17KM | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1102 | TES/IE/SC/PIL/2022/717 | Approved |
| 92 | 41 | Simustnam (ex-03) | 17KM | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1118 | TES/IE/SC/PIL/2022/784 | Approved |
| 93 | 41 | Simustnam (ex-04) | 17KM | RHS | SUBGRADE & RE WALL | 30000 | PSCHPL/SCP/IE/2022/1201 | TES/IE/SC/PIL/2022/803 | Approved |
| 94 | 42 | Silal | 12KM | RHS | EMB | 18000 | PSCHPL/SCP/IE/2022/1139 | TES/IE/SC/PIL/2022/746 | Approved |
| 95 | 43 | Kodangudi | 44KM | RHS | EMB & SUBGRADE | 30000 | PSCHPL/SCP/IE/2022/1170 | TES/IE/SC/PIL/2022/783 | Approved |
| 96 | 44 | Stahampadi | 41KM | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1300 | TES/IE/SC/PIL/2023/828 | Approved |
| 97 | 44 | Stahampadi EX-01 | 41KM | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1571 | TES/IE/SC/PIL/2023/915 | Approved |
| 98 | 45 | Suthamalli | 43KM | RHS | EMB | 30000 | PSCHPL/SCP/IE/2023/1376 | TES/IE/SC/PIL/2023/850 | Approved |
| 99 | 45 | Suthamalli EX-01 | 43KM | RHS | EMB | 30000 | PSCHPL/SCP/IE/2023/1473 | TES/IE/SC/PIL/2023/888 | Approved |
| 100 | 46 | Kulathoor | 24KM | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1498 | TES/IE/SC/PIL/2023/889 | Approved |
| 101 | 47 | Paravathipuram | 3KM | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1506 | TES/IE/SC/PIL/2023/891 | Approved |
| 102 | 48 | Vikramangalam | 48KM | RHS | RE WALL | 30000 | PSCHPL/SCP/IE/2023/1660 | TES/IE/SC/PIL/2023/949 | Approved |
| TOTAL QTY EMB M ³ | | | | | | 961500 | | | |
| TOTAL QTY SUBGRADE M ³ | | | | | | 180000 | | | |
| TOTAL QTY EMB & SUBGRADE M ³ | | | | | | 645000 | | | |
| TOTAL QTY RE WALL M ³ | | | | | | 276000 | | | |
| TOTAL QTY SUBGRADE & RE WALL M ³ | | | | | | 667500 | | | |
| TOTAL EMB & RE WALL M ³ | | | | | | 108000 | | | |
| TOTAL QTY M ³ | | | | | | 2838000 | | | |

| FLYASH CONSUMPTION (UPTO 31/08/2023) | | | | | | | | | |
|--------------------------------------|----|--------------|-------|-----|---------|-------|---|--|----------|
| 1 | 1 | FLYASH EX-01 | 30 Km | LHS | RE WALL | 25500 | PSCHPL/SCP/IE/2018/122 | TES/IE/SC/PIL/2018/101 | Approved |
| 2 | 2 | FLYASH EX-02 | 30 Km | LHS | | 25500 | PSCHPL/SCP/IE/2019/303 | TES/IE/SC/PIL/2019/255 | Approved |
| 3 | 3 | FLYASH EX-03 | 30 Km | LHS | | 30000 | | | Approved |
| 4 | 4 | FLYASH EX-04 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2019/448 | TES/IE/SC/PIL/2019/350 | Approved |
| 5 | 5 | FLYASH EX-05 | 30 Km | LHS | | 45000 | PSCHPL/SCP/IE/2019/489 | TES/IE/SC/PIL/2019/385 | Approved |
| 6 | 6 | FLYASH EX-06 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2019/518 | TES/IE/SC/PIL/2019/400 | Approved |
| 7 | 7 | FLYASH EX-07 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2019/570 | TES/IE/SC/PIL/2019/430 | Approved |
| 8 | 8 | FLYASH EX-08 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2019/571 | TES/IE/SC/PIL/2019/431 | Approved |
| 9 | 9 | FLYASH EX-09 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2020/728 | TES/IE/SC/PIL/2020/512 | Approved |
| 10 | 10 | FLYASH EX-10 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2020/761 | TES/IE/SC/PIL/2020/527 | Approved |
| 11 | 11 | FLYASH EX-11 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/814 | TES/IE/SC/PIL/2021/554 | Approved |
| 12 | 12 | FLYASH EX-12 | 31 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/828 | TES/IE/SC/PIL/2021/558 | Approved |
| 13 | 13 | FLYASH EX-13 | 30 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/846 | TES/IE/SC/PIL/2021/577 | Approved |
| 14 | 14 | FLYASH EX-14 | 31 Km | LHS | | 30000 | | | |
| 15 | 15 | FLYASH EX-15 | 31 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/919 | TES/IE/SC/PIL/2021/613 | Approved |
| 16 | 16 | FLYASH EX-16 | 32 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/917 | TES/IE/SC/PIL/2021/612 | Approved |
| 17 | 17 | FLYASH EX-17 | 32 Km | LHS | | 30000 | PSCHPL/SCP/IE/2021/949 | TES/IE/SC/PIL/2021/629 | Approved |
| 18 | 18 | FLYASH EX-18 | 32 Km | LHS | | 45000 | PSCHPL/SCP/IE/2021/960 | TES/IE/SC/PIL/2021/633 | Approved |
| 19 | 19 | FLYASH EX-19 | 32 Km | LHS | | 60000 | PSCHPL/SCP/IE/2021/964 | TES/IE/SC/PIL/2021/634 | Approved |
| 20 | 20 | FLYASH EX-20 | 32 Km | LHS | | 45000 | PSCHPL/SCP/IE/2022/1092 | TES/IE/SC/PIL/2022/690 | Approved |
| 21 | 21 | FLYASH EX-21 | 32 Km | LHS | | 30000 | PSCHPL/SCP/IE/2023/1371 | TES/IE/SC/PIL/2023/846 | Approved |
| 22 | 22 | FLYASH EX-22 | 32 Km | LHS | | 45000 | PSCHPL/SCP/IE/2023/1587 | TES/IE/SC/PIL/2023/932 | Approved |

7. Weather Report - Meensurutti

| Date | Temperature (Celsius) | | Humidity (%) | | Rainfall (mm) | Remarks |
|-------------|-----------------------|------|--------------|-----|---------------|---------|
| | Max | Min | Max | Min | | |
| 1-Aug-2023 | 37.9 | 31.3 | 62 | 50 | 0.00 | Sunny |
| 2-Aug-2023 | 38.2 | 30.4 | 61 | 49 | 0.00 | Sunny |
| 3-Aug-2023 | 39.4 | 31.5 | 58 | 47 | 0.00 | Sunny |
| 4-Aug-2023 | 38.7 | 31.7 | 61 | 46 | 0.00 | Sunny |
| 5-Aug-2023 | 37.2 | 29.9 | 65 | 47 | 0.00 | Sunny |
| 6-Aug-2023 | 38.1 | 30.1 | 66 | 45 | 7.00 | Rainy |
| 7-Aug-2023 | 38.8 | 29.5 | 73 | 42 | 0.00 | Sunny |
| 8-Aug-2023 | 39.3 | 29.8 | 69 | 40 | 10.00 | Rainy |
| 9-Aug-2023 | 39.4 | 29.6 | 72 | 43 | 55.00 | Rainy |
| 10-Aug-2023 | 33.1 | 28.2 | 78 | 56 | 0.00 | Cloudy |
| 11-Aug-2023 | 37.8 | 28.5 | 79 | 40 | 15.00 | Rainy |
| 12-Aug-2023 | 35.2 | 28.1 | 76 | 44 | 22.00 | Rainy |
| 13-Aug-2023 | 36.3 | 27.5 | 80 | 46 | 0.00 | Sunny |
| 14-Aug-2023 | 37.1 | 28.3 | 77 | 42 | 0.00 | Sunny |
| 15-Aug-2023 | 37.7 | 30.0 | 65 | 43 | 0.00 | Sunny |
| 16-Aug-2023 | 38.2 | 29.4 | 63 | 41 | 0.00 | Sunny |
| 17-Aug-2023 | 38.9 | 29.9 | 71 | 42 | 0.00 | Sunny |
| 18-Aug-2023 | 39.7 | 30.5 | 65 | 44 | 0.00 | Sunny |
| 19-Aug-2023 | 40.1 | 29.9 | 61 | 42 | 0.00 | Sunny |
| 20-Aug-2023 | 40.2 | 31.1 | 60 | 40 | 0.00 | Sunny |
| 21-Aug-2023 | 38.9 | 30.1 | 66 | 44 | 0.00 | Sunny |
| 22-Aug-2023 | 39.2 | 29.8 | 75 | 40 | 0.00 | Sunny |
| 23-Aug-2023 | 40.1 | 29.6 | 73 | 38 | 0.00 | Sunny |
| 24-Aug-2023 | 39.7 | 30.4 | 64 | 44 | 0.00 | Sunny |
| 25-Aug-2023 | 38.2 | 30.2 | 66 | 42 | 0.00 | Sunny |
| 26-Aug-2023 | 39.7 | 31.3 | 67 | 40 | 0.00 | Sunny |
| 27-Aug-2023 | 38.6 | 30.2 | 70 | 44 | 0.00 | Sunny |
| 28-Aug-2023 | 39.8 | 29.0 | 75 | 50 | 0.00 | Sunny |
| 29-Aug-2023 | 40.1 | 29.7 | 66 | 48 | 61.00 | Rainy |
| 30-Aug-2023 | 38.7 | 28.4 | 79 | 47 | 8.00 | Rainy |
| 31-Aug-2023 | 38.2 | 27.5 | 76 | 42 | 0.00 | Sunny |

Weather Report - Annakarai

| Date | Temperature (Celsius) | | Humidity (%) | | Rainfall (mm) | Remarks |
|-------------|-----------------------|------|--------------|-----|---------------|---------|
| | Max | Min | Max | Min | | |
| 1-Aug-2023 | 37.4 | 31.1 | 64 | 51 | 0.00 | Sunny |
| 2-Aug-2023 | 38.1 | 30.2 | 60 | 48 | 0.00 | Sunny |
| 3-Aug-2023 | 39.4 | 31.7 | 59 | 49 | 0.00 | Sunny |
| 4-Aug-2023 | 38.6 | 31.6 | 62 | 47 | 0.00 | Sunny |
| 5-Aug-2023 | 37.4 | 29.8 | 66 | 51 | 0.00 | Sunny |
| 6-Aug-2023 | 38.2 | 30.7 | 64 | 46 | 0.00 | Sunny |
| 7-Aug-2023 | 38.9 | 29.6 | 70 | 48 | 0.00 | Sunny |
| 8-Aug-2023 | 39.4 | 29.4 | 66 | 44 | 10.00 | Rainy |
| 9-Aug-2023 | 39.6 | 29.2 | 70 | 42 | 53.00 | Rainy |
| 10-Aug-2023 | 33.4 | 28.4 | 77 | 54 | 0.00 | Cloudy |
| 11-Aug-2023 | 37.5 | 28.6 | 78 | 42 | 17.00 | Rainy |
| 12-Aug-2023 | 35.4 | 28.3 | 76 | 43 | 24.00 | Rainy |
| 13-Aug-2023 | 36.3 | 27.5 | 77 | 45 | 0.00 | Sunny |
| 14-Aug-2023 | 37.4 | 28.5 | 74 | 43 | 0.00 | Sunny |
| 15-Aug-2023 | 37.6 | 30.2 | 69 | 41 | 0.00 | Sunny |
| 16-Aug-2023 | 38.4 | 29.1 | 66 | 40 | 0.00 | Sunny |
| 17-Aug-2023 | 38.7 | 29.7 | 74 | 42 | 0.00 | Sunny |
| 18-Aug-2023 | 39.7 | 30.4 | 67 | 44 | 0.00 | Sunny |
| 19-Aug-2023 | 40.3 | 29.7 | 62 | 43 | 0.00 | Sunny |
| 20-Aug-2023 | 40.8 | 31.2 | 64 | 44 | 0.00 | Sunny |
| 21-Aug-2023 | 38.7 | 30.4 | 66 | 41 | 0.00 | Sunny |
| 22-Aug-2023 | 39.4 | 29.7 | 74 | 40 | 0.00 | Sunny |
| 23-Aug-2023 | 40.2 | 29.4 | 72 | 39 | 0.00 | Sunny |
| 24-Aug-2023 | 39.6 | 30.2 | 66 | 41 | 0.00 | Sunny |
| 25-Aug-2023 | 38.4 | 30.3 | 67 | 40 | 0.00 | Sunny |
| 26-Aug-2023 | 39.6 | 31.2 | 65 | 41 | 0.00 | Sunny |
| 27-Aug-2023 | 38.7 | 30.4 | 69 | 42 | 0.00 | Sunny |
| 28-Aug-2023 | 39.6 | 29.4 | 73 | 49 | 0.00 | Sunny |
| 29-Aug-2023 | 40.4 | 29.6 | 64 | 46 | 65.00 | Rainy |
| 30-Aug-2023 | 38.4 | 28.2 | 77 | 47 | 0.00 | Sunny |
| 31-Aug-2023 | 38.5 | 27.4 | 74 | 40 | 0.00 | Sunny |

8. Safety

- Various issues related to environment and safety, such as traffic management, safety signage, disposal of waste materials and oil spillage, housekeeping and area barricading etc, are being taken care during the execution of the project.

Periodic Safety meetings are being conducted on a regular basis and the details of the photographs for the same along with action taken are as below:-



Safety reflective stickers pasting at Km. 80+550

9. Support required from NHAI

Concessionaire requests NHAI to take early action on the following issues:-

1. Additional land acquisition for the construction of bus bays/bus shelter, turning radius of major junctions along the project highways.
2. Insufficient Right of Way with respect to the land handed over as per Clause 10.3.1 of Concession Agreement at the time of Signing of Joint Memorandum.
3. NOC from PWD/WRO, Govt. of Tamil Nadu for the construction of project highways in the existing pond locations as mentioned below in the tabular form:-

| SI No | Chainage | | Length Affected (M) | Side | AVG Toe Width from CL "A" | Width/distance of Pond Edge from CL "C" |
|--------------|----------|---------|---------------------|------|---------------------------|---|
| | From | To | | | | |
| 1 | 75+557 | 75+632 | 74.75 | RHS | 32.50 | 7.00 |
| 2 | 77+330 | 77+400 | 70.00 | LHS | 28.16 | 3.00 |
| 3 | 80+396 | 80+415 | 19.00 | LHS | 27.00 | 7.00 |
| 4 | 80+400 | 80+423 | 23.00 | RHS | 24.00 | 6.50 |
| 5 | 97+376 | 97+535 | 159.00 | RHS | 32.67 | 11.00 |
| 6 | 100+350 | 100+389 | 39.00 | LHS | 22.70 | 4.00 |
| 7 | 103+039 | 103+056 | 17.60 | LHS | 23.00 | 6.60 |
| 8 | 103+125 | 103+360 | 235.00 | LHS | 23.00 | 6.00 |
| 9 | 104+091 | 104+262 | 171.00 | RHS | 23.00 | 16.80 |
| 10 | 103+992 | 104+264 | 271.50 | LHS | 23.00 | 10.90 |
| TOTAL | | | 1079.85 | | | |

4. Removal/relocation of existing irrigation sluice and regulator at the following locations:-

| Sl. No. | Chainage | Distance from PCL | Remarks/Action to be taken | Present Status |
|---------|----------|-------------------|-------------------------------|--|
| 1 | 81+850 | 9.3m | To be shifted to edge of PROW | Deposit Amount remitted to PWD/WRO. Work in progress |
| 2 | 81+870 | 1.8m | To be shifted to edge of PROW | |
| 3 | 81+910 | 1.8m | To be shifted to edge of PROW | |
| 4 | 82+010 | 1.8m | To be shifted to edge of PROW | |
| 5 | 82+100 | 7.4m | To be shifted to edge of PROW | |

5. Estimate for shifting of water supply utilities in Missing locations-Request Authority for earlier Approval.
6. Unprecedented/Unseasonal heavy rainfall within the project alignment affecting the construction activities and progress of work at site.

10. Important Events

Table 10.1. Details of Important Events


| Sl. No | Date of Events | Description of Events | Remarks |
|--------|----------------|---|---------|
| 1 | 18.08.2023 | Environmental Advisor, NHAI. HQ- Site visit | |
| 2 | 22.08.2023 | The General Manager (Tech) & Project Director, PIU, Thanjavur- Site visit | |

11. Organization Chart


The following figures represents the organization chart of the EPC and SPV Team.

1. Fig. 4 - Organization Chart - EPC Team
2. Fig. 5 - Organization Chart - SPV Team

ORGANIZATION CHART - EPC TEAM

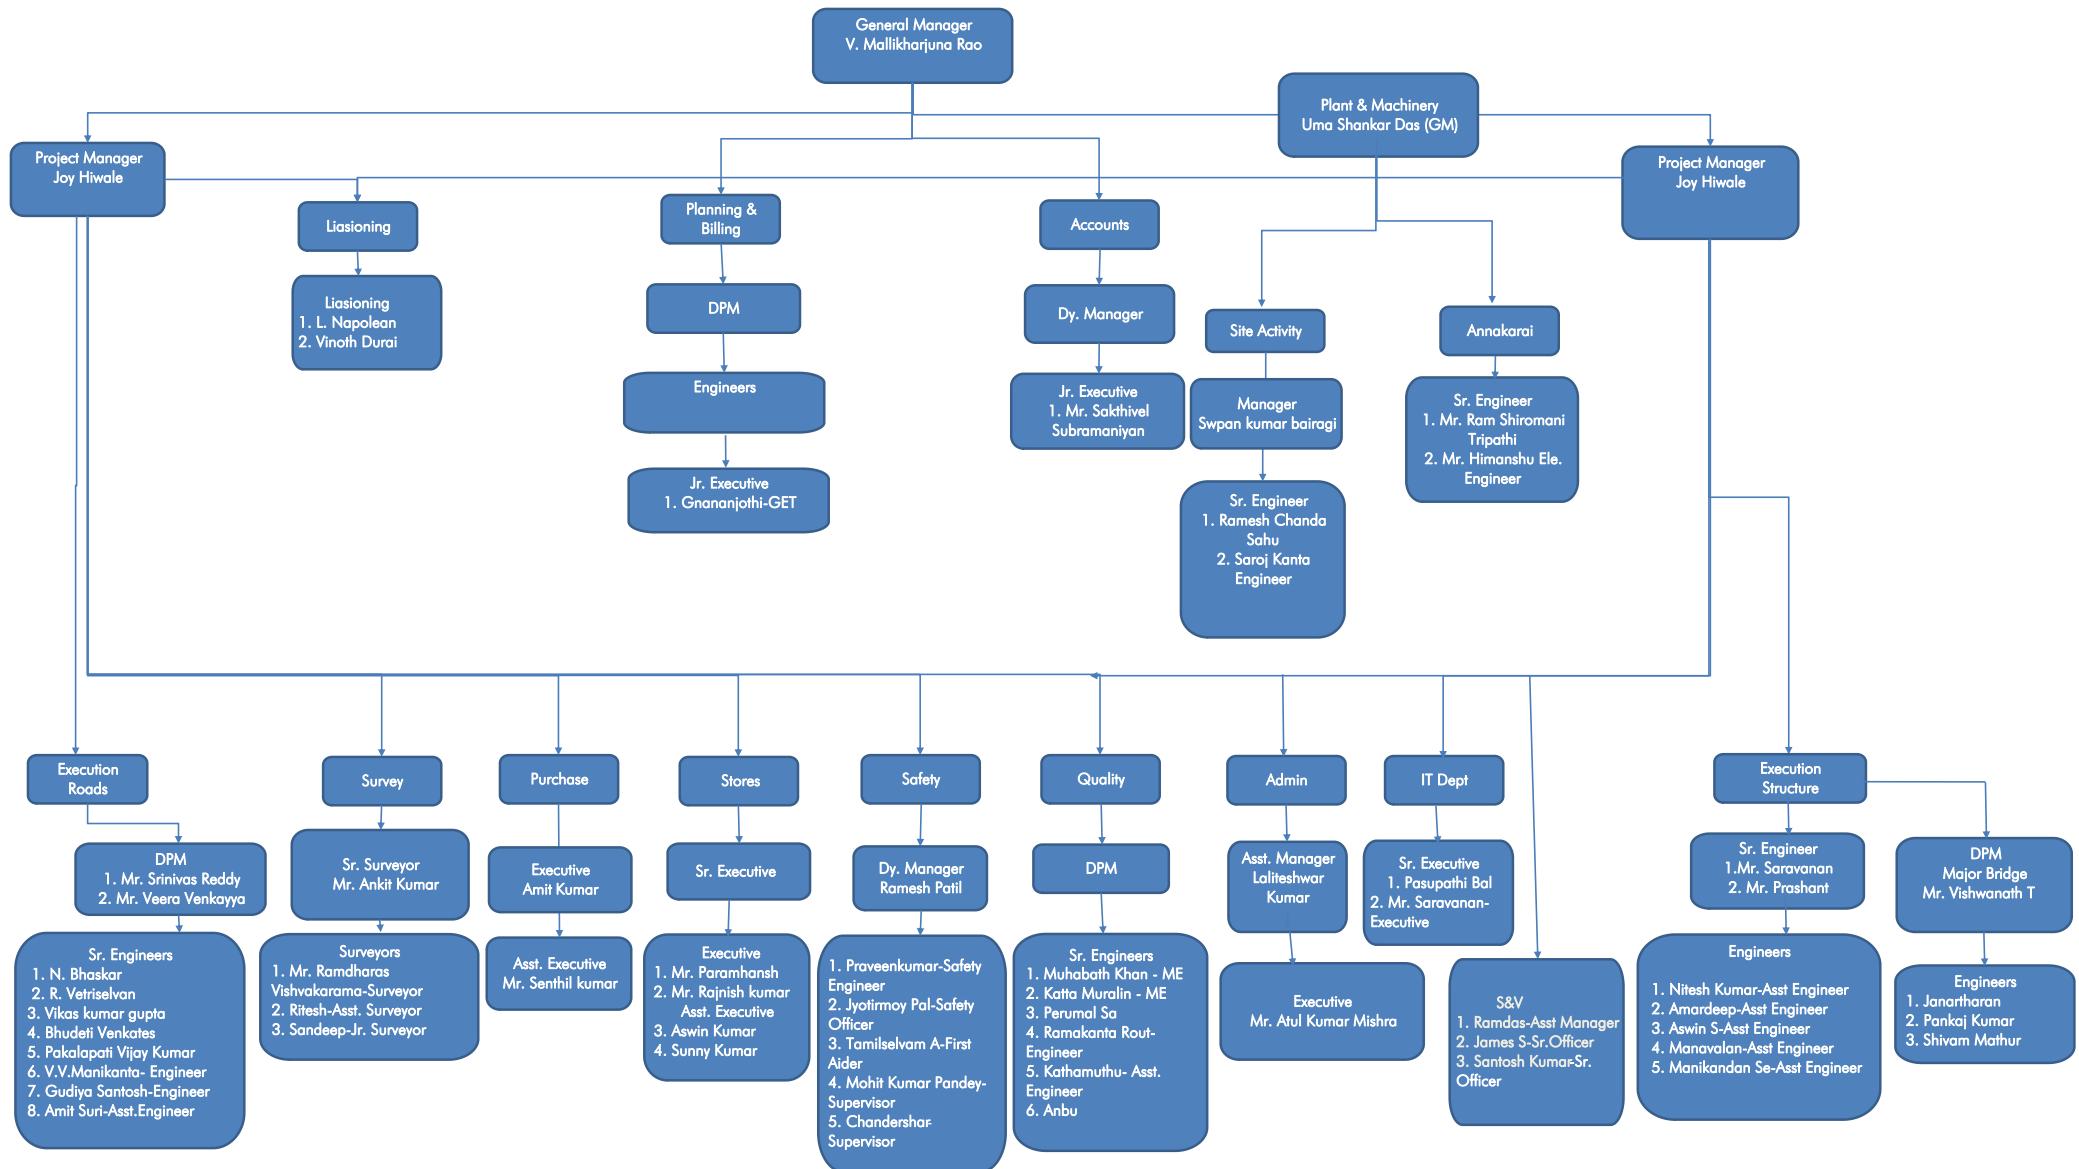

ORGANIZATION CHART - SPV TEAM

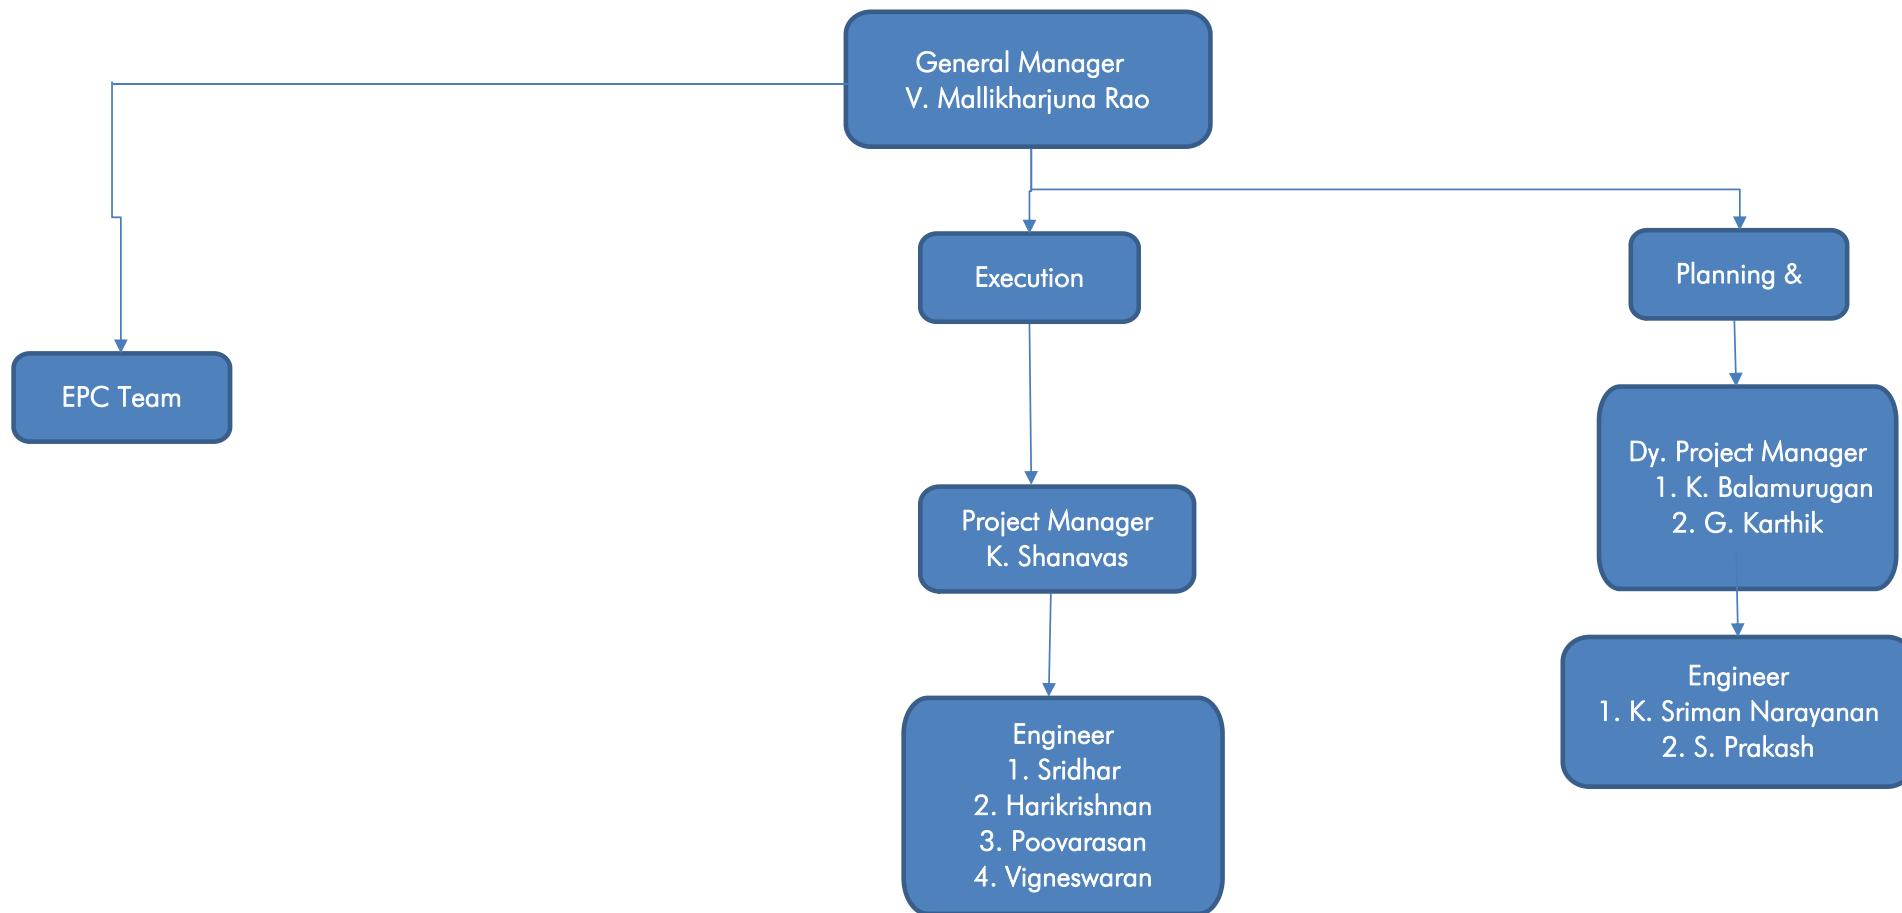

12. Manpower details

Table 12.1 Mobilization of Manpower

| Sr. No. | Department | Manager | Engineer / Executive | Supervisor / Technician / Helper | Total | Remarks |
|---------|--------------------------|---------|----------------------|----------------------------------|-------|---------|
| A1 | GENERAL MANAGER | 2 | | | 2 | |
| A2 | SR/ PROJECT MANAGER | 2 | | | 2 | |
| B | Project Management | | | | | |
| B.1 | Planning & Billing | 4 | 5 | | 9 | |
| B.2 | HR & Administration | 1 | 1 | | 2 | |
| B.3 | Accounts | 1 | | | 1 | |
| B.4 | Safety | 1 | 1 | 3 | 5 | |
| B.5 | QA / QC | 1 | 5 | 1 | 7 | |
| B.6 | Legal & Liasioning | 1 | 2 | | 3 | |
| B.7 | Purchase | 1 | 1 | | 2 | |
| B.8 | Store | | 13 | 4 | 17 | |
| B.9 | Plant & Equipment | 4 | 9 | 243 | 256 | |
| B.10 | Facility & House Keeping | | | 10 | 10 | |
| C | Project Execution | | | | | |
| C.1 | Road | 1 | 13 | 6 | 20 | |
| C.2 | Structures | 2 | 7 | 7 | 16 | |
| C.3 | Survey | 1 | 2 | 2 | 5 | |
| D | Labours | | | 171 | 171 | |
| | Grand Total | 22 | 59 | 447 | 528 | |

13. List of Plants, Machinery and Equipment's

Table 13.1 - List of Plants, Machinery and Equipment's

| Sr. No. | Name of the Machinery | Capacity / Model | Mobilized in Nos. | Remarks |
|---------|-------------------------------------|--------------------|-------------------|---------|
| 1 | Grader | 120K2 | 5 | |
| 2 | Excavator | JCB-220 | 8 | |
| 3 | Dozer | | 4 | |
| 4 | Soil Compactor | HAMM 311 | 7 | |
| 5 | Backhoe Loader | JCB 3DX | 8 | |
| 6 | Tipper | Bharat Benz- 3128C | 310 | |
| 7 | Transit Mixture | 2523C | 9 | |
| 8 | Loader | 455 ZX | 7 | |
| 9 | Trailer | | 2 | |
| 10 | Diesel Tanker | | 2 | |
| 11 | Kerb Laying machine | | 1 | |
| 12 | Light Moving Vehicles/Car/Jeep/Vans | | 30 | |
| 13 | Milling Machine | | 1 | |
| 14 | PT Roller | | 1 | |
| 15 | Tandem Roller | | 3 | |
| 16 | Water Tanker | | 9 | |
| 17 | Boom Placer | S-36 | 1 | |
| 18 | Baby Roller | VMT-330 | 2 | |
| 19 | Bitumen Sprayer | Eicher | 2 | |
| 20 | Paver | | 3 | |
| 21 | Tractor | 5036 D V-2 | 6 | |
| 22 | Mobile Service Van | | 1 | |
| 23 | Tower Light | AJASKY | 9 | |
| 24 | Hydra Crane | | 3 | |
| 25 | Asphalt Batch Mix Plant | | 1 | |
| 26 | Wet Mix Plant | 250 TPH | 1 | |
| 27 | Concrete Batch Mix Plant | 45 cum | 1 | |
| 28 | Crusher Plant (3 Stage) | 250 TPH | 2 | |
| 29 | Weigh Bridge for Camp 100MT | 100MT | 2 | |
| 30 | Weigh Bridge for Crusher 100MT | 100MT | 2 | |
| 31 | Genset Base Camp | 25KV | 2 | |
| 32 | Genset 63KVA Boiler | 63KVA Boiler | 1 | |

| | | | | |
|----|------------------------------------|----------|---|--|
| 33 | Genset (H.M & B/P) | 82.50KV | 3 | |
| 34 | Genset (B/P-CP-45) | 125KV | 4 | |
| 35 | Genset Concrete Plant-180 KVA | 180 KVA | 3 | |
| 36 | Genset (Crusher) | 1010KVA | 1 | |
| 37 | Genset 63KVA | 62.5 KVA | 2 | |
| 38 | Genset 650KV | 650KV | 1 | |
| 39 | Genset 15KV | 15KV | 2 | |
| 40 | Genset 80KV | 80KV | 2 | |
| 41 | Genset 40KV | 40KV | 4 | |
| 42 | Genset 82.5KV | 82.50KV | 3 | |
| 43 | Gantry at Box Segment Casting Yard | 100 MT | 2 | |
| 44 | Launching Girder | | 2 | |

14. Change of Scope Proposals**Table 14.1 - Status of Change of Scope Proposals**

| Sl. No | Proposal Details | Date of Proposal | Current Status | COS Amount | Actual Date of Approval |
|--------|---|------------------|--|--------------|-------------------------|
| 1 | Replacement of Pipe Culverts with Box Culverts | 23.03.2018 | Approved | 3.21 Cr | 21.02.2020 |
| 2 | Strengthening/upgrade the incident Management Service | 10.05.2019 | Required COS notice for Strengthening/upgrade the incident Management Service. | NA | NA |
| 3 | Comprehensive –COS 02 | 20.08.2018 | Approved | (-) 4.69 Cr. | 23.06.2021 |
| 4 | Additional work required to be executed as per demand of local public | 17.03.2023 | Principle approval obtained from the authority. | 18.43 Cr. | |

15. Details of Correspondences

The following tables list out the correspondences held between the parties in the particular month:-

Table 15.1. - Concessionaire to NHAI

Table 15.2. - NHAI to Concessionaire

Table 15.3. - Concessionaire to Independent Engineer

Table 15.4. - Independent Engineer to Concessionaire

Four laning of Sethiyahopu to Cholapuram from Km 65.960 to 116.440 section of NH-45C in the state of Tamilnadu under NHDP-IV on Hybrid Annuity Mode.

TABLE 14.1 - CORRESPONDANCE - CONCESSIONAIRE TO NHAI

| Sr. No. | Date | Letter No | Subject | Remarks |
|---------|------------|-----------------------------|--|---------|
| 1 | 07-08-2023 | PSCHPL-HO-SCP-NHAI-032-2023 | Request for release of differential GST on Interest 3rd Annuity | |
| 2 | 07-08-2023 | PSCHPL/SCP/NHAI/2023/1657 | GST impact calculation due to revision in GST Change in law | |
| 3 | 09-08-2023 | PSCHPL/SCP/NHAI/2023/1662 | Shifting of infringement of veeranam-Req for temporary shutdown for commissioning of pipelines | |
| 4 | 10-08-2023 | PSCHPL/SCP/NHAI/2023/1663 | Work hampered due to public protest at Km. 98+950 A1 side RE wall & Public demand of PUP | |
| 5 | 11-08-2023 | PSCHPL/SCP/NHAI/2023/1667 | Submission of RA Bill-07 for Recording of Drone video-reg | |
| 6 | 11-08-2023 | PSCHPL/SCP/NHAI/2023/1660 | Recording of Drone video for the month of July-2023 | |
| 7 | 19-08-2023 | PSCHPL/SCP/NHAI/2023/1681 | Submission of Extension Bank Guarantee Bond to Mobilization Advance 2nd Installment | |
| 8 | 24-08-2023 | PSCHPL-HO-SCP-PIU-034-2023 | Reimbursement of 50% cost & Expenditure of IE payment for the month of May & June 23 | |
| 9 | 29-08-2023 | PSCHPL/SCP/NHAI/2023/1689 | Issuance of NOC for proposed MS-HSD retail outlet at Km. 94+150 to Km. 94+190 | |
| 10 | 29-08-2023 | PSCHPL/SCP/NHAI/2023/1690 | Shifting of HT lines & towers at Km. 73.470-Insufficient vertical clearance-reply-reg | |
| 11 | 30-08-2023 | PSCHPL/SCP/NHAI/2023/1693 | Submission of Escrow account bank statement | |

| Four laning of Sethiyahopu to Cholapuram from Km 65.960 to 116.440 section of NH-45C in the state of Tamilnadu under NHDP-IV on Hybrid Annuity Mode. | | | | |
|--|------------|--|---|---------|
| TABLE 14.2 - CORRESPONDANCE - NHAI TO CONCESSIONAIRE | | | | |
| Sr. No. | Date | Letter No | Subject | Remarks |
| 1 | 01-08-2023 | NHAI/PIU/Thanjavur/11025/33/2020/2189 | Request to provide minor bridge-remarks called for | |
| 2 | 04-08-2023 | NHAI/PIU/Thanj/11020/54/2020/2226 | Request for extension of provisional NOC-reg | |
| 3 | 08-08-2023 | NHAI/PIU/Thanj/11021/112/CWSS -252/2023/2248 | Request for permssion to underground pipeline -Approval requested | |
| 4 | 09-08-2023 | NHAI/PIU/Thanj/11025/03/2018/2268 | Request to provide protection to take up the project work | |
| 5 | 09-08-2023 | NHAI/PIU/Thanj/11025/28/2019/2266 | Comprehensive COS proposal-inprinciple approval fromNHAI-communicated | |
| 6 | 10-08-2023 | NHAI/PIU/Thanj/11025/11/2018/2278 | 3rd installment O&M payment intimation | |
| 7 | 10-08-2023 | NHAI/PIU/Thanj/11025/11/2018/2279 | IPC-02 of PMS-05 payment intimation | |
| 8 | 10-08-2023 | NHAI/PIU/Thanj/11025/17/2018/2282 | No availability certificate from NLCIL-intimation-reg | |
| 9 | 14-08-2023 | NHAI/PIU/Thanjavur/11025/09/2018/2324 | Estimate for restoration works-Remarks reg | |
| 10 | 16-08-2023 | NHAI/PIU/Thanj/11019/52/2017/2333 | IE 50% claim for May 23 and June 23 | |
| 11 | 17-08-2023 | NHAI/PIU/Thanj/11025/08/2018/2349 | Confirmation of Extended BG | |
| 12 | 17-08-2023 | NHAI/PIU/Thanj/11025/09/2018/2337 | CMWSSB-Req for temporary shutdown for commissioning | |
| 13 | 24-08-2023 | NHAI/PIU/Thanj/11025/03/2018/2414 | Request to provide crossing facilities along river bank | |
| 14 | 25-08-2023 | NHAI/PIU/Thanj/11021/117/NH -45C/2009/2439 | Request to lay OFC-Remarks called for | |
| 15 | 25-08-2023 | NHAI/PIU/Thanj/11025/11/2018/2521 | IPC-02 of PMS-05 payment intimation | |
| 16 | 26-08-2023 | NHAI/PIU/Thanj/11021/112/CWSS -252/2023/2438 | Remittance of license fee requested | |
| 17 | 26-08-2023 | NHAI/PIU/Thanj/11021/117/2022/NH -45C/2437 | Remittance of license fee-Requested | |
| 18 | 26-08-2023 | NHAI/PIU/Thanj/11025/03/2018/2442 | Drainage facilities in thazhuthazai medu | |
| 19 | 28-08-2023 | NHAI/11011/1/2023/RO Madurai/1579 | Review meeting | |
| 20 | 28-08-2023 | NHAI/PIU/Thanj/11025/45/2018/2463 | Police protection for taking up construction work of LVUP at Km. 77.420 | |
| 21 | 29-08-2023 | NHAI/PIU/Thanj/11021/112/CWSS -980/2023/2474 | TWAD board nagapattinam-Remarks called for | |
| 22 | 30-08-2023 | CMWSSB/O&M-II/WT&T/VM/NHAI-Spl/2020 | Request for temporary shutdown | |

| Four laning of Sethiyahopu to Cholapuram from Km 65.960 to 116.440 section of NH-45C in the state of Tamilnadu under NHDP-IV on Hybrid Annuity Mode. | | | | |
|--|------------|-------------------------|--|---------|
| TABLE 14.3 - CORRESPONDANCE - CONCESSIONAIRE TO INDEPENDENT ENGINEER | | | | |
| Sr. No. | Date | Letter No | Subject | Remarks |
| 1 | 03-08-2023 | PSCHPL/SCP/IE/2023/1650 | Submission of Revised D&D of RE wall of VUP at 72+545 | |
| 2 | 05-08-2023 | PSCHPL/SCP/IE/2023/1653 | Submission of MPR for the month of July 2023 | |
| 3 | 07-08-2023 | PSCHPL/SCP/IE/2023/1656 | Submission of MSR for July 2023 | |
| 4 | 09-08-2023 | PSCHPL/SCP/IE/2023/1666 | Soil test report for the proposed borrow area (BA No-48)-reg | |
| 5 | 09-08-2023 | PSCHPL/SCP/IE/2023/1661 | Submission of IPC-03 of PMS-05 | |
| 6 | 14-08-2023 | PSCHPL/SCP/IE/2023/1672 | Construction of Toll plaza-Submission of D&D of toll plaza proposed at Km. 116+220 | |
| 7 | 21-08-2023 | PSCHPL/SCP/IE/2023/1683 | Compliance report for-IE comments on July 2023 MPR | |
| 8 | 26-08-2023 | PSCHPL/SCP/IE/2023/1685 | Soil test report for BA-07 Ex-09 | |

Four laning of Sethiyahopu to Cholapuram from Km 65.960 to 116.440 section of NH-45C in the state of Tamilnadu under NHDP-IV on Hybrid Annuity Mode.

TABLE 14.4 - CORRESPONDANCE - INDEPENDENT ENGINEER TO CONCESSIONAIRE / NHAI

| Sr. No. | Date | Letter No | Subject | Remarks |
|---------|------------|--------------------------|---|---------|
| 1 | 02-08-2023 | TES/IE/SCP/NHAI/2023/636 | Panchayat President Pudaiyur representation Report on the request to provide Under pass and widening of road - reg. | |
| 2 | 02-08-2023 | TES/IE/SCP/NHAI/2023/637 | Drainage System Adequacy of drain work in the ongoing project and finalization of drainage plan for the balance length – Concurrence furnished - reg. | |
| 3 | 03-08-2023 | TES/IE/SCP/NHAI/2023/638 | Shifting of HT line and towers at Km. 73+470 in SE (O), Villupuram section - IE comments | |
| 4 | 03-08-2023 | TES/IE/SCP/NHAI/2023/639 | Request for permission to lay underground OFC on (Vikkravandi – Thanjavur section) NH -45C | |
| 5 | 03-08-2023 | TES/IE/SCP/NHAI/2023/641 | UTM Petition-IE comments | |
| 6 | 09-08-2023 | TES/IE/SCP/NHAI/2023/644 | Villagers of Sundipallam requesting to provide subway IE comments - reg. | |
| 7 | 09-08-2023 | TES/IE/SCP/NHAI/2023/645 | Public demand for Minor bridge at Veeramudayanatham Village – IE Report -reg. | |
| 8 | 09-08-2023 | TES/IE/SCP/NHAI/2023/646 | IE Monthly Progress Report (MPR) for the month of July 2023-Reg. | |
| 9 | 09-08-2023 | TES/IE/SCP/NHAI/2023/647 | Request for permission to lay underground OFC on NH -45C-IE remarks | |
| 10 | 10-08-2023 | TES/IE/SCP/NHAI/2023/649 | (NOC) for the proposed MSHSD Retail outlet of Kundaveli east | |
| 11 | 10-08-2023 | TES/IE/SCP/NHAI/2023/650 | Request to provide crossing facilities along the river bank-IE comments-reg | |
| 12 | 11-08-2023 | TES/IE/SCP/NHAI/2023/653 | Public demand for Minor bridge at Veeramudayanatham Village Representation– IE comments | |
| 13 | 12-08-2023 | TES/IE/SCP/NHAI/2023/654 | Villagers of sundipallam requesting to provide subway-IE comments-reg | |
| 14 | 17-08-2023 | TES/IE/SCP/PIL/2023/941 | Submission of Revised P&P from Km 65+960 to Km 67+000 Matching of FRL incorporating COS structure – reg. | |
| 15 | 17-08-2023 | TES/IE/SCP/PIL/2023/942 | IE Review and Comments on concessionaire MPR for the month of July 2023 – Reg. | |
| 16 | 17-08-2023 | TES/IE/SCP/PIL/2023/943 | Minutes of Meeting dated 11.08.2023 - Reg | |
| 17 | 17-08-2023 | TES/IE/SCP/PIL/2023/944 | Monthly Site Inspection-reg. | |
| 18 | 17-08-2023 | TES/IE/SCP/NHAI/2023/656 | Submission of IPC-03 of PMS-05- Recommendation for payment - Reg | |
| 19 | 18-08-2023 | TES/IE/SC/PIL/2023/946 | Status report on the provisional completion-3 stretches | |
| 20 | 24-08-2023 | TES/IE/SCP/NHAI/2023/659 | IE O&M monthly status report for the monh of July 2023 | |
| 21 | 24-08-2023 | TES/IE/SCP/NHAI/2023/660 | IE inspection report for the month of July 2023 | |
| 22 | 24-08-2023 | TES/IE/SCP/NHAI/2023/661 | Construction of Toll plaza – Design & drawings - IE comments - reg. | |
| 23 | 24-08-2023 | TES/IE/SCP/PIL/2023/949 | Soil test report for the proposed BA No-48 | |
| 24 | 31-08-2023 | TES/IE/SC/PIL/2023/951 | Site Inspection Report-reg. | |



16. Progress Photographs

| Sl. No | Description | Location | Side | Remarks |
|--|---|---|------|---------------|
| 1. | RE Wall Embankment layer work in progress | 102+950 | BHS | Existing Road |
| 2. | Subgrade layer work in progress | 108+400 | BHS | Bypass |
|  | |  | | |
| Sl. No | Description | Location | Side | Remarks |
| 3. | CTSB Layer work in progress | 80+940 | LSR | Existing Road |
|  | | | | |

| Sl. No | Description | Location | Side | Remarks |
|--------|----------------------------|----------|------|---------------|
| 4. | WMM Layer work in progress | 95+540 | RSR | Existing Road |
| 5. | WMM Layer work in progress | 103+250 | RHS | Existing Road |



| Sl. No | Description | Location | Side | Remarks |
|--------|----------------------------|----------|------|---------------|
| 6. | DBM Layer work in progress | 103+000 | RHS | Existing Road |
| 7. | BC Layer work in progress | 103+000 | RHS | Existing Road |

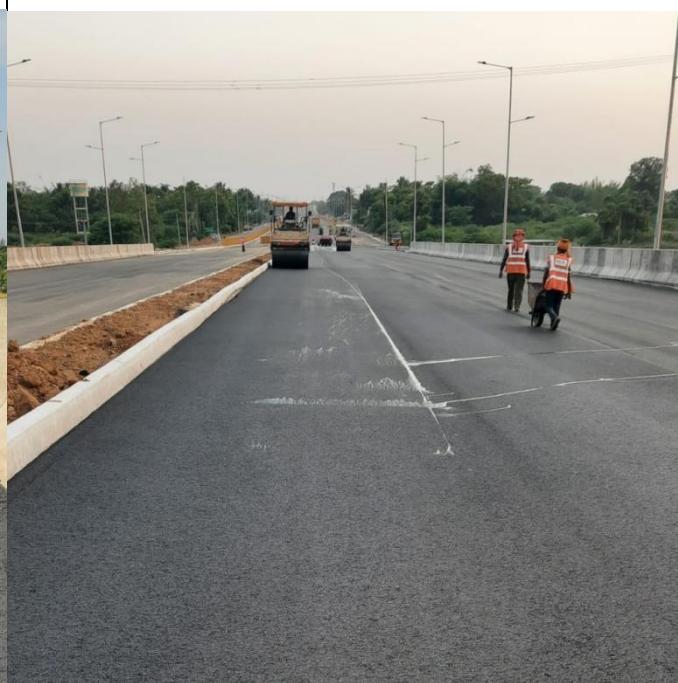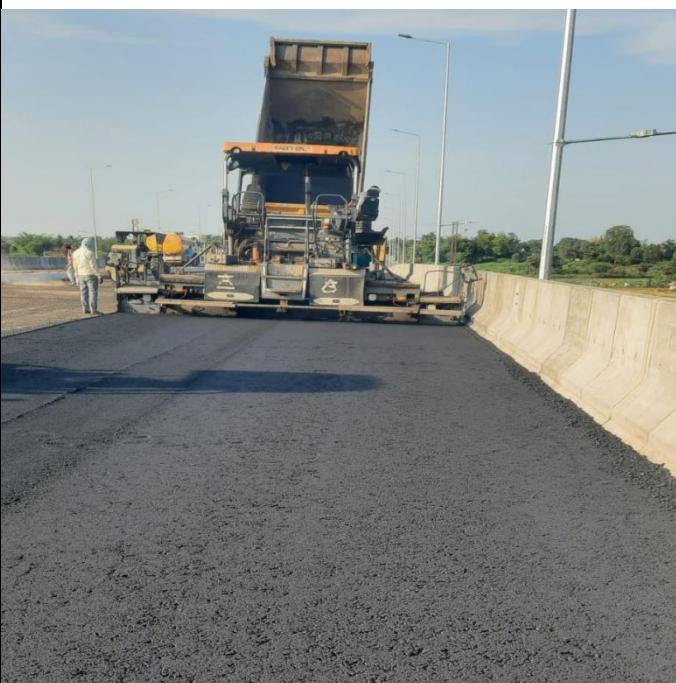

| Sl. No | Description | Location | Side | Remarks |
|--------|---|----------|------|--------------|
| 8. | Crash Barrier concrete work in progress | 73+317 | RHS | Major Bridge |
| 9. | Foundation work in progress | 80+556 | RHS | GSI |



| Sl. No | Description | Location | Side | Remarks |
|--------|---|----------|------|--------------|
| 10. | Box Segment Launching work in progress between Span P15–P14 | 107+400 | RHS | Major Bridge |

